

Arlington High School Building Committee

Meeting Date: Thursday, December 3, 2020 - 10:00 am
Location: Conducted via Remote Participation

Agenda

1. Skanska
 - ◆ Update on HVAC Firm Selection
 - ◆ GMP Review/Approval - VOTE
2. Subcommittee Reports
 - ◆ Communications
 - ◆ Finance
 - ◆ Interiors
 - ◆ Landscape & Exteriors
 - ◆ Memorials
 - ◆ SMEPPF
 - ◆ Security
 - ◆ Temp Use-Phasing
3. Meeting Schedule
4. New Business

The listings of matters are those reasonably anticipated by the Chair which may be discussed at the meeting. Not all items listed may in fact be discussed and other items not listed may also be brought up for discussion to the extent permitted by law.

Members of the public are asked to send written comment to ktassone@arlington.k12.ma.us. Documents regarding agenda items will be made available via the Town's website.

<https://www.mass.gov/doc/open-meeting-law-order-march-12-2020/download>

Topic: Arlington High School Building Committee
Time: Dec 3, 2020 10:00 AM Eastern Time (US and Canada)

Join Zoom Meeting
<https://town-arlington-ma-us.zoom.us/j/94815419621>

Meeting ID: 948 1541 9621
One tap mobile
+13126266799,,94815419621# US (Chicago)
+16468769923,,94815419621# US (New York)
Dial by your location
+1 312 626 6799 US (Chicago)

+1 646 876 9923 US (New York)
+1 301 715 8592 US (Washington D.C.)
+1 669 900 6833 US (San Jose)
+1 253 215 8782 US (Tacoma)
+1 346 248 7799 US (Houston)
+1 408 638 0968 US (San Jose)

Meeting ID: 948 1541 9621

Find your local number: <https://town-arlington-ma-us.zoom.us/j/ad3Blijk1X>

AHSBC MEETING 12/3/20 DRAFT VOTE LANAGUE

Motion to approve the Consigli Guaranteed Maximum Price total construction cost of \$234,287,347.00 (with Alternates), per the Draft GMP Package dated November 24, 2020.

AHS GMP COMPARISON SUMMARY - AHSBC 12/3/20

CONSTRUCTION COST COMPARISON

| | | |
|---|--|----------------------|
| 1 | MSBA 3011 - Total Construction Budget (w/o Alternates) | \$235,286,827 |
| 2 | GMP Construction Budget (w/o Alternates) | \$232,853,680 |
| | <i>DELTA (Line 1 Less Line 2)</i> | <i>\$2,433,147</i> |
| 3 | GMP Construction Budget (with Alternates) | \$234,287,347 |
| | <i>DELTA (Line 1 Less Line 3)</i> | <i>\$999,480</i> |



CONSIGLI

Est. 1905

DRAFT GMP PACKAGE

Town Of Arlington
Arlinton High School

SUBMITTED BY:
Consigli Construction Co., Inc.
72 Sumner Street
Milford, MA 01757

November 24, 2020

TABLE OF CONTENTS

Arlington High School



The Right Choice

Consigli Construction Co., Inc. is a fourth-generation family-led organization that can offer the resources and experience of one of the strongest construction management firms in the Northeast with the creativity and flexibility of a start-up.

1. Trade Summary
2. Alternates
3. Allowances
4. Assumptions & Qualifications
5. Change Order Log
6. Document List
7. Schedule
8. Logistics

1. TRADE SUMMARY

Arlington High School

GMP

Draft 11/24/20



| | | GMP | | | | | August 27, 2020 (90% CD) | | | |
|--------|---|------------|------------|-------|---------------|-----------------------|-----------------------------|-------------|------------|-----------|
| | | Base Bid | Alternates | \$/sf | Change Orders | Sub | w/ escalation & design cont | Delta | Alternates | Delta |
| 03.01 | CONCRETE - Ph2,3 and Site | 10,991,900 | 290,000 | 2 | 26.91 | Riggs | 11,031,325 | (39,425) | 400,000 | (110,000) |
| 03.02 | POLISHED CONCRETE | 326,854 | | | 0.80 | Business Interiors | 301,266 | 25,588 | | |
| 04.01 | MASONRY (TS) | 6,668,000 | | | 16.32 | Empire | 7,250,596 | (582,596) | | |
| 05.01 | STRUCTURAL STEEL - Ph 2 & 3 | 10,318,500 | | | 25.26 | Trimax | 9,920,656 | 397,844 | | |
| 05.02 | MISCELLANEOUS AND ORNAMENTAL (TS) | 1,525,000 | | | 3.73 | Avid (WBE) | 2,171,370 | (646,370) | | |
| | Allowance for Misc Metals | 200,000 | | | 0.49 | Allowance | | | | |
| 06.02 | FINISH CARPENTRY | 3,553,853 | | | 8.70 | NE Finish Systems | 3,322,348 | 231,505 | | |
| 06.03 | HISTORIC SALVAGE (except Stone Façade) | - | | | - | with Millwork | 154,800 | (154,800) | | |
| 07.01 | WATERPROOFING, DAMPPROOFING & CAULKING (TS) | 1,542,000 | | | 3.77 | PJ Spillane (WBE) | 2,007,538 | (465,538) | | |
| 07.02 | ROOFING & FLASHING (TS) | 3,483,000 | | | 8.53 | Greenwood | 3,121,929 | 361,071 | | |
| 07.03a | SUB SLAB VAPOR MEMBRANE | 766,000 | | | 1.88 | Budget Maint. | 778,320 | (12,320) | | |
| 07.03b | ENGINEERED BARRIER | 161,250 | | | 0.39 | Budget Maint. | 161,250 | - | | |
| 07.04 | EXTERIOR WALL PANELS | 1,827,800 | | | 4.47 | Riggs | 1,335,273 | 492,527 | | |
| 07.09 | SPRAY FIREPROOFING | 1,300,000 | | | 3.18 | Select Spray | 1,023,323 | 276,677 | | |
| 08.01 | WINDOWS & CURTAIN-WALL (TS?) | 5,670,175 | | | 13.88 | R & R (580K WBE) | 7,002,013 | (1,331,838) | | |
| 08.02 | GLASS & GLAZING (TS) | 718,000 | | | 1.76 | Kapiloff | 832,996 | (114,996) | | |
| 08.04 | DOORS AND HARDWARE | 1,680,770 | | | 4.11 | Horner/Riggs | 1,649,456 | 31,314 | | |
| 08.05 | ACCESS DOORS | 26,875 | | | 0.07 | Hold | 26,875 | - | | |
| 08.06 | MODULAR SKYLIGHTS | 144,000 | | | 0.35 | pending | 98,488 | 45,512 | | |
| 08.07 | OVERHEAD DOORS & LOADING DOCK EQUIPMENT | 182,300 | | | 0.45 | Barron | 159,661 | 22,639 | | |
| 08.09 | FOLDING GLASS DOOR | 107,000 | | | 0.26 | CRF | 89,870 | 17,130 | | |
| 09.01 | DRYWALL & CARPENTRY | 17,681,616 | 60,000 | 3 | 43.28 | Colony | 16,439,855 | 1,241,761 | 250,110 | |
| 09.02 | TILE (TS) | 1,341,480 | | | 3.28 | Capital Carpet | 1,539,697 | (198,217) | | |
| 09.03 | ACOUSTICAL TILE (TS) | 2,358,000 | | | 5.77 | K & K | 3,166,051 | (808,051) | | |
| 09.04 | RESILIENT FLOORS (TS) | 1,629,939 | | | 3.99 | Capital Carpet | 2,018,329 | (388,390) | | |
| 09.05 | PRECAST TERRAZZO | 665,510 | | | 1.63 | Roman Mosaic | 673,122 | (7,612) | | |
| 09.06 | PAINTING (TS) | 971,000 | | | 2.38 | New Generation | 1,052,275 | (81,275) | | |
| 09.07 | ATHLETIC FLOORING | 156,500 | | | 0.38 | Keifer | 154,328 | 2,172 | | |
| 09.09 | ACOUSTICAL INSULATION | 457,268 | | | 1.12 | ATI | 316,850 | 140,418 | | |
| 09.10 | WOOD FLOORING | 497,000 | | | 1.22 | FJ Roberts | 436,970 | 60,030 | | |
| 09.11 | RESINOUS FLOORING | 250,513 | | | 0.61 | Boston Flooring | 197,717 | 52,796 | | |
| 09.12 | CARPET AND ENTRANCE MATS | 383,075 | | | 0.94 | Allegheny | 348,652 | 34,423 | | |
| 09.13 | ACOUSTICAL WALLS TREATMENT | 440,800 | | | 1.08 | Northeast Interior | 700,171 | (259,371) | | |
| 09.15 | TEMPORARY CONSTRUCTION | 1,500,000 | | | 3.67 | Multiple Vendors | 2,184,303 | (684,303) | | |
| 09.20 | TRADE SUPPORT | 1,867,140 | | | 4.57 | Multiple Vendors | 2,362,754 | (495,614) | | |
| 09.25 | PEDESTRIAN PROTECTION | 440,750 | | | 1.08 | Riggs | 440,750 | - | | |
| 10.02 | SIGNAGE | 302,609 | | | 0.74 | Bluebird (WMBE) | 439,219 | (136,610) | | |
| 10.03 | SPECIALTIES | 1,322,805 | | | 3.24 | Granite State | 1,224,466 | 98,339 | | |
| 10.05 | PHOTOLUMINESCENT SAFETY PRODUCTS | 46,545 | | | 0.11 | Design Communications | 67,080 | (20,535) | | |
| 10.06 | FOLDING PANEL PARTITIONS | 73,000 | | | 0.18 | Corbin Hufcore | 52,245 | 20,755 | | |
| 11.02 | FOOD SERVICE EQUIPMENT | 669,012 | | | 1.64 | Kittridge (WBE) | 807,162 | (138,150) | | |

Arlington High School

GMP

Draft 11/24/20



| | | GMP | | | | | August 27, 2020 (90% CD) | | | |
|-------|---|------------|------------|-------|---------------|----------------------|-----------------------------|-------------|------------|-------|
| | | Base Bid | Alternates | \$/sf | Change Orders | Sub | w/ escalation & design cont | Delta | Alternates | Delta |
| 11.04 | STAGE CURTAIN & RIGGING | 782,353 | | 1.92 | | Jason Industries | 826,818 | (44,465) | | |
| 11.05 | GYMNASIUM EQUIPMENT & STANDS | 731,884 | | 1.79 | | Robert H Lord | 782,179 | (50,295) | | |
| 11.06 | APPLIANCES | 223,058 | | 0.55 | | GW Toma | 173,828 | 49,231 | | |
| 11.07 | WINDOW WASHING EQUIPMENT | 83,700 | | 0.20 | | Peak Fall Prot | 85,693 | (1,993) | | |
| 11.08 | CLOCK | 43,295 | | 0.11 | | Electric Time | 53,750 | (10,455) | | |
| 12.02 | WINDOW TREATMENT | 225,000 | | 0.55 | | Walker | 434,698 | (209,698) | | |
| 12.03 | FIXED AUDIENCE SEATING | 296,222 | | 0.73 | | Robert Lord | 366,222 | (70,000) | | |
| 12.30 | MANUFACTURED CASEWORK | 1,983,800 | | 4.86 | | Northeast Interior | 1,808,932 | 174,868 | | |
| 21.01 | FIRE PROTECTION (TS) | 2,562,300 | | 6.27 | | Delta Mech | 2,843,179 | (280,879) | | |
| 22.01 | PLUMBING (TS) | 5,640,000 | | 13.81 | | E. Amanti | 5,589,228 | 50,772 | | |
| 23.01 | HVAC (TS) | 30,173,000 | | 73.86 | | PJ Kennedy | 30,594,618 | (421,618) | | |
| 26.01 | ELECTRICAL (TS) | 18,200,000 | 558,000 | 1 | 44.55 | Wayne J Griffin | 22,588,533 | (4,388,533) | 1,110,000 | |
| | Allowance for Electrical | 750,000 | | 1.84 | | Allowance | | | | |
| 23.02 | VAPOR MITIGATION FAN ALLOWANCE | 175,000 | | 0.43 | | Allowance | - | 175,000 | | |
| 31.21 | TEMP FENCING | 244,568 | | 0.60 | | Riggs | 244,568 | 0 | | |
| 31.23 | SITWORK - Phase 2-4 | 12,140,000 | 328,000 | 2,4 | 29.72 | J. Derenzo | 11,544,400 | 595,600 | 431,799 | |
| 31.25 | PILES | 2,166,800 | | 5.30 | | NEFCo (WBE) | 2,193,897 | (27,097) | | |
| 32.04 | LANDSCAPING AND SITE FURNISHINGS | 3,485,126 | | 8.53 | | Greenscape | 2,842,613 | 642,513 | | |
| 32.07 | SYNTHETIC FIELD SPORT SURFACING | 1,551,300 | | 3.80 | | Global | 1,673,531 | (122,231) | | |
| 32.08 | FENCING | 964,930 | 102,500 | 2 | 2.36 | Union Fence | 593,211 | 371,719 | 120,525 | |
| 21-02 | EBP #2 FIRE PROTECTION | 125,000 | | 0.31 | | Rustic | 125,000 | - | | |
| 22-02 | EBP #2 PLUMBING | 118,900 | | 0.29 | | PJ Kennedy | 118,900 | - | | |
| 26-02 | EBP #2 ELECTRIC | 187,200 | | 0.46 | 39,833 | WJ Griffin | 187,200 | - | | |
| 31.21 | EBP #2 TEMP FENCE - Ph 1 | 184,330 | | 0.45 | - | Riggs | 184,330 | - | | |
| 31.22 | EBP #2 SITWORK - Ph 1 | 8,195,000 | | 20.06 | 148,548 | Derenzo | 8,195,000 | - | | |
| 99.01 | EBP #3 SWING SPACE - General Rqrmts | 125,000 | | 0.31 | | Riggs | 125,000 | - | | |
| 99.02 | EBP #3 SWING SPACE - Demo & Abatement | 52,500 | | 0.13 | 37,616 | Costello | 52,500 | - | | |
| 99.03 | EBP #3 2020 SWING SPACE - Concrete | 17,100 | | 0.04 | (4,326) | Riggs | 17,100 | - | | |
| 99.04 | EBP #3 2020 SWING SPACE - Finish Carpentry | 12,760 | | 0.03 | 4,747 | Padco | 12,760 | - | | |
| 99.05 | EBP #3 2020 SWING SPACE - D/F/H | 34,260 | | 0.08 | - | Horner/Riggs | 34,260 | - | | |
| 99.06 | EBP #3 2020 SWING SPACE - Glazing | 9,000 | | 0.02 | - | A & A Windows | 9,000 | - | | |
| 99.07 | EBP #3 2020 SWING SPACE - Drywall | 79,100 | | 0.19 | - | TJ McCartney | 79,100 | - | | |
| 99.08 | EBP #3 2020 SWING SPACE - Flooring | 33,990 | | 0.08 | - | Ayotte & King | 33,990 | - | | |
| 99.09 | EBP #3 2020 SWING SPACE - Acoustical Ceilings | 2,700 | | 0.01 | - | Cheviot | 2,700 | - | | |
| 99.10 | EBP #3 2020 SWING SPACE - Painting | 37,800 | | 0.09 | - | Color Concepts | 37,800 | - | | |
| 99.11 | EBP #3 2020 SWING SPACE - Specialties | 29,308 | | 0.07 | 624 | Automation Solutions | 29,308 | - | | |
| 99.12 | EBP #3 2020 SWING SPACE - Plumbing | 48,880 | | 0.12 | 5,490 | Robert Irvine | 48,880 | - | | |
| 99.13 | EBP #3 2020 SWING SPACE - HVAC | 167,000 | | 0.41 | 953 | CAM HVAC | 167,000 | - | | |
| 99.14 | EBP #3 2020 SWING SPACE - Electric | 194,890 | | 0.48 | 272 | WJ Griffin | 194,890 | - | | |
| 02.01 | EBP #4 DEMOLITION & ABATEMENT (also w/ EBP#3) | 6,891,075 | | 16.87 | | Costello | 6,891,075 | - | | |
| 03.01 | EBP #4 CONCRETE Ph 1 | 3,830,000 | | 9.38 | 72,500 | Riggs | 3,830,000 | - | | |

Arlington High School

GMP

Draft 11/24/20



| | | GMP | | | | | August 27, 2020 (90% CD) | | | |
|-----------|--|--------------------|------------------|---------------|---------------|----------|-----------------------------|-----------------------|---------------------|-----------------------|
| | | Base Bid | Alternates | \$/sf | Change Orders | Sub | w/ escalation & design cont | Delta | Alternates | Delta |
| 05.01 | EBP #4 STEEL Ph 1 | 7,260,500 | | 17.77 | 460,654 | Tri-Max | 7,260,500 | - | | |
| 14.01 | EBP #5 ELEVATOR (TS) | 690,000 | | 1.69 | | Beckwith | 688,000 | 2,000 | | |
| | Changes realized in EBP 2-4 | 766,911 | | 1.88 | 766,911 | | | 766,911 | | |
| | Changes to Parmeter | 217,534 | | 0.53 | | | | 217,534 | | |
| | | 195,980,913 | 1,338,500 | 479.76 | | | \$ 200,662,036 | \$ (4,681,123) | 2,312,434 | \$ (973,934) |
| | SDI | 1,339,931 | 5,886 | 3.28 | | | \$ 1,212,275 | \$ 127,656 | \$ 16,377 | \$ (10,491) |
| | | 197,320,844 | 1,344,386 | 483.04 | | | \$ 201,874,311 | \$ (4,553,467) | \$ 2,328,811 | \$ (984,425) |
| | Temp IT/DPW Project IT Coordination | 300,000 | | 0.73 | | | \$ - | \$ 300,000 | | |
| | Phasing | 650,000 | | 1.59 | | | \$ 650,000 | \$ - | | |
| | Escalation | - | | - | | | \$ - | \$ - | \$ 160,146 | \$ (160,146) |
| | Acceleration and Overtime Allowance | 700,000 | | 1.71 | | | | | | |
| | GCs | 11,931,225 | | 29.21 | | | \$ 11,931,225 | \$ - | | |
| | GRs | 4,872,887 | | 11.93 | | | \$ 4,872,887 | \$ - | | |
| | Covid | 600,000 | | | | | \$ 600,000 | \$ - | | |
| | Bonds | 2,251,695 | 10,755 | 5.51 | | | \$ 2,251,695 | \$ - | \$ - | \$ 10,755 |
| | Builder's Risk | - | | - | | | \$ - | \$ - | | |
| | GL Insurance | 2,588,155 | 16,133 | 6.34 | | | \$ 2,588,155 | \$ - | \$ - | \$ 16,133 |
| | GMP Contingency | 6,933,137 | 34,282 | 16.97 | | | \$ 5,783,137 | \$ 1,150,000 | \$ 62,224 | \$ (27,942) |
| | Fee | 4,705,737 | 28,111 | 11.52 | | | \$ 4,705,737 | \$ - | \$ - | \$ 28,111 |
| | Total without Alternates | 232,853,680 | 1,433,667 | 570.02 | | | \$ 235,257,147 | \$ (2,403,467) | 2,551,181 | \$ (1,117,514) |
| | Total with Alternates | 234,287,347 | | 573.53 | | | | \$ (969,800) | | |
| 0603-0000 | Parmenter School (Amendment #1) | 2,581,810 | | | | | | | | |



CONSIGLI
Est. 1905

2. ALTERNATES

Arlington High School**GMP - Draft****Alternates**

11/24/2020



| | Value | Carried With |
|--|-------------------|--------------|
| #1 Stadium Lighting | | |
| Stadium lights | \$ 558,000 | WJ Griffin |
| Drilled shafts and precast bases | w/base bid site | J. Derenzo |
| Bond, insurance, CM Contingency (5.4%) | \$ 30,132 | |
| Fee (2.0%) | \$ 11,763 | |
| Total: | \$ 599,895 | |
| #2 Traffic Signal | | |
| Traffic signal and associated sitework | \$ 178,000 | J. Derenzo |
| SDI (1.2%) | \$ 2,136 | |
| Bond, insurance, CM Contingency (5.4%) | \$ 9,727 | |
| Fee (2.0%) | \$ 3,797 | |
| Total: | \$ 193,661 | |
| #3 Minuteman Bike Path | | |
| Concrete | \$ 225,000 | Riggs |
| Sitework and paving | \$ 150,000 | J. Derenzo |
| Fencing and sports netting | \$ 102,500 | Union Fence |
| Subtotal: | \$ 477,500 | |
| SDI (1.2%) | \$ 5,730 | |
| Bond, insurance, CM Contingency (5.4%) | \$ 26,094 | |
| Fee (2.0%) | \$ 10,186 | |
| Total: | \$ 519,511 | |
| #4 Additional Insulation | | |
| Mineral wool insulation per drawings | \$ 60,000 | Colony |
| SDI (1.2%) | \$ 720 | |
| Bond, insurance, CM Contingency (5.4%) | \$ 3,279 | |
| Fee (2.0%) | \$ 1,280 | |
| Total: | \$ 65,279 | |

3. ALLOWANCES

Arlington High School**GMP - Draft****Allowances**

11/24/2020



| | Value | Carried With |
|---|---------------------|----------------------------|
| Cost Allowance | | |
| Temp electric consumption in GR | \$ 200,000 | General Rqrmts |
| Temp electric consumption - additional | \$ 250,000 | Trade Support |
| Temporary heating systems and rentals | \$ 125,000 | General Rqrmts |
| Temp heating fuel for construction | \$ 125,000 | General Rqrmts |
| Project identification signage | \$ 15,000 | General Rqrmts |
| Police detail | \$ 22,500 | General Rqrmts |
| Humidity control | \$ 200,000 | General Rqrmts |
| Winter conditions (shoveling, salting not purchased with trade, road plowing bought with site work) | \$ 150,000 | General Rqrmts |
| Hoisting not assigned to sub | \$ 300,000 | Trade Support |
| Temp heating fuel for construction | \$ 165,000 | Trade Support |
| Temporary construction for safe egress | \$ - | phasing contingency |
| Modifications to existing construction to allow for separation | \$ - | phasing contingency |
| Allowance for additional concrete | \$ 100,000 | concrete |
| Allowance for additional steel | \$ 300,000 | structural steel |
| Allowance for additional misc metals | \$ 200,000 | line item on trade summary |
| Pedestrian protection and access (phases 2-4) | \$ 220,000 | line item on trade summary |
| Additional kitchen equipment | \$ 103,000 | Kitchen eqp |
| Allowance for additional electrical | \$ 750,000 | line item on trade summary |
| Sewer by-pass - phase 2 | \$ 50,000 | sitework |
| Foundation and obstruction removal - phase 2,3 | \$ 75,000 | sitework |
| Create clean corridor | \$ 100,000 | sitework |
| Repair engineer barrier at ball fields | \$ 50,000 | sitework |
| Street sweeping - phase 2-3 | \$ 90,000 | sitework |
| Water treatment - allowance for beyond 9 month | \$ 100,000 | sitework |
| Vapor mitigation fans if required | \$ 175,000 | line item on trade summary |
| Clean-up Allowance | n/a | carried as lump sum |
| Phasing Contingency | \$ 650,000 | Trade summary |
| Temp IT/DPW Project IT Coordination | \$ 300,000 | Trade summary |
| Covid GR Impact Costs | \$ 600,000 | Trade summary |
| Acceleration/Selective Over Time | \$ 700,000 | Trade summary |
| TOTAL | \$ 6,115,500 | |
| Quantity Allowance | | |
| Soil disposal | per spec 312001 | with site |
| Oil in UST | 1,000 gal | with site |
| Sludge in UST | 500 gal | with site |
| Water treatment - 9 month | 9 month | lump sum with site |

4. ASSUMPTIONS & QUALIFICATIONS



CONSIGLI
Est. 1905

ASSUMPTIONS & QUALIFICATIONS

ARLINGTON HIGH SCHOOL

GMP 11/24/2020

GENERAL

1. Builders Risk Insurance is by others.
2. All building permit cost is not included and assumed waived by the Town of Arlington.
3. Utility company back charges, user fees, etc (temporary electric, water, gas, etc.) are excluded.
4. Gas, oil, water, and electrical consumption for the active/occupied school is by others.
5. We have included premiums for overtime with asbestos abatement. Overtime for other trades may require funding from the phasing allowance.
6. Winter Conditions costs are included as follows:
 - a) Hot water, admixtures and blankets for winter concrete are included lump sum with concrete contractor.
 - b) Plowing of construction roads and parking is included lump sum with sitework contractor.
 - c) Tarping and building enclosure for weather protection is included with temporary construction line item.
 - d) Temporary heating systems and rentals is included as an allowance with General Requirements.
 - e) Temporary fuel for construction is included as an allowance with General Requirements and Trade Support.
 - f) Winter conditions (shoveling, salting not purchased with trade, road plowing bought with site work) included as an allowance with general requirements.
7. Site Security costs or provisions are not included.
8. An allowance has been included for costs associated with Covid 19. This allowance would fund:
 - a) Cleaning and general requirements that are beyond what was required prior to Covid 19.
9. A phasing contingency is included in the budget and will be used to fund:
 - a) Temporary construction that is in addition to the covered sidewalk or what is identified on the bid documents.
 - b) Modification and/or shoring of the existing building that is to remain so that it may be properly separated from what is to be demolished
 - c) Temporary safety measures associated with building adjacent to an active school.
 - d) Temporary measures to reduce noise or other interruptions to students and staff.
 - e) Off-hour and/or overtime work required between phases to minimize disruption of school activities
10. In addition to the value carried in our general requirements we have included clean-up costs with select non-trade contractors. These costs are assigned as holds on the leveling sheets.
11. Non-trade Consigli RFI log dated 11/3/2020 is part of the contract documents.
12. Preconstruction fee and Parmenter School scope is an addition to the GMP.

THERMAL/MOISTURE PROTECTION

13. Third part QA/QC testing of the vapor membrane - note 8 on GT1.3, shall be by the Owner's LSP.

BUILDING EXTERIOR & STRUCTURE

14. Detail 7/A7.2.9 indicates that metal panel are "dry seal gasket system", however we have included these panels as a rain-screen system.
15. We have not included temporary shoring of metal decks.



CONSIGLI
Est. 1905

ASSUMPTIONS & QUALIFICATIONS

ARLINGTON HIGH SCHOOL

GMP 11/24/2020

FINISHES

16. Concrete slabs will have cracks even when properly installed. These cracks will be visible through the polished concrete.
17. High moisture adhesives are specified for resilient flooring, therefore we are not including moisture mitigation for these floors.
18. Moisture mitigation is included at carpet and entrance mats.
19. A vapor barrier is specified to be installed at wood flooring. No other moisture mitigation is included at these locations

SPECIALTIES/EQUIPMENT/FURNISHINGS

20. We have not included any costs or provisions for FF & E items and assume this will be by the Owner.
21. Roof Anchor plate has been included as Manufacturer's standard 7"x7". Fabricated and installed by Peak Performance.
22. We are not providing the horizontal lifeline system and have not included the design of the horizontal lifeline system required in paragraph 1.5E of Section 110140
23. Roof Anchor eye is stainless steel, the post and base are assumed to be hot dipped galvanized.
24. Roof anchor is based on the layout indicated on project roof plans. Further clarification is required on overall design intent to verify layout is compliant with regulatory standards.
25. Onsite installation of roof anchors shall not be witnessed by a MA P.E. . The installation and the load test reports will be signed off by a P.E.

SITework

26. We have included disposal of regulated soils per specification 312001 – Management and Disposition of Excavated Material. We have included 20% of these quantities with EBP#2 (phase 1) and 80% with phases 2-4.
27. Pricing assumes re-use of all excavated materials.
28. We own Boulders up to 2 Cy in open excavation and up to 1 cy in trenches. All boulders and obstructions larger than these encountered in the ground improvement work shall be removed based on the Unit price listed in the site leveling sheet.
29. Testing and cleaning, video inspection of storm drain includes the newly installed proposed system only.
30. Soil disposal facilities, including unlined and lined landfills, are nearing capacity. Pricing is based upon current capacity and tipping fees. If existing disposal sites close or no longer accept materials from this project, then such an event constitutes a change in the contract. Furthermore, a change in facility could result in additional soil testing. Cost of this testing is not included.
31. Asphalt/Bituminous paving work is based on \$552.20/ton, price as of Dec 1st, 2020
32. Rock/ledge removal premiums are not included.
33. Preparation of SWPPP is assumed to be by others.
34. Treatment of collected surface or ground water is included as an allowance per the estimate.
35. It is assumed that existing loam may be screened and reused in all phases with the need for surface applied amendments only.
36. We have included the disposal of excess loam as RCS<1. Tailings are to be disposed of as unregulated.



CONSIGLI
Est. 1905

ASSUMPTIONS & QUALIFICATIONS

ARLINGTON HIGH SCHOOL

GMP 11/24/2020

- 37. Temporary SOE is to be cut a minimum of 12" below final grade and left in place.
- 38. Stadium lighting foundations are included per drawings dated October 7, 2020 by Structural Engineers, PC. Due to a lack of borings, the engineer has indicated that this design is only a draft. Additional borings may be required. Cost to perform borings is not included.

GROUND IMPROVEMENT (PIF, Helical piles)

- 39. Please note that center of PIFs to be installed beside existing structures should be a minimum of about 3.5' from any vertical face or appurtenance.
- 40. We have not included monitoring for vibration, noise, movement, pile heave or providing Geotech instrumentation.
- 41. We have not included inspection, monitoring, testing of pile welds and certified pile logs. These services shall be provided by the Geo-Tech Engineer.
- 42. Obstructions PIF's- time lost due to obstructions will be charged at the Obstruction Hourly Unit Cost, regardless of the depth at which the obstruction is encountered. The cost impact of any out of tolerance PIFs due to obstructions is also excluded.
- 43. Obstructions Helical Pile: The presence of material that obstructs advancement of the Helical Pile may prohibit reaching the required torque. Any additional piles required due to unaccommodating ground conditions will be based on the Unit cost.

LANDSCAPING

- 44. Drinking fountain specified is section 323000 – Site Furnishings is not shown and not included.
- 45. Integral fence top netting system (par 2.04) and Ball control netting (par 2.05) specified in section 116833 Athletic Fields Equipment are included. However, "tennis court windscreen" (par 2.17) is not shown and not included.
- 46. We have included the specified perimeter drain/anchor system. Consigli may choose to buy this item with the synthetic turf vendor.
- 47. Engraving of brick pavers by others.

ALLOWANCES

See allowance summary sheet

5. CHANGE ORDER LOG

Change Request Log by Status

Consigli Construction Co., Inc.

11/23/20

2153 Arlington High School

| Number | Date | Description | Amount | CO |
|--------|------|-------------|--------|----|
|--------|------|-------------|--------|----|

CHANGE REQUESTS

Not issued

| | | | | |
|-------|----------|--|------------|--|
| CR036 | 09/29/20 | ASI-011 - Revisions to Slab Edge Drawings Part D & E_EST | 7,596.23 | |
| CR037 | 09/29/20 | ASI-013 - Revisions at Foundations Part E and Slab-Edge at 8/S6.1.5_EST | 2,712.94 | |
| CR038 | 10/13/20 | EBP #2 - ASI-012 - SKC-009 Revisions to Drain_EST | 1,085.18 | |
| CR039 | 09/30/20 | ASI-014 - (EBP #4) - Various Revisions to Steel & Concrete | 4,340.70 | |
| CR045 | 10/14/20 | ASI-016 - EBP #4 - Changes to Columns & Slap Depression Extent_EST | 9,766.58 | |
| CR046 | 10/21/20 | ASI-018 - (EBP #4) - Dimension Revisions to Slab Edge Drawings_EST | 5,425.88 | |
| CR054 | 11/03/20 | Phase 1 - Structural Steel Changes from 7/2/20 Conformed Set - 100% CD's_EST | 96,657.91 | |
| CR055 | 11/17/20 | ASI-021 - Revisions to Various Structural Details (Phase 1)_EST | 24,892.49 | |
| CR056 | 11/17/20 | ASI-019 - Various Revisions to Structural Steel (Phase 1)_EST | 18,148.02 | |
| CR058 | 11/17/20 | ASI-020 - Locating Dim. and Revised Dim. for Auditorium Risers and Found Walls_EST | 5,425.88 | |
| CR059 | 11/17/20 | ASI-022 - Roof PV Trellis Steel_EST | 235,482.98 | |

Not issued Total 411,534.79

Potential

| | | | | |
|-------|----------|--|------------|--|
| CR005 | 06/10/20 | Phase 1 (EBP#2) - Transite Pipe Abatement_T&M_EST | 10,343.80 | |
| CR028 | 08/17/20 | EBP#2 - 60% 5/14/20 CDs & 8/11/20 CAD Revisions to Ground Improvements_EST | 3,637.31 | |
| CR034 | 09/16/20 | ASI-009 - Misc. Revisions to EBP4 Steel & Concrete_EST | 19,858.70 | |
| CR040 | 09/30/20 | ASI-003Rev - (EBP #2) - West Lot Retaining Wall Revisions | -10,851.75 | |
| CR047 | 10/21/20 | EBP #2 - RFI-061 - Lining of Piping at DS-2 Structure_EST | 7,053.64 | |
| CR048 | 10/23/20 | Building D - Concrete, Steel, and Schedule Recovery due to Eversource Delay_EST | 97,665.75 | |
| CR049 | 10/26/20 | EBP #2 - Eversource 10/30 Power Shut Down Support Work_EST | 18,447.98 | |
| CR050 | 10/26/20 | EBP#3 - Costello Out of Sequence Mobilization_EST | 8,314.58 | |
| CR053 | 11/02/20 | EBP #3 - Additional Mini-Containments for Out of Sequence ACM Abatement_EST | 20,618.33 | |
| CR057 | 11/17/20 | Direct Cost for Site Safety Implementation due to COVID-19 Pandemic_November_EST | 7,596.23 | |
| CR060 | 11/19/20 | Credit for Security Cameras at Covered Walkway | -13,417.70 | |

Potential Total 169,266.87

Submitted

| | | | | |
|-------|----------|--|-----------|--|
| CR021 | 07/22/20 | EBP #2 - Eversource 2-4 Conduits - Schouler Ct._EST (WO #2387164)_Sub. 101320 | 46,902.50 | |
| CR024 | 07/26/20 | Phase 1 - Clock Tower Ballustrade Removal_Sub. 111720 | 11,868.17 | |
| CR025 | 08/04/20 | EBP#2/4 - Excavate to Expose Eversource Duct Bank Through Phase 1 Bldg. Footprint_T&M_Sub. 111720 | 2,959.03 | |
| CR030 | 08/24/20 | EBP#2 - DPW - Cut/Cap Water Main and Install new Gate Valves on Mass Ave_T&M_Sub. 111720 | 14,014.15 | |
| CR033 | 09/16/20 | EBP#4 - Steel Changes: 60% CD's MSBA Set dated 5/14/20 - "EBP#4 Conf. Set dated 7/2/20_Sub.110320 | 99,423.41 | |
| CR051 | 10/28/20 | EBP #2 - WJGE - Credit Uninstalled Hand Holes West lot & Uninstalled Telecom Duct Bank_Sub. 111720 | -4,168.10 | |

Submitted Total 170,999.16

Approved

| | | | | |
|-------|----------|---|-----------|----|
| BT008 | 09/17/20 | YES - Temp Power Connection for Trailers | 0.00 | '3 |
| CR001 | 04/14/20 | Staffing and General Requirement Costs From Schedule Impacts Due to COVID-19 Pandemic - April | 884.69 | 1 |
| CR002 | 05/06/20 | Staffing & GR Impacts due to COVID-19 - May | 6,086.10 | 3 |
| CR003 | 06/01/20 | Direct Costs for Site Safety Implementation due to COVID-19 Pandemic - June_Sub. 092320 | 11,332.23 | 4 |
| CR004 | 06/03/20 | EBP#2 - Basketball Extended Parking Lot & Phase 1 Access Road Deletion_Sub. 07172020 | 22,877.06 | 1 |

Change Request Log by Status

Consigli Construction Co., Inc.

11/23/20

2153 Arlington High School

| Number | Date | Description | Amount | CO |
|--------|------|-------------|--------|----|
|--------|------|-------------|--------|----|

CHANGE REQUESTS (continued)

Approved (continued)

| | | | | |
|-------|----------|---|------------|---|
| CR007 | 06/11/20 | ASI-004 EBP#2 - Change TMH to Handhole and Change Ductbank D-D depth_Sub. 081920 | -3,115.90 | 2 |
| CR008 | 06/16/20 | CCD-001 EBP#2 - Rev to Electrical Conduits/Ductbanks per Coordination w/ Eversource_REV100520 | -19,129.38 | 6 |
| CR009 | 06/16/20 | CCD-002 - EBP#2 - Revisions to Water Connections at Schouler Court_Sub. 091420 | 10,765.23 | 2 |
| CR012 | 06/30/20 | RFI#006 - EBP#2 - Video Inspection of Sewer Line_T&M_Sub. 100520 | 1,220.60 | 6 |
| CR013 | 07/01/20 | EBP#3 - Verizon Engineering Deposit for Pole Relocation & Disconnect Existing Cabling_Sub. 102820 | 2,329.76 | 6 |
| CR014 | 07/01/20 | EBP#2 - 6th Floor Water Heaters During Gas Shut Down_Sub. 7/30/20 | 3,831.98 | 1 |
| CR015 | 07/01/20 | Direct Costs for Safety Implementation Due to COVID-19 Pandemic - July_Sub. 101420 | 13,321.86 | 4 |
| CR018 | 07/15/20 | EBP#2 - Relocate 8" Water Main in Conflict w/ 36" Drain_T&M_Sub. 100520 | 8,597.48 | 6 |
| CR019 | 07/17/20 | CCD-004 - EBP#3 - Misc. Revisions to Downs Bldg._Sub. 7/30/20 | 2,000.27 | 1 |
| CR022 | 07/27/20 | EBP #2 - RFI #005 - Additional Test Pits at DM-X_T&M_Sub. 07.27.20 | 2,947.16 | 2 |
| CR023 | 07/27/20 | CCD-003 - EBP #2 - Revisions to Electrical MH Size per Eversource Requirement_Sub. 090920 | 16,909.10 | 6 |
| CR026 | 08/08/20 | EBP#3 - EFTR #6 Lenth Increase & Relocation of Ex. Pneumatic Controls_T&M_Sub. 102820 | 1,019.33 | 6 |
| CR027 | 08/17/20 | EBP#3 - CCD-004 - Revise Millwork for Undercounter Dishwasher_Sub. 8/19/20 | 899.41 | 2 |
| CR029 | 08/20/20 | Direct Costs for Safety Implementation Due to COVID-19 Pandemic - August_Sub. 101420 | 13,251.25 | 4 |
| CR031 | 08/26/20 | EBP#2 - Building D Ground Improvement Impacts due to Eversource Delay_Sub. 102220 | 31,334.43 | 6 |
| CR035 | 09/16/20 | Direct Costs for Safety Implementation due to COVID-19 Pandemic_September_Sub. 110220 | 8,727.69 | 5 |
| CR052 | 10/28/20 | Direct Costs for Site Safety Implementation due to COVID-19 Pandemic - October_Sub. 110920 | 6,437.05 | 5 |

Approved Total 142,527.40

Voided

| | | | | |
|-------|----------|---|------------|--|
| CR006 | 06/10/20 | ASI-003 - EBP#2 - Revisions to West Lot Retaining Wall_VOID - Future CCD | 36,895.95 | |
| CR010 | 06/23/20 | EBP#2 - 60% Documents (PV Schouler to West Lot)_VOID - Purchased in 100% | 62,301.25 | |
| CR011 | 06/23/20 | EBP#3 - PreK Red Gym Floor Protection_VOID Riggs GRs | 5,417.50 | |
| CR016 | 07/15/20 | EBP#2 - Rotate (4) Light Poles @ Tennis Court_VOID - See CR004 | 2,190.78 | |
| CR017 | 07/15/20 | EBP#3 - Fusco Cooling Option 1_VOID per SKA Email dated 082820 | 126,102.57 | |
| CR020 | 07/21/20 | EBP#2 - Install Cast Iron Cleanouts on PVC Cleanouts on Sewer Easement_T&M_VOID See HT012 | 1,457.23 | |
| CR032 | 09/09/20 | EBP#3 - CCD-005 - Ramp & Railing Extension_VOID | 9,766.58 | |
| CR041 | 09/30/20 | SKC-011 - Revised Sewer Line Routing_EST_VOID - To be Designed in 100% CD's | 80,052.91 | |
| CR042 | 09/30/20 | SKC-011 - Revised Water Line Routing_EST_VOID - To be Designed in 100% CD's | 128,180.46 | |
| CR043 | 09/30/20 | Lantern & Spire Salvaging - Option A (Phase 1)_EST_VOID - On Hold until Phase 2 | 49,918.05 | |

Voided Total 502,283.28

CHANGE REQUESTS TOTAL 1,396,611.50



Change Request Log by Status

Consigli Construction Co., Inc.

11/23/20

| | |
|-------------------------------|------------------|
| Original Contract Amount: | 55,690,700.00 |
| Approved Contract Changes: | 142,527.40 |
| Revised Contract Amount: | 55,833,227.40 |
| Pending Contract Changes: | 332,669.80 * |



Change Order (CO)

NO: 08

Date of Issuance:

10 November-2020

| | | | |
|-----------------|--|-----------------------|---------------------------------|
| Project: | Arlington Parmenter School fit-out | Contract For: | Renovation |
| Address: | 17 Irving Street, Arlington MA | Contract Date: | February 28, 2020 |
| Owner: | Town of Arlington | | |
| Address: | 730 Massachusetts Avenue Arlington, MA 02476 | Project ID: | |
| From: | HMFH Architects, Inc | To: | Consigli Construction Co., Inc. |
| Address: | 130 Bishop Allen Drive, Cambridge MA 02139 | Address: | 72 Summer Street, Milford MA |

| Items included in this Change Order: | Cost: |
|--|--------------|
| CR 020 Existing Security Conduit relocation- various locations (T&M). | \$ 9,484.09 |
| CR 029 Base scope ACM reconciliation | \$ 16,793.08 |
| CR 032 Temp. power mitigation due to Eversource delayed completion of Permanent Power. | \$ 14,999.40 |
| CR 035 Troubleshoot Existing FACP Troubles (T&M) | \$ 3,593.27 |
| CR 036 Replace Primary Electrical Disconnect (T&M) | \$ 4,460.68 |
| CR 040 Relocation of existing Heating and telecom conduits and cabling in conflict with demolition/new construction. (T&M) | \$ 1,471.59 |
| CR 042 Repairs/replacement to existing 4 th floor lights wiring discovered to be in deteriorated condition (T&M). | \$ 6,279.06 |

Change Order Total: \$ 57,081.00

| THE CONTRACT IS CHANGED AS FOLLOWS: | |
|---|----------------|
| Original Contract Sum was: | \$2,580,810.00 |
| Net change by previously authorized Change Order was: | \$ 160,453.00 |
| Contract Sum prior to this Change Order was: | \$2,741,263.00 |
| Contract Sum will be (increased) (decreased) by Change Order in the amount of: | \$ 57,081.00 |
| New Contract Sum including this Change Order will be: | \$2,798,344.00 |
| Contract Time will remain unchanged . | |
| Date of Substantial Completion as of the date of this Change Order therefore is: | 09/01/2020 |

NOTE: This Change Order does not include changes in the Contract Sum, Contract Time or Guaranteed Maximum Price, which have been authorized by Construction Change Directive until the cost and time have been agreed upon by both the Owner and Contractor, in which case a Change Order is executed to supersede the Construction Change Directive.

NOT VALID UNTIL SIGNED BY THE ARCHITECT, CONTRACTOR AND OWNER.

| | | |
|---|--|---|
| Architect HMFH Architects, Inc. 130 Bishop Allen Drive. Cambridge, MA | Owner's Project Manager Skanska USA Building, Inc. 101 Seaport Boulevard, Suite 200 Boston, MA 02210 | Construction Manager Consigli Construction Co., Inc. 72 Summer Street Milford, MA 01757 |
|  | |  |
| BY (Signature) Arthur Duffy | BY (Signature) Jim Burrows | BY (Signature) John LaMarre |
| 11/10/2020 | | 11/11/20 |
| Date | Date | Date |

| | | |
|--|----------------|----------------|
| Town Manager Adam Chapdelaine 730 Massachusetts Avenue Arlington MA, 02476 | | |
| | | |
| BY (Signature) Adam Chapdelaine | BY (Signature) | BY (Signature) |
| | | |
| Date | Date | Date |

| | | |
|----------------------|--|---|
| Attachments: | Consigli CR 020, 029, 032, 035, 036, 040, 042 | |
| Distribution: | <input checked="" type="checkbox"/> Owner – Adam Chapdelaine | <input checked="" type="checkbox"/> Architect – Arthur Duffy, Peter Rust, Lori Cowles HMFH Architects, Inc. |
| | <input checked="" type="checkbox"/> OPM – Jim Burrows, Sy Nguyen, Hal Raymond Skanska USA Building, Inc. | <input checked="" type="checkbox"/> Contractor – John LaMarre, Todd McCabe, Chris Weber Consigli Construction Co., Inc. |
| | <input checked="" type="checkbox"/> Field – David Rockwood Consigli Construction Co, Inc. | <input type="checkbox"/> Other– |

6. DOCUMENT LIST



Consigli Construction

Current Drawings

| Discipline | Drawing No. | Drawing Title | Revision | Drawing Date | Received Date | Set Name |
|----------------|-------------|---|----------|--------------|---------------|----------------|
| General | | | | | | |
| General | G0.0 v1 | Cover + Drawing List - 100% CD-Bid Set - Volume 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| General | G0.0 v2 | Cover + Drawing List - 100% CD-Bid Set - Volume 2 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| General | G0.0 v3 | Cover + Drawing List - 100% CD-BID SET - Volume 3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | | | | | | |
| Survey | EX0.1 | KEY - EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.1 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.2 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.3 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.4 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.5 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Survey | EX1.6 | EXISTING CONDITIONS PLAN | 5 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | | | | | | |
| Civil | D1.0.1 | DEMOLITION PLAN - PHASE 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | D1.0.2 | DEMOLITION PLAN - PHASE 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | D1.0.3 | DEMOLITION PLAN - PHASE 3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | D1.0.4 | DEMOLITION PLAN - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C1.0.1 | SITE PREPARATION & EROSION CONTROL PLAN - PHASE 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C1.0.2 | SITE PREPARATION & EROSION CONTROL PLAN - PHASE 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C1.0.3 | SITE PREPARATION & EROSION CONTROL PLAN - PHASE 3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C1.0.4 | SITE PREPARATION & EROSION CONTROL PLAN - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C2.0.1 | VEHICULAR & SIGNAGE PLAN - PHASE 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C2.0.2 | VEHICULAR & SIGNAGE PLAN - PHASE 2 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C2.0.3 | VEHICULAR & SIGNAGE PLAN - PHASE 3 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C2.0.4 | VEHICULAR & SIGNAGE PLAN - PHASE 4 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.0.1 | GRADING PLAN - PHASE 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.0.2 | GRADING PLAN - PHASE 2 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.0.3 | GRADING PLAN - PHASE 3 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.0.4 | OVERALL GRADING PLAN - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C3.1.4 | GRADING PLAN A - PHASE 4 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.2.4 | GRADING PLAN B - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C3.3.4 | GRADING PLAN C - PHASE 4 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C3.4.4 | GRADING PLAN D - PHASE 4 | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.1 | OVERALL UTILITY PLAN - PHASE 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C4.0.1A | UTILITY PLAN A - PHASE 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.1B | UTILITY PLAN B - PHASE 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.1C | UTILITY PLAN C - PHASE 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.2 | OVERALL UTILITY PLAN - PHASE 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C4.0.2A | UTILITY PLAN A - PHASE 2 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |



Consigli Construction

| | | | | | | |
|------------------|---------|--|---|------------|------------|----------------|
| Civil | C4.0.3 | OVERALL UTILITY PLAN - PHASE 3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C4.0.3A | UTILITY PLAN A - PHASE 3 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.3B | UTILITY PLAN B - PHASE 3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C4.0.4 | OVERALL UTILITY PLAN - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C4.0.4A | UTILITY PLAN A - PHASE 4 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C4.0.4B | UTILITY PLAN B - PHASE 4 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C5.0.0 | DETAILS SHEET | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C5.1.0 | DETAILS SHEET | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C5.2.0 | DETAILS SHEET | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Civil | C5.3.0 | DETAILS SHEET | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Civil | C5.4.0 | DETAILS SHEET | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | | | | | | |
| Landscape | L-1.1 | LANDSCAPE DEMOLITION AND SITE PREPARATION PLAN 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-1.2 | LANDSCAPE DEMOLITION AND SITE PREPARATION PLAN 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-2.1 | LANDSCAPE MATERIAL PLAN 1 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-2.2 | LANDSCAPE MATERIAL PLAN 2 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-3.1 | LANDSCAPE PLANTING PLAN 1 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-3.2 | LANDSCAPE PLANTING PLAN 2 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Landscape | L-4.1 | LANDSCAPE LAYOUT PLAN 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-4.2 | LANDSCAPE LAYOUT PLAN 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-5.0 | IRRIGATION PLAN, SOUTH LANDSCAPE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-5.1 | IRRIGATION PLAN, NORTH LANDSCAPE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-5.2 | IRRIGATION PLAN, SOUTH TREES | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-5.3 | IRRIGATION PLAN, NORTH TREES | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-5.4 | IRRIGATION DETAILS | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-6.1 | LANDSCAPE ENLARGEMENT PLAN 1 - COURTYARD | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Landscape | L-6.2 | LANDSCAPE ENLARGEMENT PLAN 2 - AMPHITHEATER | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-6.3 | LANDSCAPE ENLARGEMENT PLAN 3 - LOADING DOCK | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-6.4 | LANDSCAPE ENLARGEMENT PLAN 4 - SOUTH PLAZA | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Landscape | L-6.5 | LANDSCAPE ENLARGEMENT PLAN 5 - NORTH PLAZA | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Landscape | L-6.6 | LANDSCAPE ENLARGEMENT PLAN 6 - PLAY AREA | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Landscape | L-7.01 | LANDSCAPE DETAIL - PLANTING | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.02 | LANDSCAPE DETAIL - PAVING | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-7.03 | LANDSCAPE DETAIL - PEDESTRIAN AND TRAFFIC | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.04 | LANDSCAPE DETAIL - FURNISHING I | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.05 | LANDSCAPE DETAIL - FURNISHING II | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.06 | LANDSCAPE DETAIL - STAIR AND RAMP | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L-7.07 | LANDSCAPE DETAIL - BIKE RAMP | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.08 | LANDSCAPE DETAIL - OUTDOOR CLASSROOM AND PLAY | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.09 | LANDSCAPE DETAIL - CHAINLINK FENCE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.10 | LANDSCAPE DETAIL - STEEL PICKET FENCE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L-7.11 | LANDSCAPE DETAIL - PICKET FENCE GATE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | | |
|---------------------|--------|---|---|------------|------------|----------------|
| Landscape | L-7.12 | LANDSCAPE DETAIL - PLANTER | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.1 | OUTDOOR ATHLETIC IMPROVEMENTS MATERIALS PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.2 | OUTDOOR ATHLETIC IMPROVEMENTS LAYOUT PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.3 | OUTDOOR ATHLETIC IMPROVEMENTS GRADING AND DRAINAGE PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.4 | OUTDOOR ATHLETIC IMPROVEMENTS FIELD MARKING PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.5 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L8.6 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.7 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Landscape | L8.8 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.9 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.10 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.11 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.12 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.13 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.14 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.15 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Landscape | L8.16 | OUTDOOR ATHLETIC IMPROVEMENTS DETAILS | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | | | | | | |
| Geotechnical | GT1.1 | First Floor Sub-Slab Ventilation System Plan | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Geotechnical | GT1.2 | Second Floor Sub-Slab Ventilation Sytem Plan | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Geotechnical | GT1.3 | Sub-Slab Ventilation System Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT3.1 | Permanent Soldier Pile Wall Layout | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT3.2 | Permanent Soldier Pile Wall Section | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT3.3 | Permanent Soldier Pile Wall Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT4.1 | Foundation Drainage Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT4.2 | Foundation Drainage Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT6.1 | REPLACEMENT ENGINEERED BARRIER PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT6.2 | REPLACEMENT ENGINEERED BARRIER DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Geotechnical | GT6.3 | REPLACEMENT ENGINEERED BARRIER DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | | | | | | |
| Structural | S0.0 | Structural Framing Model | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S0.1 | General Notes | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.2 | Typical Details I | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.3 | Typical Details II | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.4 | Typical Details III | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.5 | Typical Details IV | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.6 | Typical Details V | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.7 | Typical Details VI | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S0.8 | Typical Details VII | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S1.0 | Grid Layout | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S1.1 | Existing Foundation Overlay Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S1.2 | Phasing Structural Work | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | |
|------------|---------|---|---|------------|---------------------------|
| Structural | S2.0 | First Floor/Foundation Plan - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.0.1a | Pile Cap and Grade Beam Plan - Part a | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.0.1b | Pile Cap and Grade Beam Plan - Part b | 5 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Structural | S2.0.1c | Pile Cap and Grade Beam Plan - Part c | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.0.1e | First Floor/Foundation Plan - Part e | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.0.2a | First Floor Plan - Part a | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.0.2b | First Floor Plan - Part b | 5 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Structural | S2.0.2c | First Floor Plan - Part c | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.1 | Upper First Floor Framing Plan - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.1a | Upper First Floor Framing Plan - Part a | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.1b | Upper First Floor Framing Plan - Part b | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.1c | Upper First Floor Framing Plan - Part c | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.2 | Second Floor Foundation/Framing Plan - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.2a | Second Floor Framing Plan - Part a | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.2b | Second Floor Framing Plan - Part b | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.2c | Second Floor Framing Plan - Part c | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.2d | Second Floor Foundation Plan - Part d | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.2e | Second Floor Foundation Plan - Part e | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Structural | S2.3 | Third Floor/Roof Framing Plan - Overall | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.3a | Third Floor Framing Plan - Part a | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Structural | S2.3b | Third Floor Framing Plan - Part b | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.3c | Third Floor/Roof Framing Plan - Part c | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.3d | Third Floor Framing Plan - Part d | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Structural | S2.3e | Third Floor Framing Plan - Part e | 1 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Structural | S2.4 | Fourth Floor/Roof Framing Plan - Overall | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.4a | Fourth Floor/Roof Framing Plan - Part a | 3 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Structural | S2.4b | Fourth Floor Framing Plan - Part b | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.4d | Fourth Floor Framing Plan - Part d | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Structural | S2.4e | Fourth Floor/Roof Framing Plan - Part e | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.5 | Fifth Floor/Roof Framing Plan - Overall | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.5b | Fifth Floor/Roof Framing Plan - Part b | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.5d | Fifth Floor/Roof Framing Plan - Part d | 2 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S2.5e | EBP4 Fifth Floor/Roof Framing Plan - Part e | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.6 | Roof Framing Plan - Overall | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S2.6b | Roof Framing Plan - Part b | 5 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Structural | S2.6d | Roof Framing Plan - Part d | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S3.1a | Graphical Column Schedule Part a | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Structural | S3.1b | Graphical Column Schedule Part b | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S3.1c | Graphical Column Schedule Part b cont. and Part c | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Structural | S3.1d | EBP4 Graphical Column Schedule Part d | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S3.1e | EBP4 Graphical Column Schedule Part e | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Structural | S3.2 | Base Plate and Pier Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |



Consigli Construction

| | | | | | | |
|------------|---------|--|---|------------|------------|----------------|
| Structural | S3.3 | Pile Cap, Slab, and Grade Beam Details | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Structural | S4.1a.1 | Brace Elevations Part a I | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.1a.2 | Brace Elevations Part a II | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.1b.1 | Brace Elevations Part b | 5 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Structural | S4.1b.2 | Brace and Moment Frame Elevations Part b | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Structural | S4.1c | Brace Elevations Part c | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.1d.1 | EBP4 Brace Elevations Part d I | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.1d.2 | EBP4 Brace Elevations Part d II | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.1e | EBP4 Brace Elevations Part e | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.2.1 | Brace and Moment Frame Details I | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.2.2 | Brace and Moment Frame Details II | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.3.1 | Building Sections I | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.3.2 | Building Sections II | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S4.3.3 | Building Sections III | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Structural | S5.1.1 | EBP4 Foundation Sections I Phase 1 | 1 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S5.1.2 | EBP4 Foundation Sections II Phase 1 | 1 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S5.1.3 | EBP4 Foundation Sections III Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S5.2.1 | Foundation Sections IV Phase 2/3 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Structural | S5.2.2 | Foundation Sections V Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S5.2.3 | Foundation Sections VI Phase 2/3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S5.2.4 | Foundation Sections VII Phase 2/3 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Structural | S5.2.5 | Foundation Sections VIII Phase 2/3 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Structural | S5.2.6 | Foundation Sections IX Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.1 | EBP4 Floor Framing Sections I Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.2 | EBP4 Floor Framing Section II Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.3 | EBP4 Floor Framing Sections III Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.4 | EBP4 Floor Framing Sections IV Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.5 | EBP4 Floor Framing Sections V Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.1.6 | EBP4 Floor Framing Sections VI Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.1 | Floor Framing Sections VII Phase 2/3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.2 | Floor Framing Sections VIII Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S6.2.3 | Floor Framing Sections IX Phase 2/3 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Structural | S6.2.4 | Floor Framing Sections X Phase 2/3 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Structural | S6.2.5 | Floor Framing Sections XI Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S6.2.6 | Floor Framing Sections XII Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.7 | Floor Framing Sections XIII Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.8 | Floor Framing Sections XIV Phase 2/3 | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S6.2.9 | Floor Framing Sections XV Phase 2/3 | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Structural | S6.2.10 | Floor Framing Sections XVI Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.11 | Floor Framing Sections XVII Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S6.2.12 | Floor Framing Sections XVIII Phase 2/3 | 0 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S7.1.1 | EBP4 Roof Framing Sections I Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476

Consigli Construction

| | | | | | | |
|----------------------|--------------|--|---|------------|------------|----------------|
| Structural | S7.1.2 | EBP4 Roof Framing Sections II Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.1.3 | EBP4 Roof Framing Sections III Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.1.4 | EBP4 Roof Framing Sections IV Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.1.5 | EBP4 Roof Framing Sections V Phase 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | EBP4 S7.1.6 | EBP4 Roof Framing Sections VI Phase 1 | 3 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | EBP4 S7.1.10 | EBP4 Roof Framing Sections VII Phase 1 | 3 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.2.1 | Roof Framing Sections VIII Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S7.2.2 | Roof Framing Sections IX Phase 2/3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.2.3 | Roof Framing Sections X Phase 2/3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.2.4 | Roof Framing Sections XI Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S7.2.5 | Roof Framing Sections XII Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.2.6 | Roof Framing Sections XIII Phase 2/3 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Structural | S7.2.7 | Roof Framing Sections XIV Phase 2/3 | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Structural | S7.2.10 | Roof Framing Sections XV Phase 2/3 | 3 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Structural | S7.2.11 | Roof Joist Loading Diagrams Phase 2/3 | 1 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Structural | S10.0 | Forum Seating Framing Details Phase 2/3 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Structural | S13.0 | Athletic Toilet Facility Plans and Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | | | | | | |
| Architectural | A0.1 | Abbreviations & Symbols | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.2 | Code Sheet | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.3 | Code Sheet | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.4 | Code Sheet | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.5 | Code Sheet | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.6 | Code Sheet - Assembly Egress | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A0.7 | Code Sheet - Roof Structure Fire Rating | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.0.0 | Existing Building Information & Demolition Phasing | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.1 | Phase 1a & 2 - First and Upper First Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.2 | Phase 1a & 2 - Third, Fourth, and Fifth Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.3 | Phase 1a & 2 - Infill Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.4 | Phase 1a & 2 - Bridge Connection | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.5 | Temporary Wall Sections and Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.6 | Temporary Wall Sections and Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.7 | Temporary Wall Sections and Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.8 | Phase 2 - Third Floor LABBB Demo, New, & Clg plans, Serv | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.2.9 | Phase 2 - Level 2 Library Floor Plan, Elevs, Details, & Door Sched | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.3.1 | Phase 3 - First and Second Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.3.2 | Phase 3 - Third and Fourth Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.3.3 | Phase 3 - Demo & New Locker Rm, Passageway Plans & Door Schedule | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.4.1 | Phase 4 - Third Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A1.5 | Temporary Phasing Plans/RCPs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.0 | First Floor Plan - Overall | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.0a | First Floor Plan - Part a - ADD4 | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |



Consigli Construction

| | | | | | | |
|---------------|--------|--|---|------------|------------|----------------|
| Architectural | A2.0b | First Floor Plan - Part b - ADD4 | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.0c | First & Upper First Floor Plan - Part c | 4 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Architectural | A2.1 | Upper First Floor Plan - Overall | 3 | 10/6/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.1a | Upper First Floor Plan - Part a | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.1b | Upper First Floor Plan - Part b - ADD4 | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.2 | Second Floor Plan - Overall | 3 | 10/6/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.2a | Second Floor Plan - Part a - ADD4 | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.2b | Second Floor Plan - Part b | 5 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Architectural | A2.2c | Second Floor Plan - Part c | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.2d | Second Floor Plan - Part d | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.2e | Second Floor Plan - Part e - ADD4 | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.3 | Third Floor Plan - Overall | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.3a | Third Floor Plan - Part a | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.3b | Third Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.3d | Third Floor Plan - Part d | 5 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Architectural | A2.3e | Third Floor Plan - Part e | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.4 | Fourth Floor Plan - Overall | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.4b | Fourth Floor Plan - Part b | 3 | 10/6/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.4d | Fourth Floor Plan - Part d | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.4e | Fourth Floor Plan - Part e | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.5 | Fifth Floor Plan - Overall | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.5b | Fifth Floor Plan - Part b & Roof Access | 3 | 10/6/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.5d | Fifth Floor Plan - Part d & Roof Access | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.6 | Overall Roof Plan | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A2.6.1 | Roof Plan Parts d and e (Phase 1) | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.6.2 | Roof Plan Parts b and c (Phase 2) | 3 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.6.3 | Roof Plan Parts a and e (Phase 3) | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.7a | First Floor Slab Edge Plan | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.7b | Upper First Floor Slab Edge Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.7c | Second Floor Slab Edge Plan | 2 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.7d | Third Floor Slab Edge Plan | 1 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.7e | Fourth Floor Slab Edge Plan | 1 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.7f | Fifth Floor Slab Edge Plan | 2 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A2.7g | Roof Slab Edge Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.7h | Slab Edge Detail Plans | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.7i | Control Joint Plans | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A2.8 | Catwalk Plans and Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.9.0 | First Floor Plan - Flooring Patterns | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.9.1 | Upper First Floor Plan - Flooring Patterns | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.9.2 | Second Floor Plan - Flooring Patterns | 1 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Architectural | A2.9.3 | Third Floor Plan - Flooring Patterns | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A2.9.4 | Fourth Floor Plan - Flooring Patterns | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | |
|---------------|--------|--|---|------------|---------------------------|
| Architectural | A2.9.5 | Fifth Floor Plan - Flooring Patterns | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.0 | First Floor Reflected Ceiling Plan | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.0a | First Floor Reflected Ceiling Plan - Part a | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.0b | First & Upper First Floor Reflected Ceiling Plan - Part b - ADD4 | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.0c | First & Upper First Floor Reflected Ceiling Plan - Part c - ADD4 | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.1a | Upper First Floor Reflected Ceiling Plan - Part a | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.2 | Second Floor Reflected Ceiling Plan | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.2a | Second Floor Reflected Ceiling Plan - Part a - ADD2 | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A3.2b | Second Floor Reflected Ceiling Plan - Part b - ADD3 | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.2c | Second Floor Reflected Ceiling Plan - Part c - ADD3 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.2d | Second Floor Reflected Ceiling Plan - Part d - ADD3 | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.2e | Second Floor Reflected Ceiling Plan - Part e - ADD2 | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.3 | Third Floor Reflected Ceiling Plan | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.3a | Third Floor Reflected Ceiling Plan - Part a | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.3b | Third Floor Reflected Ceiling Plan - Part b | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.3d | Third Floor Reflected Ceiling Plan - Part d - ADD3 | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.3e | Third Floor Reflected Ceiling Plan - Part e - ADD3 | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.4 | Fourth Floor Reflected Ceiling Plan | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.4b | Fourth Floor Reflected Ceiling Plan - Part b - ADD3 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.4d | Fourth Floor Reflected Ceiling Plan - Part d - ADD3 | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A3.4e | Fourth Floor Reflected Ceiling Plan - Part e | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.5 | Fifth Floor Reflected Ceiling Plan | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.5b | Fifth Floor Reflected Ceiling Plan - Part b - ADD2 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.5d | Fifth Floor Reflected Ceiling Plan - Part d - ADD3 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A3.6 | Reflected Ceiling Plan - Legend, Types & Details | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A3.7 | Reflected Ceiling Plan - Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A3.8 | Skylight Details - ADD2 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A4.1.1 | Building Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.1.2 | Building Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.1.3 | Building Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.2.1 | Isometric Views - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.2.2 | Isometric Views - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.3.1 | Exterior Elevations - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.3.2 | Exterior Elevations - Overall | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.3.3 | Exterior Elevations - Part a and b | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.3.4 | Exterior Elevations - Part b and c | 3 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Architectural | A4.3.5 | Exterior Elevations - Part b and c | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A4.3.6 | Exterior Elevations - Part b and d | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A4.3.7 | Exterior Elevations - Part d | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A4.3.8 | Exterior Elevations - Part e | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Architectural | A4.3.9 | Exterior Elevations - Part a and e | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A4.4.1 | Exterior Enlarged Elevations - Window Layout | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |



Consigli Construction

| | | | | | | |
|---------------|---------|---|---|------------|------------|----------------|
| Architectural | A4.4.2 | Exterior Enlarged Elevations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A4.4.3 | Brick and CMU Patterning | 1 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A4.5.1 | Exterior Elevations - Part a and b Shade Locations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A4.5.2 | Exterior Elevations - Part b and c Shade Locations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A4.5.3 | Exterior Elevations - Part b and d Shade Locations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A4.5.4 | Exterior Elevations - Part d and e Shade Locations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A4.5.5 | Exterior Elevations - Part a and e Shade Locations | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1a | Wall Sections - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1b.1 | Wall Sections - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1b.2 | Wall Sections - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1c | Wall Sections - Part c | 3 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1d.1 | Wall Sections - Part d | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A5.1d.2 | Wall Sections - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1d.3 | Wall Sections - Part d | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1d.4 | Wall Sections - Part d & b | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A5.1e.1 | Wall Sections - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A5.1e.2 | Wall Sections - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A6.1.1 | Exterior Wall Types and Section Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A6.1.2 | Exterior Wall Types and Section Details | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A6.1.3 | Exterior Wall Types and Section Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A6.1.4 | Exterior Wall Details - ADD 4 | 1 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Architectural | A6.2.1 | Fusco Building Entry - Salvage and Reuse | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A6.3.1 | Roof Details - Thermoplastic Membrane Roofing | 3 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Architectural | A7.1.1 | Window, Louver & Fiberglass Sandwich Panel Types & Profiles | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.1.2 | Window, Louver & Fiberglass Sandwich Panel Details | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A7.2.1 | Curtainwall Schedule CW 01 - CW 18B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A7.2.2 | Curtainwall Schedule CW 19-CW 34 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.2.3 | Curtainwall Schedule CW 35A - CW 46 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.2.4 | Curtainwall Schedule CW 48A - CW 59 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A7.2.5 | Interior Curtainwall Schedule | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A7.2.6 | Curtainwall Details and Profiles | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.2.7 | Curtainwall Details | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Architectural | A7.2.8 | Curtainwall Details | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A7.2.9 | Curtainwall Details | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Architectural | A7.2.10 | Curtainwall and Modular Skylight Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.2.11 | Modular Skylight Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A7.2.12 | Enlarged Plan at North Entry | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Architectural | A8.1 | Partition Types | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A8.2 | Typical Interior Partition Details | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A8.3.1 | Interior Wall Sections - Lightwells | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A8.3.2 | Interior Wall Sections - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A8.3.3 | Interior Wall Sections - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | |
|---------------|---------|---|---|------------|---------------------------|
| Architectural | A8.3.4 | Interior Wall Sections - Part d and e | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.3.5 | Interior Wall Sections - Part e | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.3.6 | Interior Wall Sections - Part a | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A8.3.7 | Interior Wall Section Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.4.1 | Enlarged Plan Details | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A8.4.2 | Enlarged Plan Details | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A8.4.3 | Enlarged Plan Details | 4 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Architectural | A8.4.4 | Enlarged Plan Details - Expansion Joints - Part a - ADD4 | 2 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A8.4.5 | Enlarged Plan Details - Expansion Joints - Part d and e | 0 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A8.5.1 | Locker Pod Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.6.1 | Custom Millwork Details - Benches | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.6.2 | Custom Millwork Details - Benches | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.6.3 | Custom Millwork Details - Desks | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.6.4 | Custom Millwork Details - Display Cases | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Architectural | A8.6.5 | Custom Millwork Details - Forum & PreK | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.6.6 | Custom Millwork Details | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Architectural | A8.6.7 | Custom Millwork Details - Counters | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A8.6.8 | Custom Millwork Details - Counters | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A8.6.9 | Wood Paneling Elevations & Details | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A8.7.1 | Auditorium and Wood Paneling Elevations and Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.2 | Auditorium and Wood Paneling Elevations and Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.3 | Auditorium Ceiling Wood Paneling Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.3a | Auditorium Ceiling Section Diagrams | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.4 | Auditorium and Wood Paneling Details | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A8.7.4a | Auditorium and Wood Paneling Section and Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.5 | Auditorium Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.6 | Auditorium Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.7 | Auditorium Balcony Enlarged Plans and Elevations | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.7a | Auditorium Balcony Facets - North | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.7b | Auditorium Balcony Facets - East | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.7c | Auditorium Balcony Facets - South | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.8 | Auditorium Entry Plans, Elevations and Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A8.7.9 | Auditorium Entry Sections and Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A9.1 | Door Schedule - Exterior & First | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A9.2 | Door Schedule - Upper First & Second | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Architectural | A9.3 | Door Schedule - Third, Fourth, & Fifth | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A9.4 | Borrowed Light & Glass Partition Schedule - 1st, U 1st, & 2nd | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A9.5 | Borrowed Light & Glass Partition Schedule - 3rd, 4th & 5th | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A9.6 | Door Frame Details & Thresholds | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A9.7.1 | Specialty Doors and Operable Partition Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A9.7.2 | Specialty Doors and Operable Partition Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A9.7.3 | Specialty Doors and Operable Partition Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |



Consigli Construction

| | | | | | |
|---------------|----------|--|---|------------|---------------------------|
| Architectural | A10.0.1 | Stair Details | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.0.2 | Stair Details | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A10.0.3 | Roof & Interior Ladder Details | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Architectural | A10.1.1 | Stair 1 - Enlarged Plans and Sections | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A10.1.2 | Stair 1 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.1.3 | Stair 2 - Enlarged Plans and Sections | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A10.1.4 | Stair 3 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.1.5 | Stair 4 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.1.6 | Stair 5 & 6 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.1.7 | Stair 7 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.1.8 | Stair 8 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.2.1 | Stair 9 & 10 - Enlarged Plans and Sections | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A10.2.2 | Stair 11 & 12 - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.2.3 | Stair 13 & DLab Ramp - Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.3.1 | Forum Stair | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A10.3.2 | Forum Stair | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A10.4.1 | Elevator & Wheelchair Lift Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A10.4.2 | Elevator Plans and Sections | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A11.1 | Toilet Plans & Elevations | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A11.2 | Toilet Plans & Elevations | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A11.3 | Toilet Plans & Elevations | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A11.4 | Toilet Plans & Elevations | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.1.1 | Interior Elevations - Typical Core Academic Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.1.2 | Interior Elevations - SPED Core Academic Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.2.1 | Interior Elevations - Pre-School and Daycare | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.3.1 | Interior Elevations - Art and Music Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.3.2 | Interior Elevations - Art and Music Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.4.1 | Interior Elevations - Vocations and Technology Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.5.1 | Interior Elevations - Health and Physical Education Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.5.2 | Interior Elevations - Health and Physical Education Spaces | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A12.5.3 | Interior Elevations - Health and Physical Education Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.5.4 | Interior Elevations - Locker Rooms | 2 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Architectural | A12.6.1 | Interior Elevations - Library Learning Commons | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.6.2 | Interior Elevations - LLC and Associated Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.7.1 | Interior Elevations - Performing Arts Spaces & Discourse Lab | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.7.2 | Interior Elevations - Performing Arts Spaces | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.7.3 | Interior Elevations - Auditorium | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.8.0a | Interior Elevations - Spine East | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.8.0b | Interior Elevations - Spine West | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.8.0c | Interior Elevations - Spine Upper Corridors | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Architectural | A12.8.1 | Interior Elevations - Cafeteria | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Architectural | A12.8.2 | Interior Elevations - Circulation Corridors - Part a | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |

Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476



Consigli Construction

| | | | | | | |
|---------------------|---------|---|---|------------|------------|----------------|
| Architectural | A12.8.3 | Interior Elevations - Circulation Corridors - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.8.4 | Interior Elevations - Circulation Corridors - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.8.5 | Interior Elevations - Circulation Corridors - Part b/d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.8.6 | Interior Elevations - Circulation Corridors - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.8.7 | Interior Elevations - Circulation Corridors - Part d | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.8.8 | Interior Elevations - Circulation Corridors - Part c - Pre-School | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A12.8.9 | Interior Elevations - Circulation Corridors - Part e | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A12.9 | Interior Elevations - District Admin | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | A13.0 | Athletic Toilet Facility | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Architectural | A13.1 | Athletic Toilet Facility Exterior Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Architectural | AV2.2e | TECH AV - Second Floor Plan - Part e | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | | | | | | |
| Casework | FC2.0a | First Floor Plan - Part a Fixed Casework | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Casework | FC2.0b | First Floor Plan - Part b Fixed Casework | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Casework | FC2.0c | First & Upper First Floor Plan - Part c Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.1b | Upper First Floor Plan - Part b Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.2a | Second Floor Plan - Part a Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.2b | Second Floor Plan - Part b Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.2c | Second Floor Plan - Part c Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.2d | Second Floor Plan - Part d Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.2e | Second Floor Plan - Part e Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.3b | Third Floor Plan - Part b Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.3d | Third Floor Plan - Part d Fixed Casework | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Casework | FC2.3e | Third Floor Plan - Part e Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.4b | Fourth Floor Plan - Part b Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.4d | Fourth Floor Plan - Part d Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.5b | Fifth Floor Plan - Part b Fixed Casework | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Casework | FC2.5d | Fifth Floor Plan - Part d Fixed Casework | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Casework | FC3.1. | CASEWORK ELEVATIONS | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Casework | FC3.2. | CASEWORK ELEVATIONS | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Casework | FC3.3. | CASEWORK ELEVATIONS & DETAILS | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Food Service | | | | | | |
| Food Service | K0.1 | Foodservice Utility Schedule & Equipment Layout | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K0.2 | Foodservice Point Of Connection Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K1.1 | Foodservice Utility Schedule | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K2.1 | Foodservice Equipment Layout | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K2.2 | Foodservice Building Conditions Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K2.3 | Foodservice Plumbing Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K2.4 | Foodservice Electrical Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K3.1 | Foodservice Fabrication Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K3.2 | Foodservice Fabrication Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K3.3 | Foodservice Fabrication Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |

Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476



Consigli Construction

| | | | | | | |
|------------------------|---------|--|---|------------|------------|----------------|
| Food Service | K4.1 | Foodservice Millwork Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K4.2 | Foodservice Millwork Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K5.1 | Foodservice Fabrication Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K5.2 | Foodservice Fabrication Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K6.1 | Foodservice Manufacturer Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K6.2 | Foodservice Manufacturer Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K6.3 | Foodservice Manufacturer Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Food Service | K6.4 | Foodservice Manufacturer Drawings | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Protection | | | | | | |
| Fire Protection | FP0.1 | FIRE PROTECTION LEGEND AND NOTES | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP1.2.3 | FIRE PROTECTION 1A & 2 - INFILL DETAILS | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Protection | FP1.2.4 | FIRE PROTECTION ENLARGED BRIDGE PLAN | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.0a | FIRE PROTECTION FIRST FLOOR PLAN - PART A | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.0b | FIRE PROTECTION FIRST FLOOR PLAN - PART B | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.0c | FIRE PROTECTION FIRST FLOOR PLAN - PART C | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Protection | FP2.2a | FIRE PROTECTION SECOND FLOOR PLAN - PART A | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.2b | FIRE PROTECTION SECOND FLOOR PLAN - PART B | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.2c | FIRE PROTECTION SECOND FLOOR PLAN - PART C | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.2d | FIRE PROTECTION SECOND FLOOR PLAN - PART D | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.2e | FIRE PROTECTION SECOND FLOOR PLAN - PART E | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.3a | FIRE PROTECTION THIRD FLOOR PLAN - PART A | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.3b | FIRE PROTECTION THIRD FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.3d | FIRE PROTECTION THIRD FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.3e | FIRE PROTECTION THIRD FLOOR PLAN - PART E | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.4b | FIRE PROTECTION FOURTH FLOOR PLAN - PART B | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.4d | FIRE PROTECTION FOURTH FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.4e | FIRE PROTECTION FOURTH FLOOR PLAN - PART E | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.5b | FIRE PROTECTION FIFTH FLOOR PLAN - PART B | 6 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.5d | FIRE PROTECTION FIFTH FLOOR PLAN - PART D | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Protection | FP2.6 | FIRE PROTECTION ROOF PLAN | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Protection | FP3.1 | FIRE PROTECTION DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Protection | FP3.2 | FIRE PROTECTION RISER DIAGRAM | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | | | | | | |
| Plumbing | P0.1 | PLUMBING SCHEDULE, LEGEND, AND NOTES | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P1.0 | PLUMBING PHASING PLAN | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P1.2.1 | PLUMBING PHASE 2 - FIRST AND UPPER FIRST FLOOR PLAN | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P1.2.3 | PLUMBING PHASE 1A & 2 - INFILL DETAILS | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P1.2.8 | PLUMBING PHASE 2 - LEVEL 3 DEMO & NEW ENLARGED PLANS | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P1.3.3 | PLUMBING PHASE 3 - DEMO & NEW ENLARGED LOCKER RM PLANS | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.00a | PLUMBING UNDERSLAB PLAN - PART A | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.00b | PLUMBING UNDERSLAB PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.00c | PLUMBING UNDERSLAB PLAN - PART C | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |

Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476



Consigli Construction

| | | | | | | |
|-------------------|--------|--|---|------------|------------|----------------|
| Plumbing | P2.00d | PLUMBING UNDERSLAB PLAN - PART D | 3 | 10/27/2020 | 10/26/2020 | Addendum no. 2 |
| Plumbing | P2.00e | PLUMBING UNDERSLAB PLAN - PART E | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Plumbing | P2.0a | PLUMBING FIRST FLOOR PLAN - PART A | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.0b | PLUMBING FIRST FLOOR PLAN - PART B | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.0c | PLUMBING FIRST & UPPER FLOOR PLAN - PART C | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.2a | PLUMBING SECOND FLOOR PLAN - PART A | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.2b | PLUMBING SECOND FLOOR PLAN - PART B | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.2c | PLUMBING SECOND FLOOR PLAN - PART C | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.2d | PLUMBING SECOND FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.2e | PLUMBING SECOND FLOOR PLAN - PART E | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Plumbing | P2.3a | PLUMBING THIRD FLOOR PLAN - PART A | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.3b | PLUMBING THIRD FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.3d | PLUMBING THIRD FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.3e | PLUMBING THIRD FLOOR PLAN - PART E | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.4b | PLUMBING FOURTH FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.4d | PLUMBING FOURTH FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.4e | PLUMBING FOURTH FLOOR PLAN - PART E | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.5b | PLUMBING FIFTH FLOOR PLAN - PART B | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Plumbing | P2.5d | PLUMBING FIFTH FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.6a | PLUMBING ROOF PLAN - PART A | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Plumbing | P2.6b | PLUMBING ROOF PLAN - PART B | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P2.6c | PLUMBING ROOF PLAN - PART C | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P2.6d | PLUMBING ROOF PLAN - PART D | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Plumbing | P2.6e | PLUMBING ROOF PLAN - PART E | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Plumbing | P3.1 | PLUMBING DETAILS #1 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P3.2 | PLUMBING DETAILS #2 | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P4.1 | PLUMBING KITCHEN PART PLAN | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P5.0 | PLUMBING RISER DIAGRAMS | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Plumbing | P5.1 | PLUMBING RISER DIAGRAMS | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Mechanical | | | | | | |
| Mechanical | M0.1 | HVAC LEGEND | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Mechanical | M0.2 | HVAC DETAILS SHEET #1 | 3 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Mechanical | M0.3 | HVAC DETAILS SHEET #2 | 3 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Mechanical | M0.4 | HVAC DETAILS SHEET #3 | 4 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M0.5 | HVAC DETAILS SHEET #4 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Mechanical | M0.6 | HVAC DETAILS SHEET #5 | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Mechanical | M0.7 | HVAC ZONING PLAN 1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M0.8 | HVAC ZONING PLAN 2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M0.9 | HVAC AIR HANDLING UNIT DETAILS #1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M0.10 | HVAC AIR HANDLING UNIT DETAILS #2 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M0.11 | HVAC AIR HANDLING UNIT DETAILS #3 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M0.12 | HVAC AIR HANDLING UNIT DETAILS #4 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | |
|------------|--------|--|---|------------|---------------------------|
| Mechanical | M1.1 | HVAC PHASE 2 TEMPORARY WORK PLAN | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M1.2.3 | HVAC Phase 1a & 2 - Infill Details | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M1.2.4 | HVAC Enlarged Bridge Plan | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M1.2.8 | HVAC Phase 2 - Level 3 Demo & New Enlarged Plans | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M1.3.1 | HVAC Phase 3 - First and Upper First Floor Plan | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M2.0a | HVAC FIRST FLOOR PLAN - PART A | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.0b | HVAC FIRST FLOOR PLAN - PART B | 7 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M2.0c | HVAC FIRST FLOOR PLAN - PART C | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.1b | HVAC FIRST FLOOR PART PLANS - PART B | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.1c | HVAC UPPER FIRST FLOOR PLAN - PART C | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.2a | HVAC SECOND FLOOR PLAN - PART A | 5 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M2.2b | HVAC SECOND FLOOR PLAN - PART B | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.2c | HVAC SECOND FLOOR PLAN - PART C | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.2d | HVAC SECOND FLOOR PLAN - PART D | 6 | 11/6/2020 | 11/6/2020 Addendum no. 5 |
| Mechanical | M2.2e | HVAC SECOND FLOOR PLAN - PART E | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.3a | HVAC THIRD FLOOR PLAN - PART A | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.3b | HVAC THIRD FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.3d | HVAC THIRD FLOOR PLAN - PART D | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.3e | HVAC THIRD FLOOR PLAN - PART E | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.4b | HVAC FOURTH FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.4d | HVAC FOURTH FLOOR PLAN - PART D | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.4e | HVAC FOURTH FLOOR & ROOF PLAN - PART E | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.5b | HVAC FIFTH FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Mechanical | M2.5d | HVAC FIFTH FLOOR PLAN - PART D | 7 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M2.6a | HVAC ROOF PLAN - PART A | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M2.6b | HVAC ROOF PLAN - PART B | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Mechanical | M2.6c | HVAC ROOF PLAN - PART C | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Mechanical | M2.6d | HVAC ROOF PLAN - PART D | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.0a | HVAC FIRST FLOOR PIPING PLAN - PART A | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.0b | HVAC FIRST FLOOR PIPING PLAN - PART B | 5 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M3.0c | HVAC FIRST FLOOR PIPING PLAN - PART C | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Mechanical | M3.1b | HVAC FIRST FLOOR PIPING PART PLANS - PART B | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.1c | HVAC UPPER FIRST FLOOR PIPING PLAN - PART C | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Mechanical | M3.2a | HVAC SECOND FLOOR PIPING PLAN - PART A | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.2b | HVAC SECOND FLOOR PIPING PLAN - PART B | 4 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M3.2c | HVAC SECOND FLOOR PIPING PLAN - PART C | 1 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Mechanical | M3.2d | HVAC SECOND FLOOR PIPING PLAN - PART D | 4 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M3.2e | HVAC SECOND FLOOR PIPING PLAN - PART E | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.3a | HVAC THIRD FLOOR PIPING PLAN - PART A | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Mechanical | M3.3b | HVAC THIRD FLOOR PIPING PLAN - PART B | 5 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M3.3d | HVAC THIRD FLOOR PIPING PLAN - PART D | 4 | 11/6/2020 | 11/6/2020 Addendum no. 6 |
| Mechanical | M3.3e | HVAC THIRD FLOOR PIPING PLAN - PART E | 2 | 11/6/2020 | 11/6/2020 Addendum no. 6 |



Consigli Construction

| | | | | | | |
|-------------------|----------|---|---|------------|------------|----------------|
| Mechanical | M3.4b | HVAC FOURTH FLOOR PIPING PLAN - PART B | 5 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M3.4d | HVAC FOURTH FLOOR PIPING PLAN - PART D | 4 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M3.4e | HVAC FOURTH FLOOR & ROOF PIPING PLAN - PART E | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M3.5b | HVAC FIFTH FLOOR PIPING PLAN - PART B | 5 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M3.5d | HVAC FIFTH FLOOR PIPING PLAN - PART D | 4 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M3.6a | HVAC ROOF PIPING PLAN - PART A | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Mechanical | M3.6b | HVAC ROOF PIPING PLAN - PART B | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Mechanical | M3.6c | HVAC ROOF PIPING PLAN - PART C | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Mechanical | M3.6d | HVAC ROOF PIPING PLAN - PART D | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M4.1 | HVAC MECHANICAL ROOM ENLARGED PART PLANS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M5.1 | HVAC SCHEDULES SHEET #1 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M5.2 | HVAC SCHEDULES SHEET #2 | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Mechanical | M5.3 | HVAC SCHEDULES SHEET #3 | 8 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M5.4 | HVAC SCHEDULES SHEET #4 | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Mechanical | M5.5 | HVAC SCHEDULES SHEET #5 | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Mechanical | M5.6 | HVAC SCHEDULE SHEET #6 | 3 | 11/6/2020 | 11/6/2020 | Addendum no. 6 |
| Mechanical | M5.7 | HVAC SCHEDULE SHEET #7 | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Mechanical | M5.8 | HVAC SCHEDULE SHEET #8 | 4 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Mechanical | M6.1 | HVAC TOILET FACILITY BUILDING | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | | | | | | |
| Electrical | E0.1 | ELECTRICAL LEGEND | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E0.2.0 | LUMINARE SCHEDULE | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E0.2.1 | LUMINAIRE SCHEDULE | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E0.2.2 | LUMINAIRE SCHEDULE NOTES | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E0.3 | LIGHTING CONTROL NARRATIVE AND DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E0.3.1 | LIGHTING CONTROL DETAILS | 4 | 11/4/2020 | 11/9/2020 | Addendum no. 5 |
| Electrical | E1.2.1 | Phase 1a & 2 - First and Second Floor Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.2.2 | Phase 1a & 2 - Third, Fourth and Fifth Floor Plan | 0 | 8/2/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.2.3 | Electrical Phase 1a & 2 - Infill Details | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E1.2.4 | Phase 1a & 2 - Bridge Connection | 2 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E1.2.5 | Phase 2 Third Floor Temp. Survey Plan | 1 | 10/15/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E1.2.5.1 | Phase 1a & 2 Temp. Servery Equipment Schedule | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E1.2.6 | PHASE 1A & 2 POWER RISER DIAGRAM | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.2.7 | Phase 2 - Third Floor - LABBB Enlarged Plans | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E1.2.7.1 | Phase 2 - Third Floor- LABBB Diagrams and Schedules | 0 | 4/30/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.2.8 | Phase 2 - Second Floor - Library Part Plans | 0 | 8/27/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.2.9 | Phase 2 - Panel Schedules | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E1.2.10 | PHASE 2 - FIFTH FLOOR TEMP. FACS CLASSROOMS | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E1.3.1 | Phase 3 - First and Second Floor Plan | 0 | 8/27/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.3.2 | Phase 3 - Third and Fourth Floor Plan | 0 | 10/1/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.3.3 | Phase 3 - Enlarged Locker Room Plans - Demo and New | 0 | 8/27/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E1.4.1 | Phase 4 - Third Floor Plan | 0 | 10/1/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | | |
|------------|---------|---|---|------------|------------|----------------|
| Electrical | E2.0 | POWER AND SYSTEMS FIRST FLOOR PLAN-OVERALL | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E2.0a | POWER AND SYSTEMS FIRST FLOOR PLAN - PART A | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.0b | POWER AND SYSTEMS FIRST FLOOR PLAN - PART B | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.0c | POWER & SYSTEMS FIRST FLOOR UPPER FIRST PLAN - PART C | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.0d | UNDERSLAB PLAN - PARTS D, E | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E2.0d.1 | PART D STORAGE TUNNEL PLANS | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.0e | UNDERSLAB PLAN - PARTS A, B, C | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E2.1 | POWER AND SYSTEMS UPPER FIRST FLOOR PLAN-OVERALL | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E2.1a | POWER AND SYSTEMS UPPER FIRST FLOOR PLAN - PART A | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E2.2 | POWER AND SYSTEMS SECOND FLOOR PLAN-OVERALL | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Electrical | E2.2a | POWER AND SYSTEMS SECOND FLOOR PLAN - PART A | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.2b | POWER AND SYSTEMS SECOND FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.2c | POWER AND SYSTEMS SECOND FLOOR PLAN - PART C | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.2d | POWER AND SYSTEMS SECOND FLOOR PLAN - PART D | 7 | 11/4/2020 | 11/9/2020 | Addendum no. 5 |
| Electrical | E2.2e | POWER AND SYSTEMS SECOND FLOOR PLAN - PART E | 5 | 11/4/2020 | 11/9/2020 | Addendum no. 5 |
| Electrical | E2.3 | POWER AND SYSTEMS THIRD FLOOR PLAN-OVERALL | 2 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E2.3a | POWER AND SYSTEMS THIRD FLOOR PLAN - PART A | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E2.3b | POWER AND SYSTEMS THIRD FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.3d | POWER AND SYSTEMS THIRD FLOOR PLAN - PART D | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.3e | POWER AND SYSTEMS THIRD FLOOR PLAN - PART E | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.4 | POWER AND SYSTEMS FOURTH FLOOR PLAN-OVERALL | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.4a | POWER AND SYSTEMS FOURTH FLOOR PLAN - PART A | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.4b | POWER AND SYSTEMS FOURTH FLOOR PLAN - PART B | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.4d | POWER AND SYSTEMS FOURTH FLOOR PLAN - PART D | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.4e | POWER AND SYSTEMS FOURTH FLOOR PLAN - PART E | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.5 | POWER AND SYSTEMS FIFTH FLOOR PLAN-OVERALL | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E2.5b | POWER AND SYSTEMS FIFTH FLOOR PLAN - PART B | 6 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E2.5d | POWER AND SYSTEMS FIFTH FLOOR PLAN - PART D | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.6 | POWER AND SYSTEMS ROOF PLAN-OVERALL | 2 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Electrical | E2.6b | POWER AND SYSTEMS ROOF PLAN - PART B | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.6c | POWER AND SYSTEMS ROOF PLAN - PART C | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.6d | POWER AND SYSTEMS ROOF PLAN - PART D | 5 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E2.6e | POWER AND SYSTEMS ROOF PLAN - PART E | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E2.7e | POWER AND SYSTEMS CATWALK PLANS - PART E | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E3.0 | LIGHTING FIRST FLOOR PLAN-OVERALL | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E3.0a | LIGHTING FIRST FLOOR PLAN - PART A | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E3.0b | LIGHTING FIRST FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E3.0c | LIGHTING FIRST FLOOR PLAN - PART C | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E3.0.1 | LIGHTING SITE PLAN 1 | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E3.0.2 | LIGHTING SITE PLAN 2 | 3 | 11/4/2020 | 11/9/2020 | Addendum no. 5 |
| Electrical | E3.2 | LIGHTING SECOND FLOOR PLAN-OVERALL | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E3.2a | LIGHTING SECOND FLOOR PLAN - PART A | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |



Consigli Construction

| | | | | | |
|------------|---------|---|-----|------------|---------------------------|
| Electrical | E3.2b | LIGHTING SECOND FLOOR PLAN - PART B | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.2c | LIGHTING SECOND FLOOR PLAN - PART C | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.2d | LIGHTING SECOND FLOOR PLAN - PART D | 6 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.2e | LIGHTING SECOND FLOOR PLAN - PART E | 5 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E3.3 | LIGHTING THIRD FLOOR PLAN-OVERALL | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E3.3a | LIGHTING THIRD FLOOR PLAN - PART A | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E3.3b | LIGHTING THIRD FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E3.3d | LIGHTING THIRD FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E3.3e | LIGHTING THIRD FLOOR PLAN - PART E | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.4 | LIGHTING FOURTH FLOOR PLAN-OVERALL | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E3.4b | LIGHTING FOURTH FLOOR PLAN - PART B | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.4d | LIGHTING FOURTH FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E3.4e | LIGHTING FOURTH FLOOR PLAN - PART E | 3.2 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E3.5 | LIGHTING FIFTH FLOOR PLAN-OVERALL | 0 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E3.5b | LIGHTING FIFTH FLOOR PLAN - PART B | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E3.5d | LIGHTING FIFTH FLOOR PLAN - PART D | 4 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E3.6e | LIGHTING CATWALK PLANS PART E | 1 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E4.0.1 | SITE DEMOLITION PLAN - PHASE 1 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.0.2. | SITE DEMOLITION PLAN - PHASE 2 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.0.3 | SITE DEMOLITION PLAN - PHASE 3 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.0.4 | SITE DEMOLITION PLAN - PHASE 4 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.1.1 | SITE PLAN - PHASE 1 - PART 1 | 2 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E4.1.2 | SITE PLAN PHASE 1 - PART 2 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.2.1 | SITE PLAN - PHASE 2 - PART 1 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E4.2.2 | SITE PLAN - PHASE 2 - PART 2 | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.3.1 | SITE PLAN - PHASE 3 - PART 1 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E4.3.2 | SITE PLAN - PHASE 3 - PART 2 | 3 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.4.1 | SITE PLAN - PHASE 4 - PART 1 | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E4.4.2 | SITE PLAN - PHASE 4 - PART 2 | 1 | 10/23/2020 | 10/26/2020 Addendum no. 2 |
| Electrical | E4.5.1 | SITE DETAILS | 2 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E4.5.2 | SITE DETAILS | 3 | 11/4/2020 | 11/9/2020 Addendum no. 5 |
| Electrical | E4.5.3 | SPORTS LIGHTING DETAILS | 1 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E5.0.1 | LIGHTNING PROTECTION DETAILS | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E5.0.2 | LIGHTNING PROTECTION DETAILS | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E6.0 | NORMAL POWER RISER DIAGRAM | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E6.0.1 | NORMAL SWITCHBOARD DETAILS AND SCHEDULES | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E6.1 | EMERGENCY POWER RISER DIAGRAM | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E6.1.1 | EMERGENCY SWITCHBOARD DETAILS AND SCHEDULES | 2 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| Electrical | E6.2 | PHOTOVOLTAICS RISER DIAGRAM | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Electrical | E6.2.1 | PHOTOVOLTAICS ONE-LINE DIAGRAM | 0 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Electrical | E6.3 | METERING RISER DIAGRAM AND DETAILS | 2 | 10/7/2020 | 10/6/2020 100% CD-Bid |
| Electrical | E6.4.1 | ELECTRICAL DETAILS 1 | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |



Consigli Construction

| | | | | | | |
|-------------------|---------|---|---|------------|------------|----------------|
| Electrical | E6.4.2 | ELECTRICAL DETAILS 2 | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E6.4.3 | GROUNDING DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E6.4.4 | FIRE STOP DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E6.4.5 | GENERAL DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E6.4.6 | GENERAL DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E6.5 | THEATER LIGHTING CONTROLS DIAGRAM | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E6.6 | PERFORMING ARTS LIGHTING CONTROLS DIAGRAM | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Electrical | E7.0 | ELECTRIC ROOM PART PLANS | 4 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Electrical | E7.1 | KITCHEN PART PLAN | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Electrical | E7.1.1 | KITCHEN EQUIPMENT POWER CONNECTION SCHEDULE | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | | | | | | |
| Fire Alarm | E8.0 | FIRE ALARM LEGEND | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.0a | FIRE ALARM FIRST FLOOR PLAN - PART A | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.0b | FIRE ALARM FIRST FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.0c | FIRE ALARM FIRST FLOOR PLAN - PART C | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.0.1 | FIRE ALARM DETAILS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E8.1a | FIRE ALARM UPPER FIRST FLOOR PLAN - PART A | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E8.2a | FIRE ALARM SECOND FLOOR PLAN - PART A | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.2b | FIRE ALARM SECOND FLOOR PLAN - PART B | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.2c | FIRE ALARM SECOND FLOOR PLAN - PART C | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.2d | FIRE ALARM SECOND FLOOR PLAN - PART D | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.2e | FIRE ALARM SECOND FLOOR PLAN - PART E | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.3a | FIRE ALARM THIRD FLOOR PLAN - PART A | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.3b | FIRE ALARM THIRD FLOOR PLAN - PART B | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.3d | FIRE ALARM THIRD FLOOR PLAN - PART D | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.3e | FIRE ALARM THIRD FLOOR PLAN - PART E | 4 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E8.4b | FIRE ALARM FOURTH FLOOR PLAN - PART D | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.4d | FIRE ALARM FOURTH FLOOR PLAN - PART D | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.4e | FIRE ALARM FOURTH FLOOR PLAN - PART E | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.5b | FIRE ALARM FIFTH FLOOR PLAN - PART B | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.5d | FIRE ALARM FIFTH FLOOR PLAN - PART D | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E8.6b | FIRE ALARM ROOF PLAN - PART B | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E8.6d | FIRE ALARM ROOF PLAN - PART D | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E8.7 | FIRE ALARM CATWALK PLANS | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E8.8 | FIRE ALARM RISER DIAGRAM | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Fire Alarm | E9.0 | ELECTRICAL STADIUM TOILET BUILDING PLAN | 3 | 11/4/2020 | 11/9/2020 | Addendum no. 5 |
| Fire Alarm | E10.0.1 | POWERED EQUIPMENT SCHEDULE | 2 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Fire Alarm | E10.0.2 | MECHANICAL EQUIPMENT SCHEDULE | 4 | 11/4/2020 | 11/4/2020 | Addendum no. 5 |
| Fire Alarm | E10.0.3 | MECHANICAL EQUIPMENT SCHEDULE 2 | 3 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Fire Alarm | E10.1.1 | PANEL SCHEDULES PART A EMERGENCY | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.1.2 | PANEL SCHEDULES PART A STANDBY | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.1.3 | PANEL SCHEDULES PART A MECHANICAL | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |

Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476



Consigli Construction

| | | | | | | |
|------------|---------|---------------------------------------|---|------------|------------|----------------|
| Fire Alarm | E10.1.4 | PANEL SCHEDULES PART A MECHANICAL 2 | 0 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Fire Alarm | E10.2.1 | PANEL SCHEDULES PART B 480V | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.2.2 | PANEL SCHEDULES PART B FLOOR 1 208V | 1 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Fire Alarm | E10.2.3 | PANEL SCHEDULES PART B 208V | 3 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Fire Alarm | E10.2.4 | PANEL SCHEDULES PART B EMERGENCY 480V | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Fire Alarm | E10.2.5 | PANEL SCHEDULES PART B EMERGENCY 208V | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.2.6 | PANEL SCHEDULES PART B KITCHEN | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.2.7 | PANEL SCHEDULES PART B MECHANICAL | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.2.8 | PANEL SCHEDULES PART B MECHANICAL | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.3.1 | PANEL SCHEDULES PART C STANDBY | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.3.2 | PANEL SCHEDULES PART C EMERGENCY | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.3.3 | PANEL SCHEDULES PART C MECHANICAL | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.1 | PANEL SCHEDULES PART D 480V | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.2 | PANEL SCHEDULES - PART D FLOOR 2 208V | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.3 | PANEL SCHEDULES PART D FLOOR 3 208V | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.4 | PANEL SCHEDULES PART D FLOOR 4 208V | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.5 | PANEL SCHEDULES PART D 5TH FLOOR 208V | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.6 | PANEL SCHEDULES PART D EMERGENCY | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.7 | PANEL SCHEDULES PART D MECHANICAL 1 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.4.8 | PANEL SCHEDULES PART D MECHANICAL 2 | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.1 | PANEL SCHEDULES PART E 480V | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.2 | PANEL SCHEDULES PART E 208V | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.3 | PANEL SCHEDULES PART E EMERGENCY | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.4 | PANEL SCHEDULES PART E STANDBY | 3 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.5 | PANEL SCHEDULES PART E MECHANICAL | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Fire Alarm | E10.5.6 | PANEL SCHEDULES PART E MECHANICAL 2 | 0 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |

Security & Communications

Technology

| | | | | | | |
|------------|--------|--|---|------------|------------|----------------|
| Technology | T0.01 | TELECOM - Legend | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Technology | T1.0.0 | TELECOM - Existing Fiber Site Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.0.1 | TELECOM - Existing Building Information & Demolition Phasing | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Technology | T1.1.1 | TELECOM - Phase 1 - First and Second Floor Plan | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Technology | T1.1.2 | TELECOM - Phase 1 - Third and Fourth Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.1.3 | TELECOM - Phase 1 - Fifth and Sixth Floor Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.2.1 | TELECOM - Phase 1a & 2 - First and Second Floor Plan | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Technology | T1.2.2 | TELECOM - Phase 1a & 2 - Third and Fourth Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.2.3 | TELECOM - Phase 1a & 2 - Fifth and Sixth Floor Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.2.4 | TELECOM - Phase 1a & 2 - Temp Spaces | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Technology | T1.3.1 | TELECOM - Phase 3 - First and Second Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.3.2 | TELECOM - Phase 3 - Third and Fourth Floor Plan | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.3.3 | TELECOM - Phase 3 - Fifth and Sixth Floor Plan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.4.1 | TELECOM - Phase 4 - First and Second Floor Plan | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |



Consigli Construction

| | | | | | | |
|-----------------|---------|--|---|------------|------------|----------------|
| Technology | T1.4.2 | TELECOM - Phase 4 - Third and Fourth Floor Plan | B | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T1.5 | TELECOM - New Building Fiber Site Plan | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Technology | T1.6.1 | TELECOM - Site Plan - Building | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T1.6.2 | TELECOM - Site Plan - Fields | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.0a | TELECOM - First Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.0b | TELECOM - First Floor Plan - Part b | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.0c | TELECOM - First & Upper First Floor Plan - Part c | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.1a | TELECOM - Upper First Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.1b | TELECOM - Upper First Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.2a | TELECOM - Second Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.2b | TELECOM - Second Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.2c | TELECOM - Second Floor Plan - Part c | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.2d | TELECOM - Second Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.2e | TELECOM - Second Floor Plan - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.3a | TELECOM - Third Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.3b | TELECOM - Third Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.3d | TELECOM - Third Floor Plan - Part d | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.3e | TELECOM - Third Floor Plan - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T2.4b | TELECOM - Fourth Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.4d | TELECOM - Fourth Floor Plan - Part d | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.5b | TELECOM - Fifth Floor Plan - Part b | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.5d | TELECOM - Fifth Floor Plan - Part d | 4 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.6b | TELECOM - Roof Plan - Part b | 2 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T2.6d | TELECOM - Roof Plan - Part d | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T3.01 | TELECOM - Data Room Layouts | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T3.02 | TELECOM - Data Room Layouts | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T4.01 | TELECOM - PA System Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T4.02 | TELECOM - PA System Keyplan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T4.03 | TELECOM - Speech Amplification Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Technology | T4.04 | TELECOM - Details | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T4.05 | TELECOM - TV & Wall Plates Details | 1 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T4.06 | TELECOM - ECS Details | 1 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| Technology | T5.01 | TELECOM - Riser Diagrams | 3 | 10/23/2020 | 10/26/2020 | Addendum no. 2 |
| Technology | T6.01 | TELECOM - Toilet Building | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | | | | | | |
| Security | SEC0.0 | SECURITY - Legend | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC1.0 | SECURITY - Site Camera Plan - Building | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC1.1 | SECURITY - Site Camera Plan - Fields | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.0a | SECURITY - First Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.0b | SECURITY - First Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.0c | SECURITY - First & Upper First Floor Plan - Part c | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.1b | SECURITY - Upper First Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |

Job #: 2153 Arlington High School
869 Massachusetts Avenue
Arlington, MA 02476



Consigli Construction

| | | | | | | |
|--------------------|---------|---|---|------------|------------|----------------|
| Security | SEC2.2a | SECURITY - Second Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.2b | SECURITY - Second Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.2c | SECURITY - Second Floor Plan - Part c | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.2d | SECURITY - Second Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.2e | SECURITY - Second Floor Plan - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.3b | SECURITY - Third Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.3d | SECURITY - Third Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.3e | SECURITY - Third Floor Plan - Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.4b | SECURITY - Fourth Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.4d | SECURITY - Fourth Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.5b | SECURITY - Fifth Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.5d | SECURITY - Fifth Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.6b | SECURITY - Roof Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC2.6d | SECURITY - Roof Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC3.01 | SECURITY - Door Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC3.02 | SECURITY - Security Alarm Keyplan | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC3.03 | SECURITY - One-Line Diagrams | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC4.01 | SECURITY - Equipment List | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Security | SEC5.01 | SECURITY - Toilet Building | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | | | | | | |
| Audiovisual | AV0.0 | TECH AV - Legend | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.0a | TECH AV - First Floor Plan - Part a | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.0b | TECH AV - First Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.0c | TECH AV - First & Upper First Floor Plan - Part c | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.1b | TECH AV - Upper First Floor Plan - Part b | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.2a | TECH AV - Second Floor Plan - Part a | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Audiovisual | AV2.2b | TECH AV - Second Floor Plan - Part b | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Audiovisual | AV2.2c | TECH AV - Second Floor Plan - Part c | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.2d | TECH AV - Second Floor Plan - Part d | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.3b | TECH AV - Third Floor Plan - Part b | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.3d | TECH AV - Third Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.3e | TECH AV - Third Floor Plan - Part e | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.4b | TECH AV - Fourth Floor Plan - Part b | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.4d | TECH AV - Fourth Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.5b | TECH AV - Fifth Floor Plan - Part b | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV2.5d | TECH AV - Fifth Floor Plan - Part d | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV3.01 | TECH AV - Equipment List & Narrative | 3 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Audiovisual | AV3.02 | TECH AV - TV Details | 1 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Audiovisual | AV3.03 | TECH AV - Projection Details | 1 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| Audiovisual | AV3.04 | TECH AV - School Committee Room Details | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | | | | | | |
| Theatrical | TA0 | Audiovisual Keys and Notes | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | | |
|----------------|----------|---|---|-----------|-----------|----------------|
| Theatrical | TA0.1 | Audiovisual Conduit Risers | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA0.2 | Audiovisual Device Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA2.2e | Audiovisual Equipment Plan - Second Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA2.3e | Audiovisual Equipment Plan - Third Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA2.4e | Audiovisual Device Plan - Fourth Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA3.1.1 | Audiovisual Elevations and Sections | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA3.1.2 | Audiovisual Elevations and Sections - Auditorium | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.0 | Audiovisual Diagram Key and Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.1 | Audiovisual Functional Diagram | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.2 | Audiovisual Functional Diagram | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.3 | Audiovisual Functional Diagram | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.4 | Audiovisual Functional Diagram | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA4.1.5 | Audiovisual Functional Diagram | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA6.1.1 | Audiovisual Plate and Panel Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA6.1.2 | Audiovisual Plate and Panel Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA6.2.1 | Audiovisual Equipment Rack Elevations | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TA10.1.1 | Enlarged Plans and Sections | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TF1 | Fall Restraint | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL2.2e | Theatrical Lighting Device Plan - Second Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL2.3e | Theatrical Lighting Device Plan - Third Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL2.4e | Theatrical Lighting Device Plan - Fourth & Fifth Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL4.1.1 | Riser Diagram - Auditorium | 3 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| Theatrical | TL4.1.2 | Riser Diagram - Performing Arts Classroom | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL4.2.1 | Schedules - Auditorium | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL4.2.2 | Schedules - Performing Arts Classroom | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL6.1.1 | Theatrical Lighting Plate and Panel Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL6.2.2 | Theatrical Lighting Plate and Panel Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TL6.2.3 | Theatrical Lighting Mounting Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TP2.2e | Theatrical Platforms Plans | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR0 | Theatrical Rigging | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR2.2e | Theatrical Rigging Plan - Second Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR2.3e | Theatrical Rigging Plan - Third Floor Part e | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR3.1.1 | Theatrical Rigging Sections | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR4.1.1 | Theatrical Rigging Details | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Theatrical | TR10.1.1 | Enlarged Plans | 2 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | | | | | | |
| Signage | GS01.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS02.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS03.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS04.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS05.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS06.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |



Consigli Construction

| | | | | | | |
|-----------------------------|--------|---------------------------------|---|-----------|-----------|----------------|
| Signage | GS07.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS08.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS09.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS10.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS11.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS12.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Signage | GS13.0 | Graphics/Signs | 0 | 10/7/2020 | 10/6/2020 | 100% CD-Bid |
| Existing Conditions | | | | | | |
| Civil Transportation | | | | | | |
| Civil Transportation | CT1.1 | MILL STREET CONSTRUCTION PLAN | 0 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Civil Transportation | CT1.2 | MILL STREET TRAFFIC SIGNAL PLAN | 0 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Civil Transportation | CT1.3 | TRAFFIC DETAILS | 0 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Civil Transportation | CT1.4 | MILL STREET SIGN SUMMARY | 0 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |
| Civil Transportation | CT1.5 | TRAFFIC MANAGEMENT PLAN | 0 | 11/2/2020 | 11/3/2020 | Addendum no. 4 |



Consigli Construction

Current Specifications

| Division | Number | Description | Revision | Issued Date | Received Date | Set |
|---|--------|---|----------|-------------|---------------|----------------|
| Procurement And Contracting Requirements | | | | | | |
| 00 - Procurement and Contracting Requirements | 000100 | Cover Page - Volume 1 of 3 | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 000100 | Cover Page - Volume 2 of 3 | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 000100 | Cover Page - Volume 3 of 3 | 2 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 000105 | List of Consultants | 8 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 000107 | Professional Seals | 6 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 000110 | Table of Contents | 6 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| 00 - Procurement and Contracting Requirements | 001116 | Invitation to Bid | 5 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 001153 | List of Prequalified Trade Contractors | 5 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| 00 - Procurement and Contracting Requirements | 002216 | Instructions to Bidders | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 003116 | Project and Trade Contract Budgets | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 003150 | Tax Exemption | 5 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004113 | Trade Contractor Bid Form | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004313 | Bid Security Form | 5 | 10/16/2020 | 10/19/2020 | Addendum no. 1 |
| 00 - Procurement and Contracting Requirements | 004511 | DCAMM Update Statement | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004519 | Non-Collusion Affidavit | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004520 | Affidavit of Compliance with State Secretary | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004521 | Affidavit of Prequalified Subtrade Subcontractors | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004522 | Affidavit of Prevailing Wage Rate Compliance | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004533 | Certificate of Vote of Authorization | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004536 | Affidavit of Tax Compliance | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 004546 | Certifications | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 005213 | Form of Trade Subcontract | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 005223 | Owner-CM Agreement | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 006113 | Performance Bond | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 006116 | Payment Bond | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 007223 | General Conditions of the Contract for Construction | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 007225 | CM Supplemental Instructions to Bidders | 8 | 11/5/2020 | 11/9/2020 | Addendum no. 5 |
| 00 - Procurement and Contracting Requirements | 007336 | MBE and WBE Participation | 3 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 007337 | Equal Employment Opportunity Utilization Reporting | 2 | 10/28/2020 | 10/29/2020 | Addendum no. 3 |
| 00 - Procurement and Contracting Requirements | 007346 | Prevailing Wage Rates | 5 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 007373 | Statutory Requirements | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 00 - Procurement and Contracting Requirements | 008100 | Available Project Information | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| General Requirements | | | | | | |
| 01 - General Requirements | 011100 | Summary of Work | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |
| 01 - General Requirements | 011400 | Work Restrictions | 4 | 10/7/2020 | 10/6/2020 | 100% CDs-Bid |



Consigli Construction

| | | | | | |
|---------------------------|---------|---|---|------------|---------------------------|
| 01 - General Requirements | 011401 | Electronic Release Form | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 012201 | Unit Price Proposal Sheet | 5 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 012300 | Alternates | 1 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 012400 | Schedule of Values | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 01 - General Requirements | 013100 | Project Management and Coordination | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 013119 | Project Meetings | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 013200 | Construction Progress Documentation | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 013300 | Submittal Procedures | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 013301 | Substitution / or Equal Request Form | 6 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 013543 | Environmental Procedures | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 014000 | Quality Requirements | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 014001 | Program of Structural Testing and Inspections | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 014001a | Arlington HS-FBRA Statement of Special Instructions | 0 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 015000 | Temporary Facilities and Controls | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 017329 | Cutting and Patching | 0 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 017400 | Cleaning and Waste Management | 6 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 017700 | Closeout Procedures | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 017839 | Project Record Documents | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 018100 | General Building Commissioning Requirements | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 01 - General Requirements | 018110 | Sustainable Design Requirements | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 01 - General Requirements | 018111 | Sustainable Design Reference Documents | 5 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 018119 | Indoor Air Quality Management Plan | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 01 - General Requirements | 019115 | Building Exterior Commissioning | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |

Existing Conditions

| | | | | | |
|--------------------------|---------|--------------------------------|---|-----------|------------------------|
| 02 - Existing Conditions | 024113 | Utility Line Removal | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 02 - Existing Conditions | 024119 | Demolition | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 02 - Existing Conditions | 024120 | Salvaging | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 02 - Existing Conditions | 024120a | Salvaging (a) | 0 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 02 - Existing Conditions | 025620 | Replacement Engineered Barrier | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |

Concrete

| | | | | | |
|---------------|--------|--------------------------------|---|------------|---------------------------|
| 03 - Concrete | 033000 | Cast-in-Place Concrete | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 03 - Concrete | 033300 | Architectural Concrete | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 03 - Concrete | 033650 | Concrete Finishes | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 03 - Concrete | 034500 | Precast Architectural Concrete | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 03 - Concrete | 034501 | Precast Concrete for Landscape | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |

Masonry

| | | | | | |
|--------------|--------|-------------------------------|---|-----------|--------------------------|
| 04 - Masonry | 040001 | Masonry Work | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 04 - Masonry | 042000 | Unit Masonry | 5 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| 04 - Masonry | 044213 | Stone Masonry for Landscaping | 0 | 10/7/2020 | 10/6/2020 100% CDs-Bid |



Consigli Construction

| Metals | | | | | |
|--|--------|--|---|------------|---------------------------|
| 05 - Metals | 050001 | Miscellaneous and Ornamental Iron | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 05 - Metals | 051200 | Structural Steel Framing | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 051226 | Shear Connectors | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 052100 | Steel Joist Framing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 053100 | Steel Decking | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 054000 | Cold-Formed Metal Framing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 055000 | Metal Fabrications | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 05 - Metals | 057300 | Decorative Glass Railings | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 05 - Metals | 057500 | Decorative Formed Metal | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| Wood, Plastics, and Composites | | | | | |
| 06 - Wood, Plastics, and Composites | 061000 | Rough Carpentry | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 06 - Wood, Plastics, and Composites | 061600 | Sheathing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 06 - Wood, Plastics, and Composites | 064020 | Interior Architectural Woodwork | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 06 - Wood, Plastics, and Composites | 066400 | FRP Paneling | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| Thermal and Moisture Protection | | | | | |
| 07 - Thermal and Moisture Protection | 070001 | Waterproofing, Dampproofing and Caulking | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 070002 | Roofing and Flashing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 071100 | Bituminous Dampproofing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 071400 | Self-Adhering Sheet Waterproofing | 3 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 07 - Thermal and Moisture Protection | 071610 | Crystalline Waterproofing | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 07 - Thermal and Moisture Protection | 072100 | Thermal Insulation | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 072500 | Air Barriers | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 074200 | Metal Wall Panels | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 074210 | Wall Cladding Support System | 3 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| 07 - Thermal and Moisture Protection | 074249 | Sintered Stone Wall Cladding System | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 075400 | Thermoplastic Membrane Roofing | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 07 - Thermal and Moisture Protection | 075510 | Fluid-Applied Membrane Roofing | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 07 - Thermal and Moisture Protection | 076200 | Sheet Metal Flashing and Trim | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 07 - Thermal and Moisture Protection | 077200 | Roof Accessories | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 07 - Thermal and Moisture Protection | 078100 | Applied Fireproofing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 078400 | Firestopping | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 07 - Thermal and Moisture Protection | 079200 | Joint Sealants | 6 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 07 - Thermal and Moisture Protection | 079500 | Expansion Control | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| Openings | | | | | |
| 08 - Openings | 080001 | Metal Windows | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 080002 | Glass and Glazing | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 081110 | Hollow Metal Frames | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 081400 | Flush Wood Doors | 5 | 10/16/2020 | 10/19/2020 Addendum no. 1 |



Consigli Construction

| | | | | | |
|---------------|--------|---|---|------------|---------------------------|
| 08 - Openings | 083100 | Access Doors and Frames | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083300 | Overhead Coiling Doors | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083320 | Overhead Coiling Grilles | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083325 | Fire Shutters | 1 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083336 | Side Coiling Grilles | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083510 | Horizontal-Sliding Accordion Fire Doors | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 083513 | Folding Doors | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 08 - Openings | 084220 | All-Glass Partitions | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 084410 | Glazed Aluminum Curtain Walls | 4 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 08 - Openings | 084523 | Fiberglass-Sandwich-Panel Assemblies | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 08 - Openings | 085110 | Aluminum Windows | 4 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 08 - Openings | 086200 | Unit Skylights | 3 | 10/16/2020 | 10/19/2020 Addendum no. 1 |
| 08 - Openings | 086300 | Modular Skylights | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 08 - Openings | 087100 | Door Hardware | 6 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 08 - Openings | 088000 | Glazing | 5 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 08 - Openings | 089000 | Louvers and Vents | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |

Finishes

| | | | | | |
|---------------|--------|-----------------------------|---|------------|---------------------------|
| 09 - Finishes | 090002 | Tile | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 09 - Finishes | 090003 | Acoustical Tile | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 090005 | Resilient Floors | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 090006 | Terrazzo | 1 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 090007 | Painting | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 090160 | Vapor Mitigation at Slabs | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 09 - Finishes | 092900 | Gypsum Board Assemblies | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 09 - Finishes | 093000 | Tiling | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 09 - Finishes | 095100 | Acoustical Panel Ceilings | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 09 - Finishes | 096400 | Stage Wood Flooring | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 096466 | Wood Athletic Flooring | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 096500 | Resilient Flooring | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 09 - Finishes | 096566 | Resilient Athletic Flooring | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 096600 | Terrazzo Flooring | 4 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| 09 - Finishes | 096625 | Precast Terrazzo | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 096700 | Fluid-Applied Flooring | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 096820 | Carpeting | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 098120 | Sprayed Acoustic Insulation | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 09 - Finishes | 098400 | Acoustic Room Components | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 09 - Finishes | 099000 | Painting and Coating | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |

Specialties

| | | | | | |
|------------------|--------|-------------------------|---|-----------|------------------------|
| 10 - Specialties | 101100 | Visual Display Surfaces | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
|------------------|--------|-------------------------|---|-----------|------------------------|



Consigli Construction

| | | | | | |
|------------------|--------|----------------------------------|---|------------|---------------------------|
| 10 - Specialties | 101400 | Signage | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 10 - Specialties | 101453 | Traffic Signage | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 10 - Specialties | 101500 | Photoluminescent Safety Products | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 10 - Specialties | 102100 | Toilet Compartments and Cubicles | 5 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 10 - Specialties | 102220 | Operable Partitions | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 10 - Specialties | 102800 | Toilet Accessories | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 10 - Specialties | 104400 | Fire Protection Specialties | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 10 - Specialties | 105100 | Lockers | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |

Equipment

| | | | | | |
|----------------|--------|---|---|------------|---------------------------|
| 11 - Equipment | 110140 | Tieback and Lifeline Anchors | 3 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 11 - Equipment | 110610 | Stage Rigging and Curtains | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 110680 | Portable Platforms | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 110700 | Monumental Clock System | 1 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 111300 | Loading Dock Equipment | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 112400 | Auditorium Fall Restraint | 1 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 114000 | Food Service Equipment | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 114500 | Residential Appliances | 3 | 10/23/2020 | 10/24/2020 Addendum no. 2 |
| 11 - Equipment | 114843 | Athletic Fields Scoreboard | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 115210 | Projection Screens | 5 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 11 - Equipment | 115213 | Projection Screens - Performance Spaces | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 116620 | Athletic Equipment | 4 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 11 - Equipment | 116813 | Playground Equipment | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 116832 | Track and Field Equipment | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 116833 | Athletic Fields Equipment | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 11 - Equipment | 116850 | Skin Infield and Mound Clay | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |

Furnishings

| | | | | | |
|------------------|--------|--------------------------------|---|-----------|--------------------------|
| 12 - Furnishings | 122110 | Horizontal Louver Miniblinds | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 12 - Furnishings | 122400 | Shades | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 12 - Furnishings | 123000 | Manufactured Casework | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 12 - Furnishings | 124810 | Entrance Floor Mats and Frames | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 12 - Furnishings | 126100 | Fixed Audience Seating | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 12 - Furnishings | 126600 | Telescoping Stands | 3 | 11/5/2020 | 11/9/2020 Addendum no. 5 |

Conveying Equipment

| | | | | | |
|--------------------------|--------|------------------|---|------------|---------------------------|
| 14 - Conveying Equipment | 144200 | Wheelchair Lifts | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
|--------------------------|--------|------------------|---|------------|---------------------------|

Fire Suppression

| | | | | | |
|-----------------------|--------|-----------------|---|-----------|--------------------------|
| 21 - Fire Suppression | 210000 | Fire Protection | 5 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
|-----------------------|--------|-----------------|---|-----------|--------------------------|

Plumbing

| | | | | | |
|---------------|--------|----------|---|------------|---------------------------|
| 22 - Plumbing | 220000 | Plumbing | 7 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
|---------------|--------|----------|---|------------|---------------------------|

HVAC



Consigli Construction

| | | | | | |
|---------------------------------------|--------|--|----|------------|---------------------------|
| 23 - HVAC | 230000 | Heating, Ventilating, and Air Conditioning (HVAC) | 10 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Electrical | | | | | |
| 26 - Electrical | 260000 | Electrical | 10 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| 26 - Electrical | 265000 | Theatrical Lighting Controls and Fixtures | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Communications | | | | | |
| 27 - Communications | 271000 | Structured Cabling | 4 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 27 - Communications | 274100 | Audiovisual Systems | 3 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 27 - Communications | 274116 | Integrated Audiovisual Systems and Equipment | 3 | 11/5/2020 | 11/9/2020 Addendum no. 5 |
| Electronic Safety and Security | | | | | |
| 28 - Electronic Safety and Security | 281000 | Electronic Security Systems | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| Earthwork | | | | | |
| 31 - Earthwork | 311000 | Site Clearing | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 312000 | Earthwork | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 312001 | Management and Disposition of Excavated Material | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 312115 | Sub-Slab Ventilation System | 5 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 31 - Earthwork | 312319 | Dewatering | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 312500 | Erosion and Sedimentation Controls | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 315000 | Temporary Excavation Support and Protection | 4 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 316213 | Pressure-Injected Footings (PIFs) | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 31 - Earthwork | 316615 | Helical Piles | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| Exterior Improvements | | | | | |
| 32 - Exterior Improvements | 321213 | Heavy Duty Concrete Paving | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 321216 | Asphalt Paving | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 321313 | Concrete Paving | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 321413 | Precast Concrete Unit Paving for Landscape | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 321416 | Brick Unit Paving | 2 | 11/5/2020 | 11/9/2020 Addendum no. 6 |
| 32 - Exterior Improvements | 321600 | Granite Curb Stockpiles | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 321613 | Granite Curb | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 321723 | Pavement Markings | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 321816 | Playground Protective Surfacing | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 321825 | Synthetic Field Sport Surfacing | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 321843 | Synthetic Landscape Amphitheater Surfacing | 1 | 11/2/2020 | 11/3/2020 Addendum no. 4 |
| 32 - Exterior Improvements | 323100 | Steel Picket Fence & Gates and Aluminum Screen | 2 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 323113 | Chain Link Fences and Gates | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 323114 | Athletic Fields Chain Link Fence, Gates, and Backstops | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 323200 | Segmental Retaining Walls | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 323216 | Precast Modular Block Gravity Retaining Wall | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 323300 | Site Furnishings | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 328400 | Irrigation System | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |



Consigli Construction

| | | | | | |
|----------------------------|--------|---|---|------------|---------------------------|
| 32 - Exterior Improvements | 329100 | Planting Soils | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 32 - Exterior Improvements | 329200 | Turf and Grasses | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 329300 | Plants | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 32 - Exterior Improvements | 329419 | Grass Paver | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 33 - Utilities | 330500 | Athletic Fields Buried Pipe Installation | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 331000 | Water Utilities | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 333000 | Sanitary Sewerage | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334000 | Stormwater Utilities | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334010 | Athletic Fields Polyvinyl Chloride Pipe | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334020 | Athletic Fields High Density Polyethylene Pipe | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334420 | Athletic Fields Trench Drain | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334436 | Oil and Stormwater Separators | 3 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 33 - Utilities | 334623 | Synthetic Turf Sport Field Drainage and Anchor System | 3 | 10/28/2020 | 10/29/2020 Addendum no. 3 |
| 33 - Utilities | 334926 | Athletic Fields Premolded Polyvinyl Chloride Drainage | 2 | 10/7/2020 | 10/6/2020 100% CDs-Bid |
| 34 - Transportation | 344113 | Traffic Signals | 0 | 11/2/2020 | 11/3/2020 Addendum no. 4 |








CONSIGLI
Est. 1905

7. SCHEDULE

| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish | 2019 | 2020 | | | | 2021 | | | | 2022 | | | | 2023 | | | | 2024 | | | | 2025 | | | | 2026 | | | | 2027 |
|---|--|----------|---------|-------|-------------|------|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|
| | | | | | | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 |
| Arlington High School Project | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Milestones | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A1090 | Notice to Proceed - Preconstruction | | 0d | 0d | 26-Jun-19 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A6950 | Start Enabling Work | | 0d | 0d | 23-Apr-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A10160 | Complete EBP #3: Enabling Existing HS [08/28/20] | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A1730 | Issue Final Construction Documents | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A10170 | Complete Phase 1: Substantial Completion & TCO [02-14-22] | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A41930 | Complete Phase 2: Substantial Completion & TCO [09-19-23] | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A41940 | Complete Phase 3: Substantial Completion & TCO [09-18-24] | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A6930 | Project Completion | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A41950 | Complete Phase 4: Full Use of Fields [04-25-25] | | 0d | 0d | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Construction Summary | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7800 | Phase 1 Utility Relocation / RAPS | | 155d | 2d | 10-Aug-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7810 | Phase 1 Building | | 354d | 309d | 31-Aug-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7830 | Phase 2 Abatement / Demo | | 90d | 90d | 14-Feb-22 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7840 | Phase 2 Building | | 336d | 336d | 18-May-22 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7850 | Phase 3 Abatement / Demo | | 50d | 50d | 03-Jul-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7860 | Phase 3 Building | | 250d | 250d | 20-Sep-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7870 | Phase 4 Abatement / Demo | | 60d | 60d | 25-Jun-24 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A7880 | Phase 4 Site Development | | 208d | 208d | 25-Jun-24 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Schedule Impacts | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| RFI #03 EBP#2 Confirmation of Ground Improvement Design | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43150 | FBRA issued clarifications to items requested during PreOp (became RFI #3) | | 0d | 0d | 05-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43160 | Meeting held to talk through required information. HMFH Issues response to RFI #3 based on i | | 0d | 0d | 19-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43170 | Follow-up Call Held - Additional Structural Information Required | | 0d | 0d | 26-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| RFI #04 on New 8" Domestic Water Location | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43140 | RFI 04 - New 8" Domestic Water Location | | 5d | 0d | 19-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A44510 | Issue CCD#2 | | 0d | 0d | 15-Jun-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A44520 | Price CCD#2 | | 5d | 0d | 15-Jun-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A44530 | Approve Pricing CCD#2 | | 5d | 0d | 22-Jul-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Unforeseen Transite Pipe | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43850 | Transite Pipe Discovered | | 0d | 0d | 21-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A43860 | 10 Day Notification for Abatement | | 10d | 0d | 25-May-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Surplus Topsoil | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46260 | Notify Design Team/ Owner | | 0d | 0d | 03-Jun-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46270 | RFI #9 - Surplus Topsoil | | 5d | 0d | 05-Jun-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46280 | McPhail Performed Hazardous Soil Testing | | 5d | 0d | 09-Jul-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46290 | Issued Unlined Landfill Profile Documentation | | 5d | 0d | 29-Jul-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Eversource Duct Bank | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46630 | Eversource Duct Bank (Waiting for Eversource to perform work) | | 10d | 4d | 04-Aug-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46650 | Eversource internal energize permit (DELAY) | | 30d | 0d | 12-Oct-20 A | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| A46640 | Eversource Tying into Vault/ Installing Cable | | 1d | 1d | 20-Nov-20 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Owner Moves | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Start Date 24-May-19
Finish Date 27-Apr-25
Data Date 17-Nov-20
Run Date 23-Nov-20 10:06

© Primavera Systems, Inc.

 Remaining Level of Effort ◆ ◆ Milestone
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work

Consigli Construction Co., Inc.
Arlington High School Project
Project Schedule - Updated 17-Nov-20




| 2153-GMP - Arlington High School Project | | | | | | * Distribution Schedule TASK filter: All Activities | | | | | | | | | | | | | | | | | | | | Page 36 of 48 | | | | | | | | | | |
|--|--|---|---------|-----------|-----------|---|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|----|----|------|----|---------------|----|------|----|----|----|------|----|----|----|------|
| Activity ID | Activity Name | Orig Dur | Rem Dur | Start | Finish | 2019 | | 2020 | | | | 2021 | | | | 2022 | | | | 2023 | | | | 2024 | | | | 2025 | | | | 2026 | | | | 2027 |
| | | | | | | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | |
| C.03.GB2.1840 | Install Metal Stud Wal Framing - [L3; Gang Bathrooms] | 2d | 2d | 15-Dec-22 | 16-Dec-22 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Top Off GWB Walls - [L3; Gang Bathrooms] | 6d | 6d | 19-Dec-22 | 27-Dec-22 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Install GWB, Tape & Sand - Walls - [L3; Gang Bathrooms] | 20d | 20d | 27-Jan-23 | 24-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Prime Paint - Walls - [L3; Gang Bathrooms] | 7d | 7d | 27-Feb-23 | 07-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Finish MEP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.1960 | Install Radiant Panels - [L3; Gang Bathrooms] | 3d | 3d | 17-Mar-23 | 21-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.1980 | Install Ceiling Lights, RGD's, Heads - [L3; Gang Bathrooms] | 5d | 5d | 17-Mar-23 | 23-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.1990 | Complete Overhead MEP + 3rd Party Inspection - [L3; Gang Bathrooms] | 4d | 4d | 24-Mar-23 | 29-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.2030 | Install Plumbing Fixtures & Accessories - [L3; Gang Bathrooms] | 7d | 7d | 13-Apr-23 | 24-Apr-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.2010 | Install Mech/Elec/Plumb/FP Trim - [L3; Gang Bathrooms] | 7d | 7d | 25-Apr-23 | 03-May-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Finish Architectural | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.SC.1740 | Install Acoustical Clg Grid - [L3; Gang Bathrooms] | 7d | 7d | 08-Mar-23 | 16-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.SC.1750 | Install Ceiling Tile - [L3; Gang Bathrooms] | 5d | 5d | 30-Mar-23 | 05-Apr-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.2020 | Install Ceramic Tile Floors & Walls - [L3; Gang Bathrooms] | 10d | 10d | 30-Mar-23 | 12-Apr-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.2040 | Install Toilet Partitions & Accessories - [L3; Gang Bathrooms] | 5d | 5d | 13-Apr-23 | 20-Apr-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.2000 | Finish Paint - [L3; Gang Bathrooms] | 6d | 6d | 13-Apr-23 | 21-Apr-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.1940 | Final Clean - [L3; Gang Bathrooms] | 5d | 5d | 04-May-23 | 10-May-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | C.03.GB2.1950 | Complete Punch List - [L3; Gang Bathrooms] | 5d | 5d | 28-Jun-23 | 05-Jul-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Level 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| | Electric Rooms | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.ELC.1300 | Pour Equipment Pads - [L2: Elec] | 7d | 7d | 04-Jan-23 | 12-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.ELC.1330 | Install GWB / Plywood & Painting - Walls - [L2: Elec] | 7d | 7d | 04-Jan-23 | 12-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.ELC.1310 | Set Transformers - [L2: Elec] | 2d | 2d | 13-Jan-23 | 17-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.ELC.1320 | Install Distribution Panels - [L2: Elec] | 5d | 5d | 18-Jan-23 | 24-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Classrooms | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Rough MEP | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2870 | Install AV/Tel-Data/Security Rough-in - [L2; Classrooms] | 25d | 25d | 15-Dec-22 | 23-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2910 | Install Controls Wiring Rough - [L2; Classrooms] | 20d | 20d | 16-Dec-22 | 17-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2800 | Install Duct Mains, Branches & Equip - [L2; Classrooms] | 15d | 15d | 05-Jan-23 | 26-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2850 | Install Overhead Plumbing - Sanitary - [L2; Classrooms] | 15d | 15d | 05-Jan-23 | 26-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2860 | Install Overhead Plumbing Piping - [L2; Classrooms] | 15d | 15d | 05-Jan-23 | 26-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2830 | Install Fire Protection Mains & Branches - [L2; Classrooms] | 15d | 15d | 12-Jan-23 | 02-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2840 | Install HVAC Piping - [L2; Classrooms] | 30d | 30d | 12-Jan-23 | 24-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2810 | Install Overhead Power Distribution - [L2; Classrooms] | 15d | 15d | 20-Jan-23 | 09-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2940 | Install Electrical Wall Rough-in - [L2; Classrooms] | 15d | 15d | 25-Jan-23 | 14-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2900 | Install Insulation - Plumbing - [L2; Classrooms] | 7d | 7d | 27-Jan-23 | 06-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2880 | Install Insulation - Ductwork - [L2; Classrooms] | 10d | 10d | 27-Jan-23 | 09-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2950 | Install Plumbing Wall Rough-in - [L2; Classrooms] | 10d | 10d | 27-Jan-23 | 09-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2820 | Install Overhead Power/Light/Fire Alarm Circuits - [L2; Classrooms] | 10d | 10d | 10-Feb-23 | 24-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.3200 | Complete In-Wall MEP Inspection - Hard Ceiling - [L2; Classrooms] | 3d | 3d | 15-Feb-23 | 17-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2920 | Complete Overhead MEP + 3rd Party Inspection - Acoustic Ceiling - [L2; Classrooms] | 4d | 4d | 27-Feb-23 | 02-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2890 | Install Insulation - HVAC Piping - [L2; Classrooms] | 10d | 10d | 27-Feb-23 | 10-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.3140 | Complete Overhead MEP + 3rd Party Inspection - Hard Ceiling - [L2; Classrooms] | 4d | 4d | 06-Mar-23 | 09-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Rough Architectural | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2790 | Install Metal Stud Wal Framing - [L2; Classrooms] | 7d | 7d | 30-Dec-22 | 10-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.3120 | Top Off GWB Walls - [L2; Classrooms] | 6d | 6d | 05-Jan-23 | 12-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2930 | Frame Soffits - [L2; Classrooms] | 5d | 5d | 13-Jan-23 | 20-Jan-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2980 | Install GWB, Tape & Sand - Soffits - [L2; Classrooms] | 10d | 10d | 23-Jan-23 | 03-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2960 | Frame Hard Ceilings - [L2; Classrooms] | 5d | 5d | 10-Feb-23 | 16-Feb-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| C.02.CLS.2970 | Install GWB, Tape & Sand - Walls - [L2; Classrooms] | 20d | 20d | 21-Feb-23 | 20-Mar-23 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

8. LOGISTICS

Arlington High School




Phase 1
February 2022 Completion

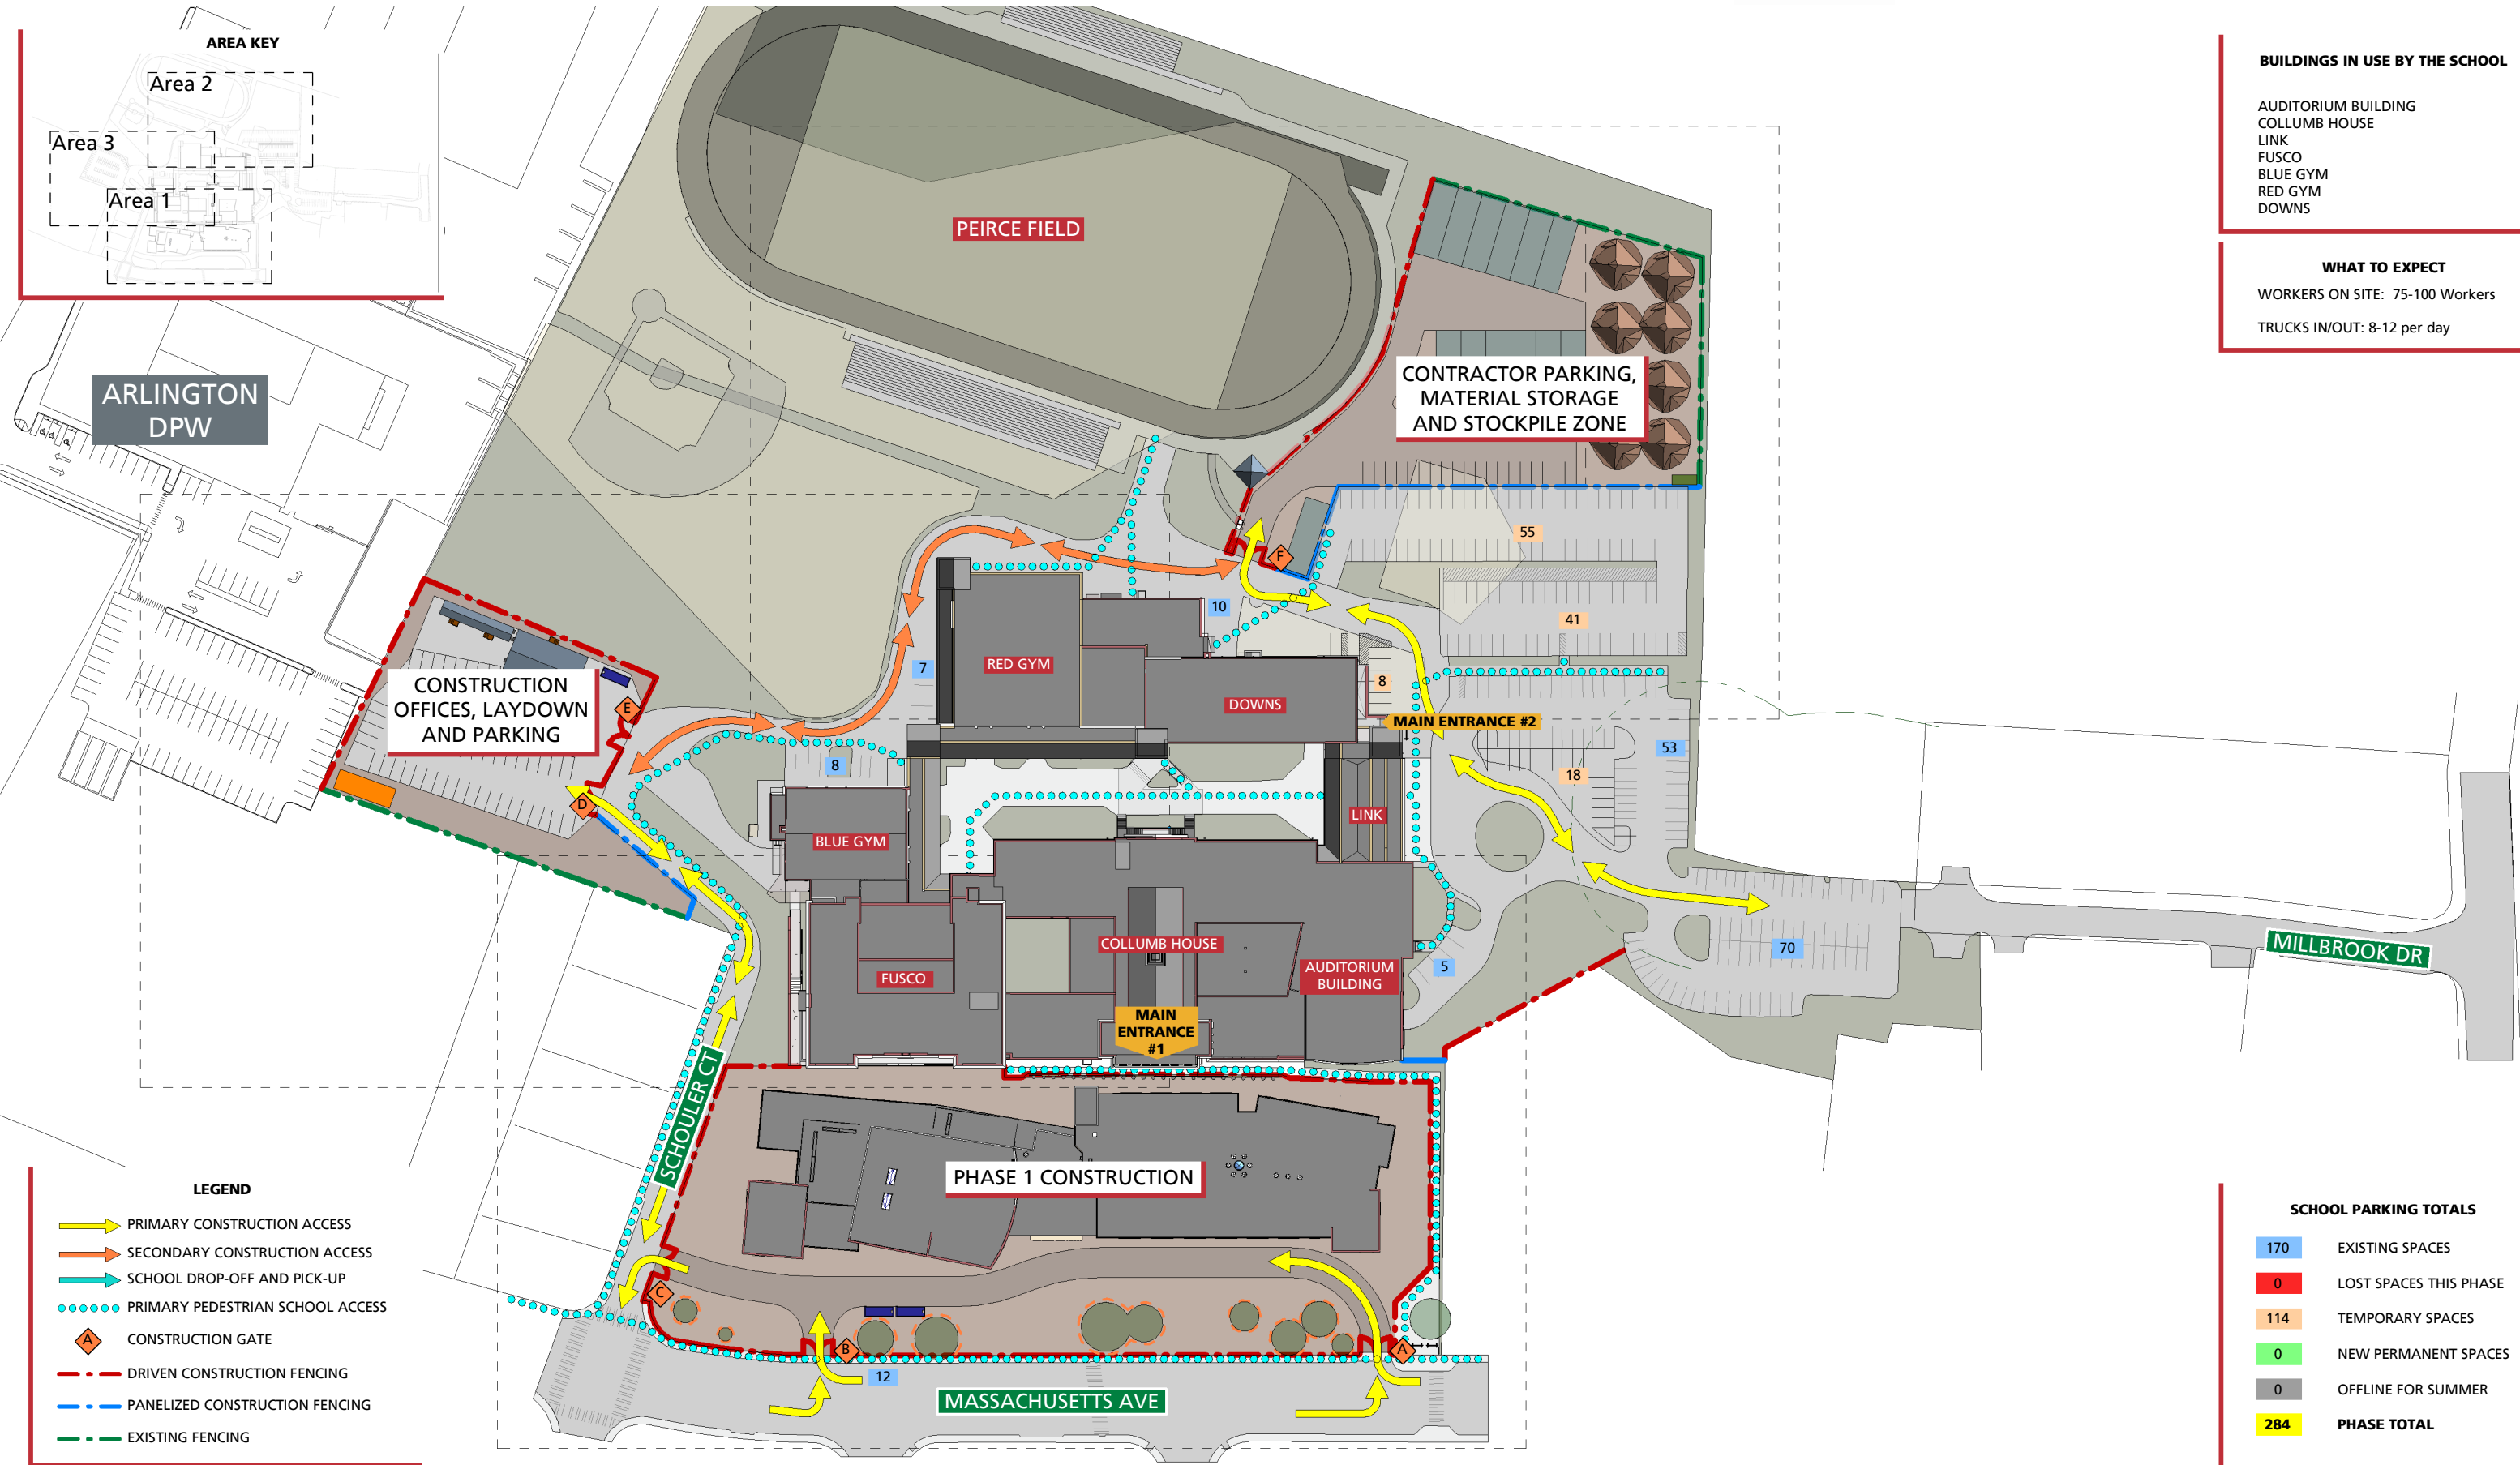


Arlington High School



Phase 1
Enlarged Plan - Area 1

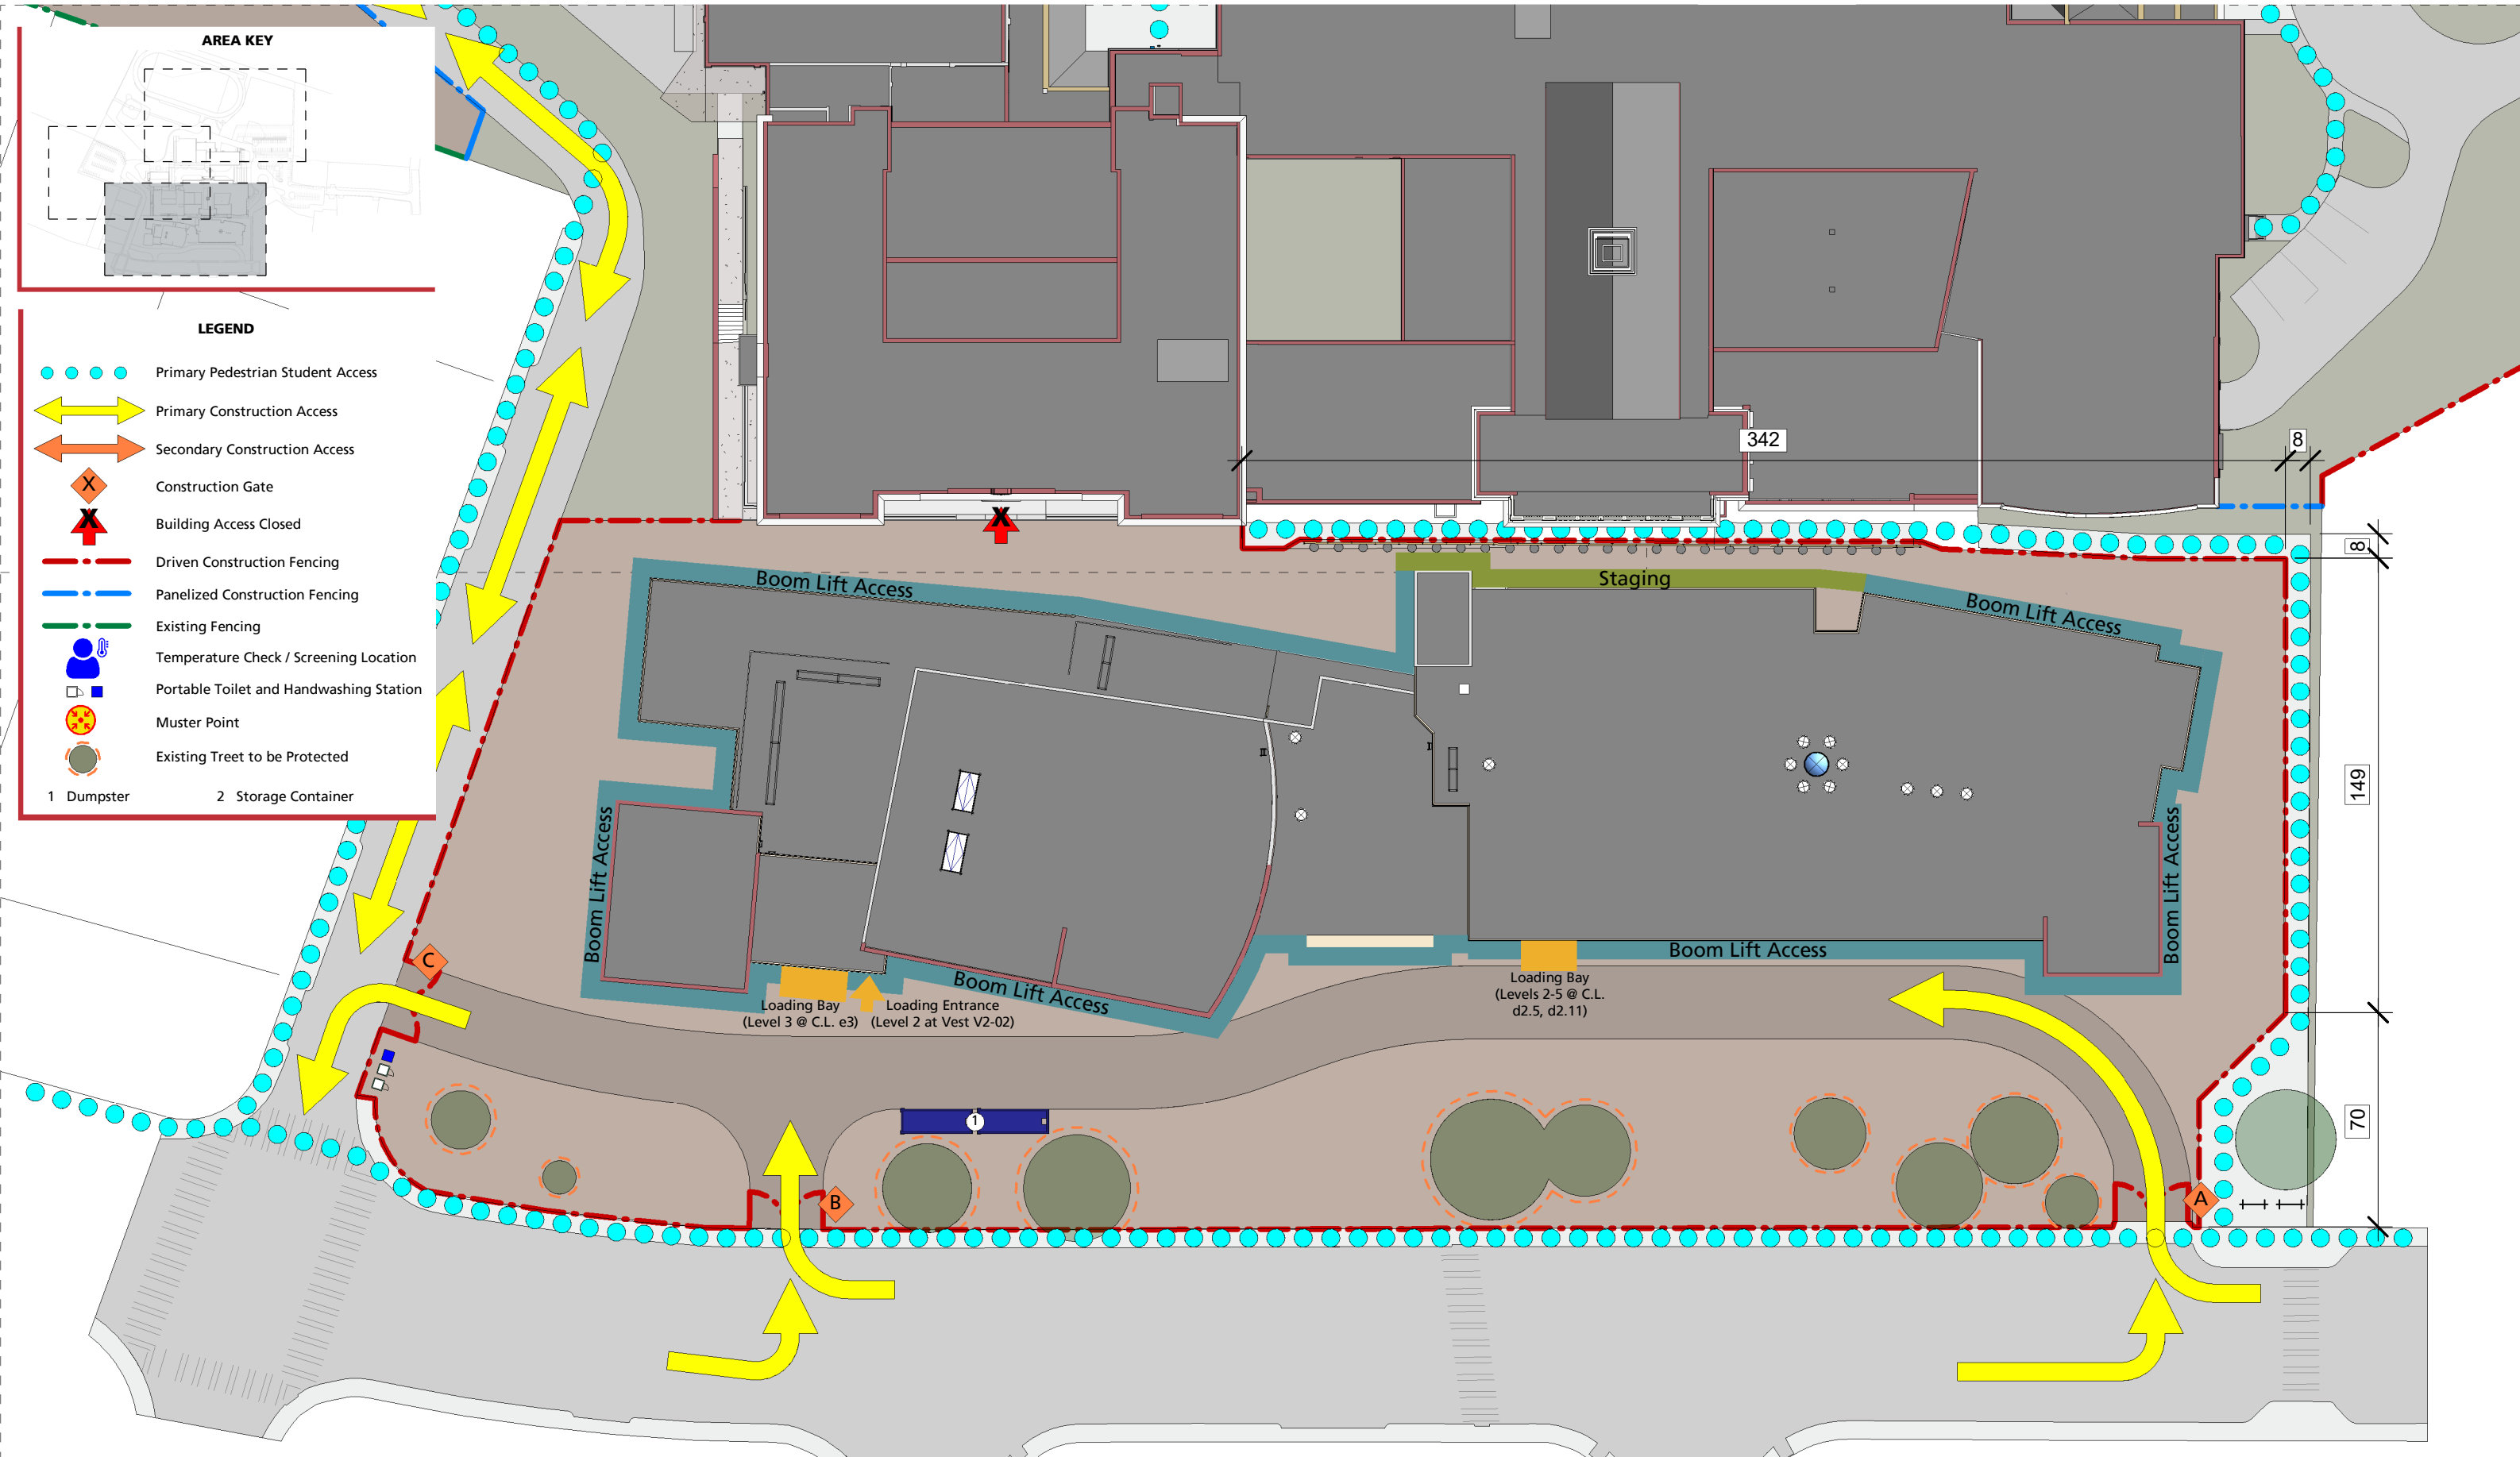


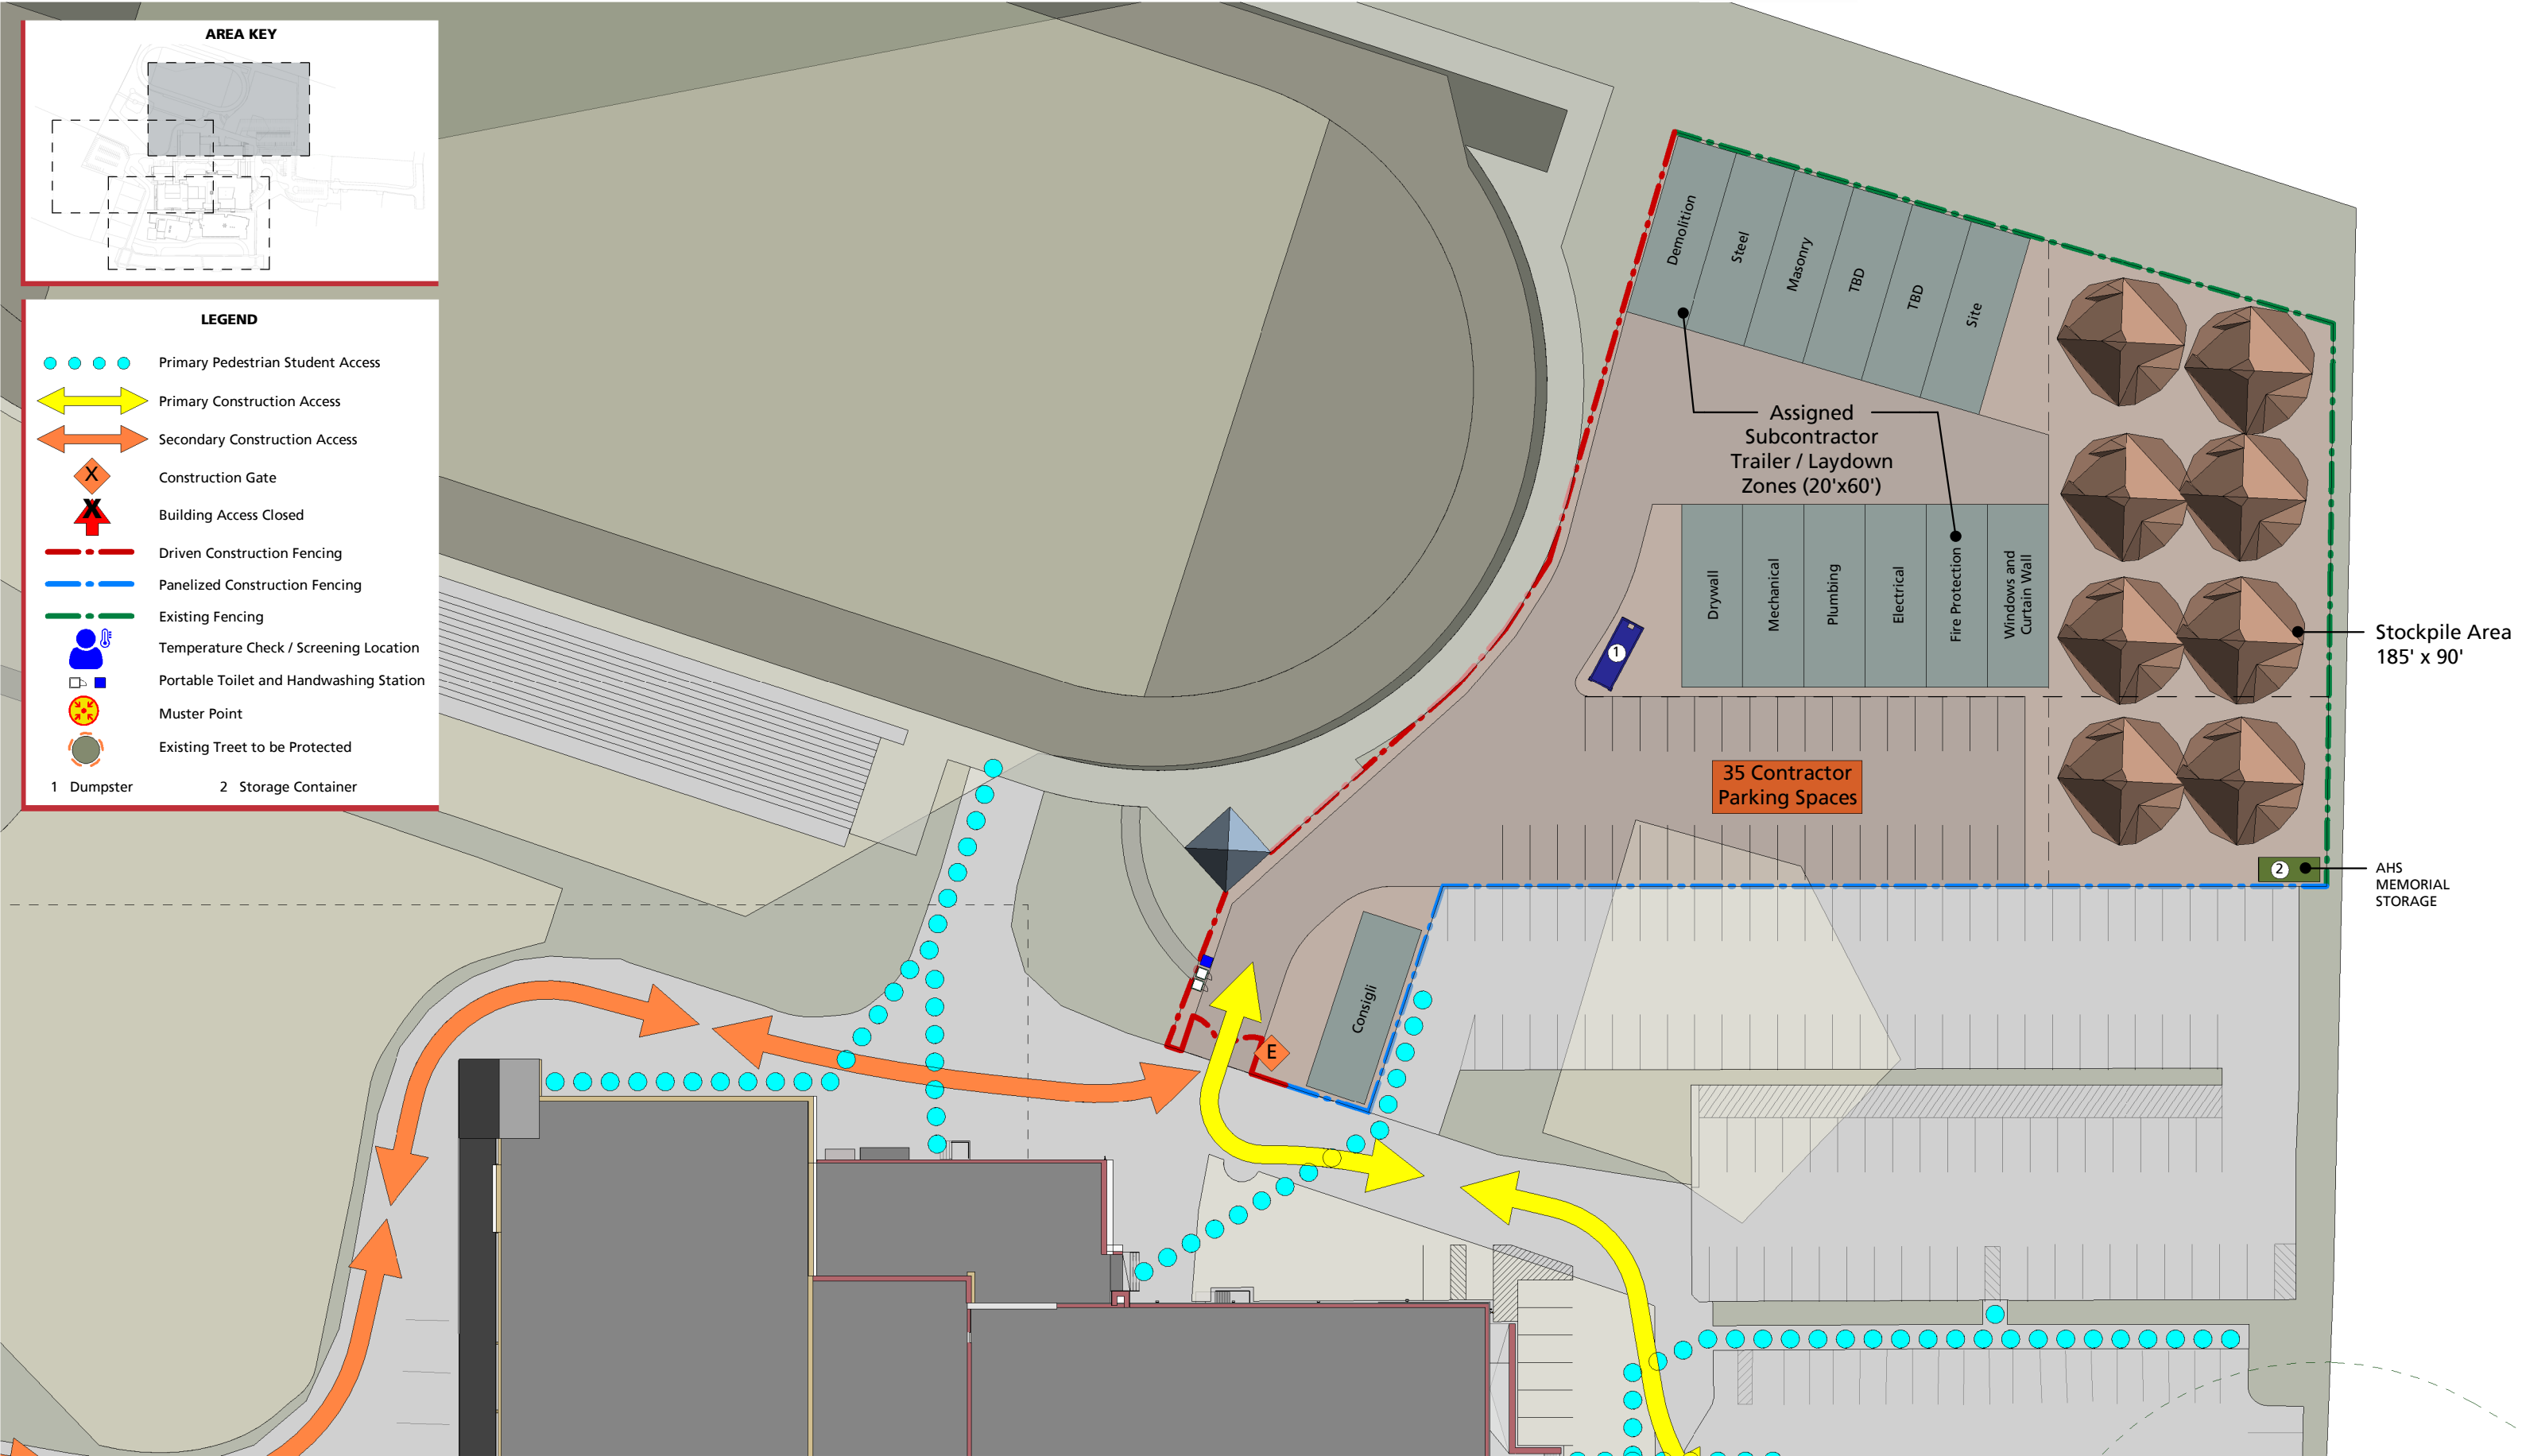

Arlington High School




Phases 1-2
Enlarged Plan - Area 3

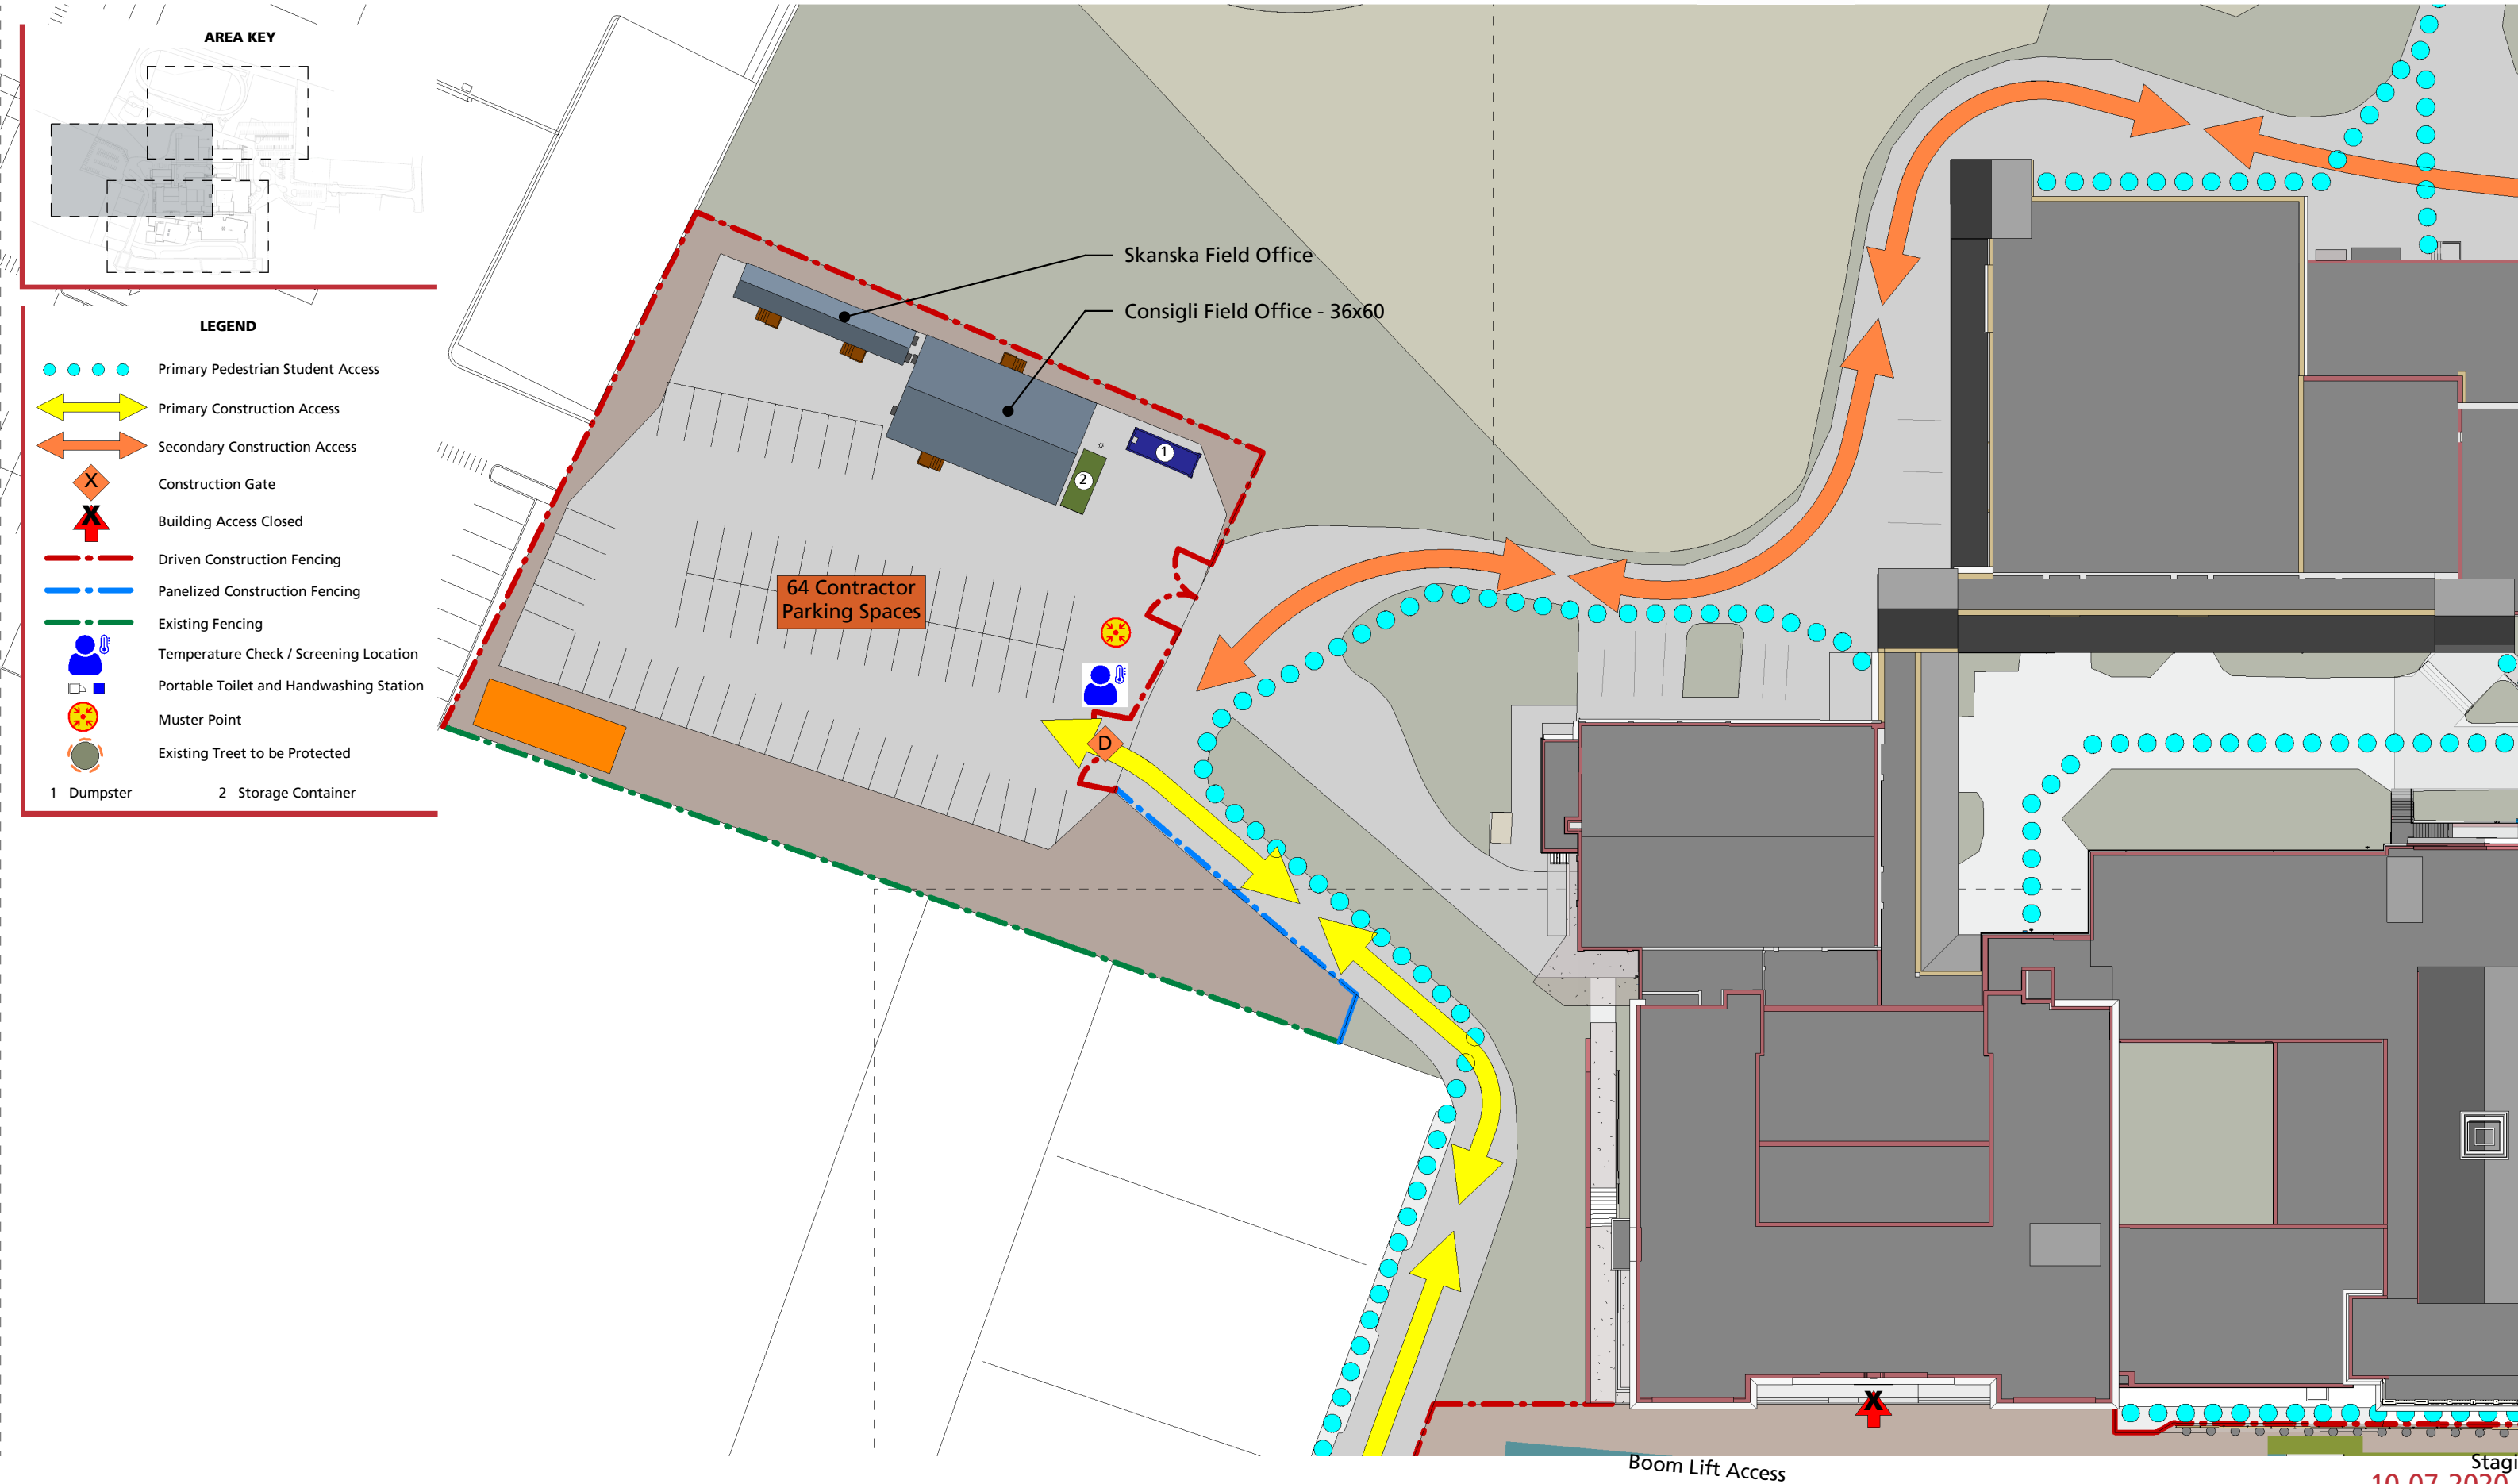

Arlington High School




Phase 2 - Demolition (A)
February 2022 Start

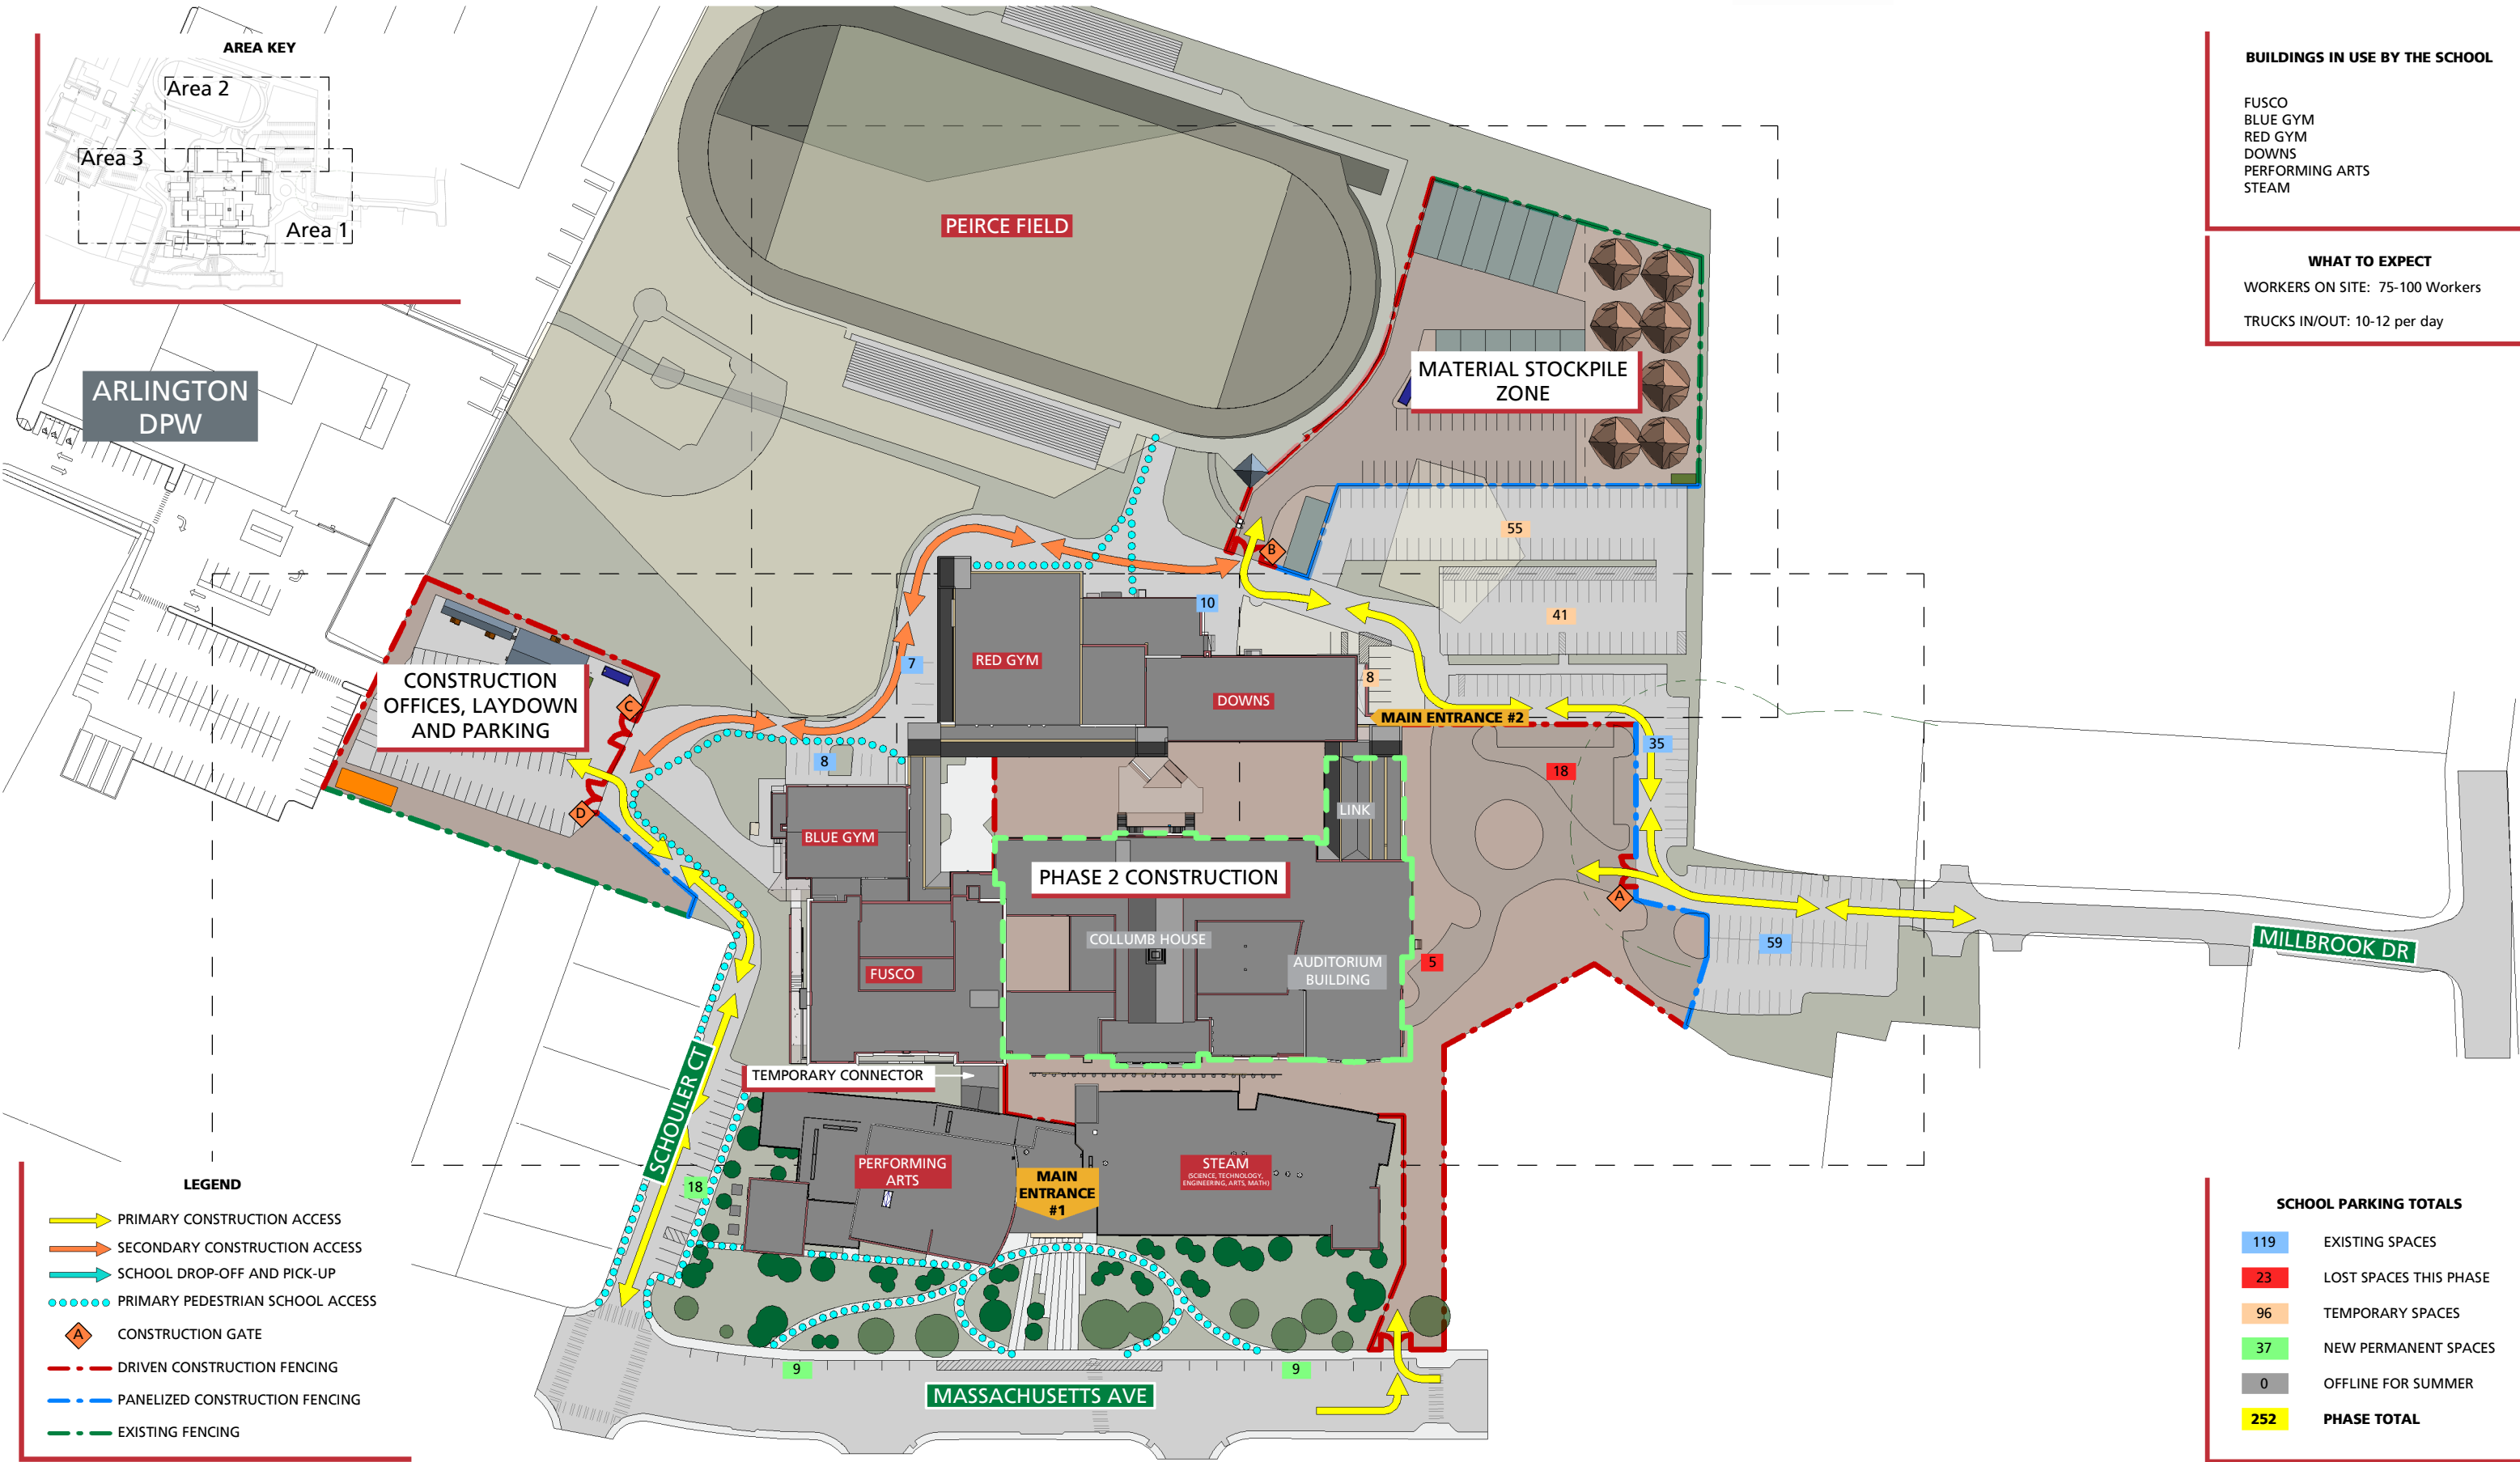

Arlington High School



Phase 2 - New Construction (B)
September 2023 Completion

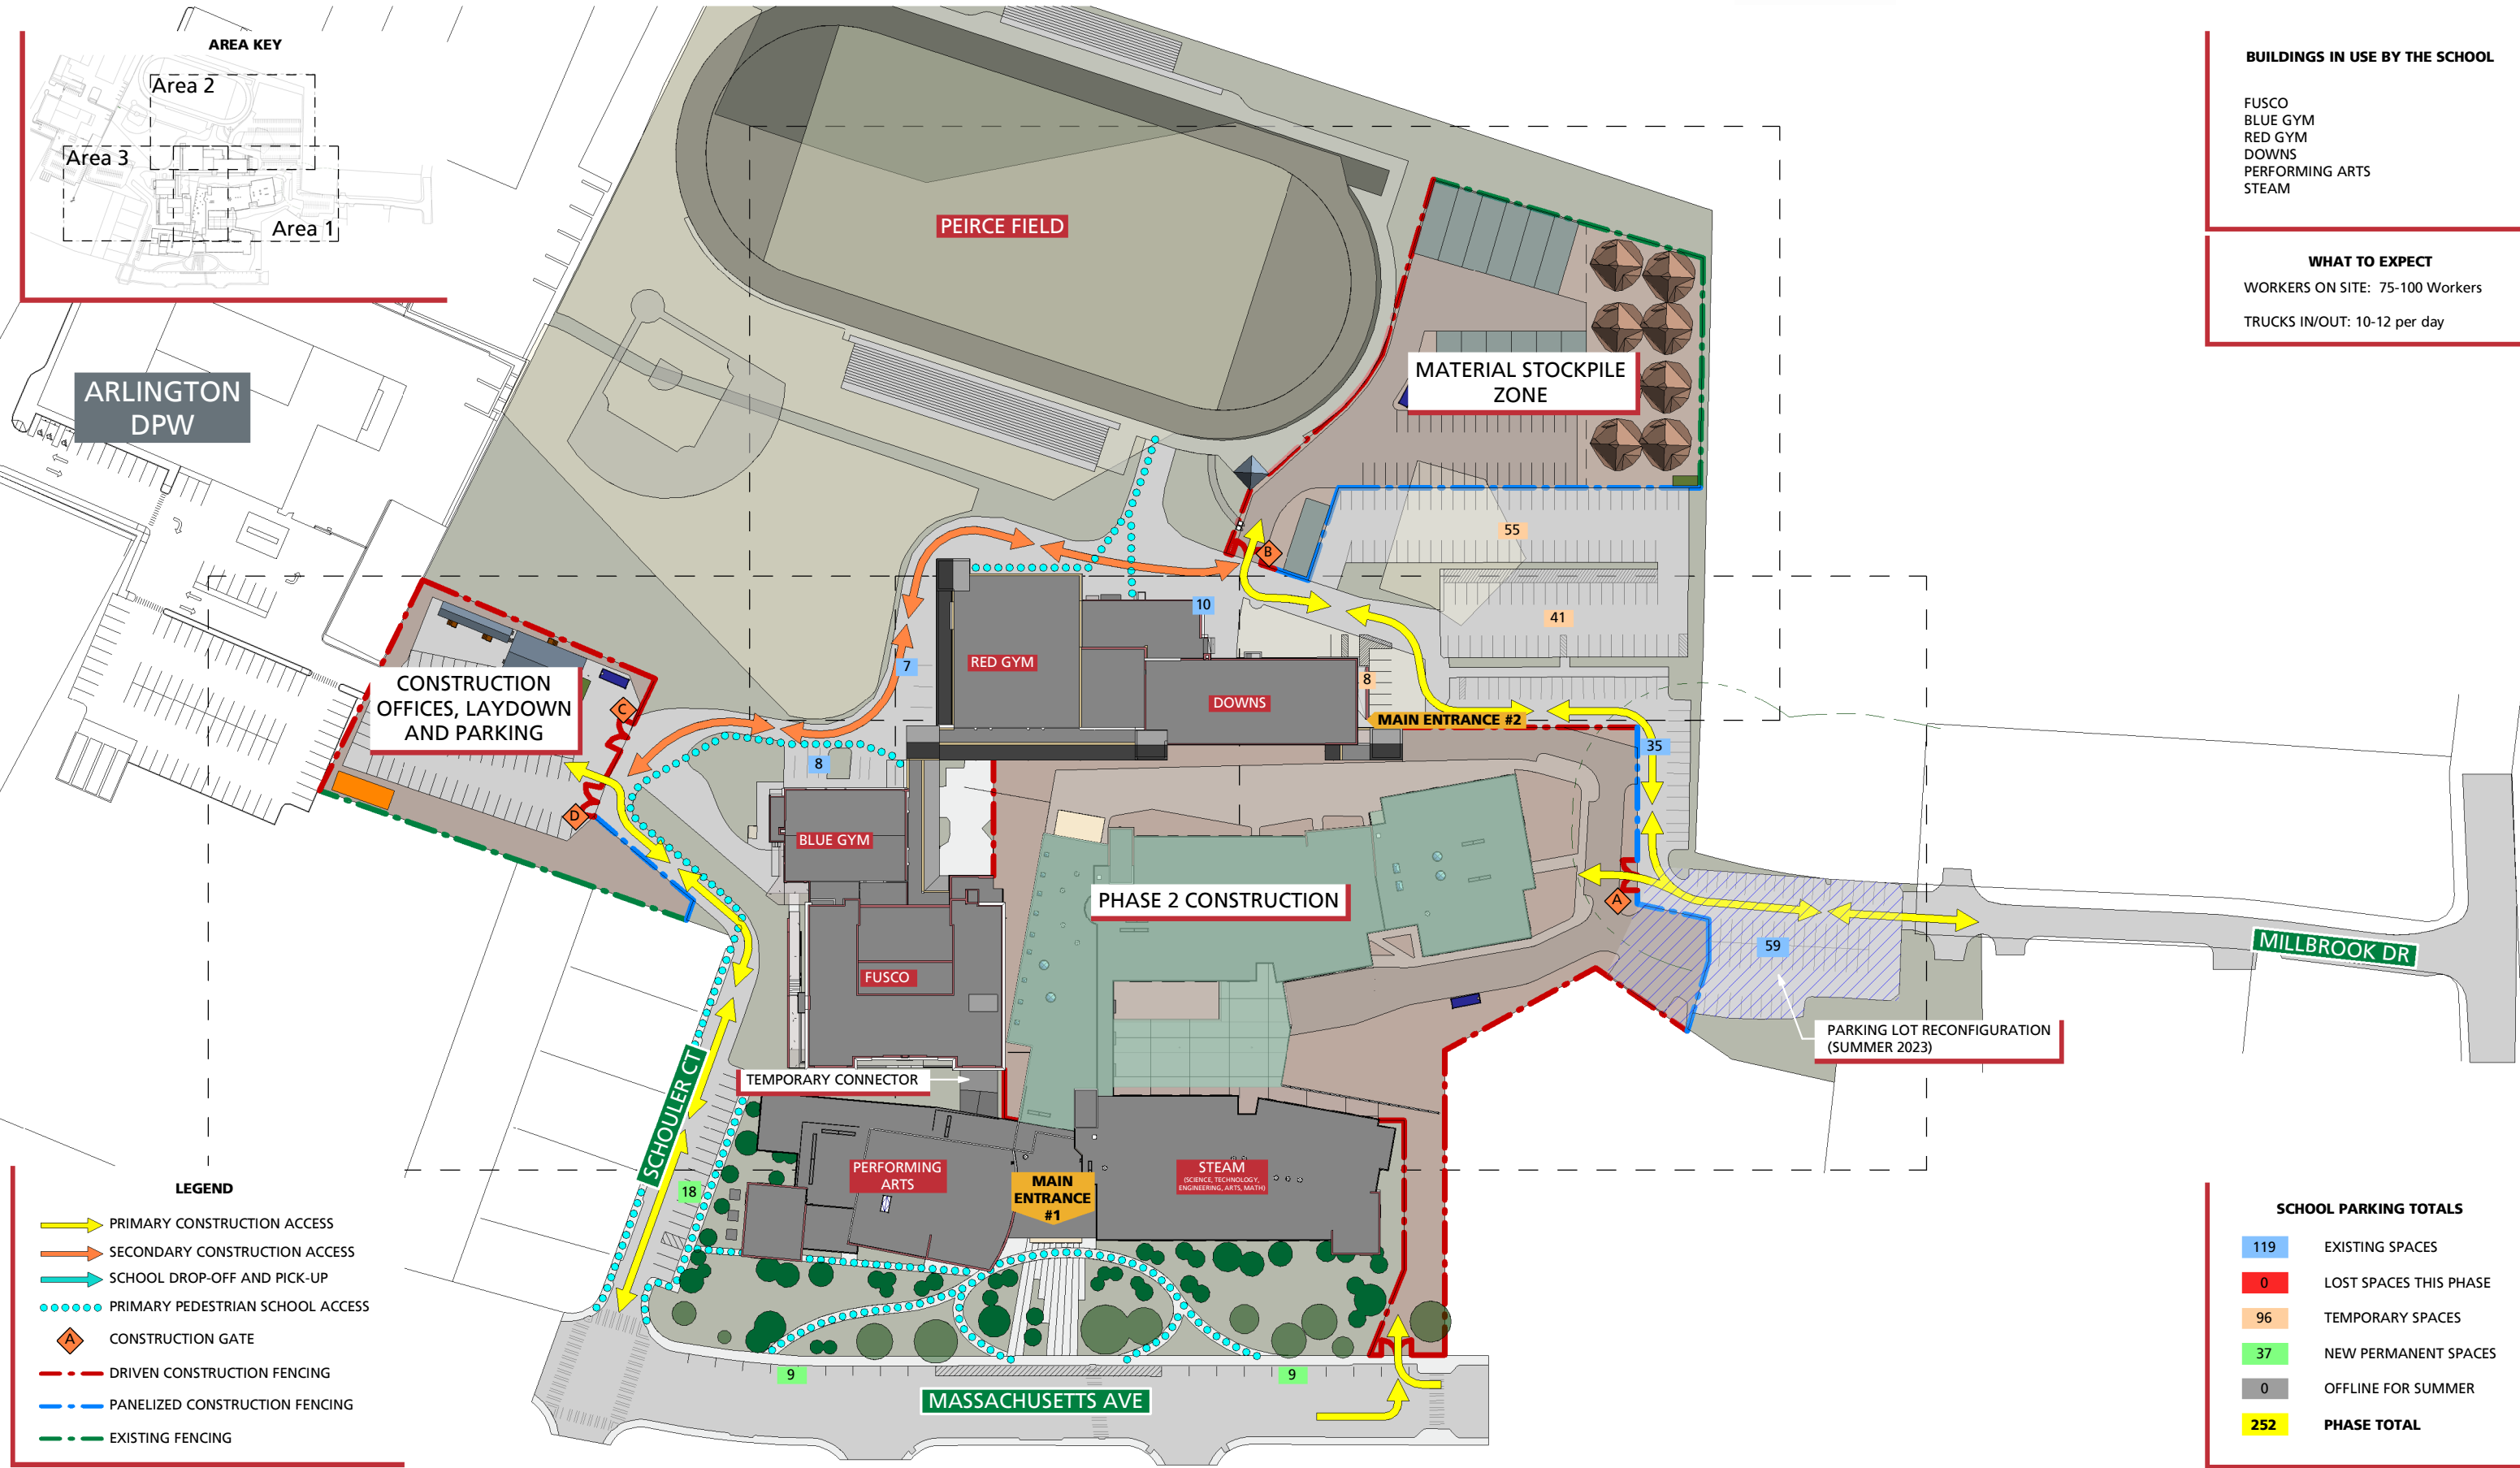




Arlington High School




Phase 3 - Demolition (A)
July 2023 Start

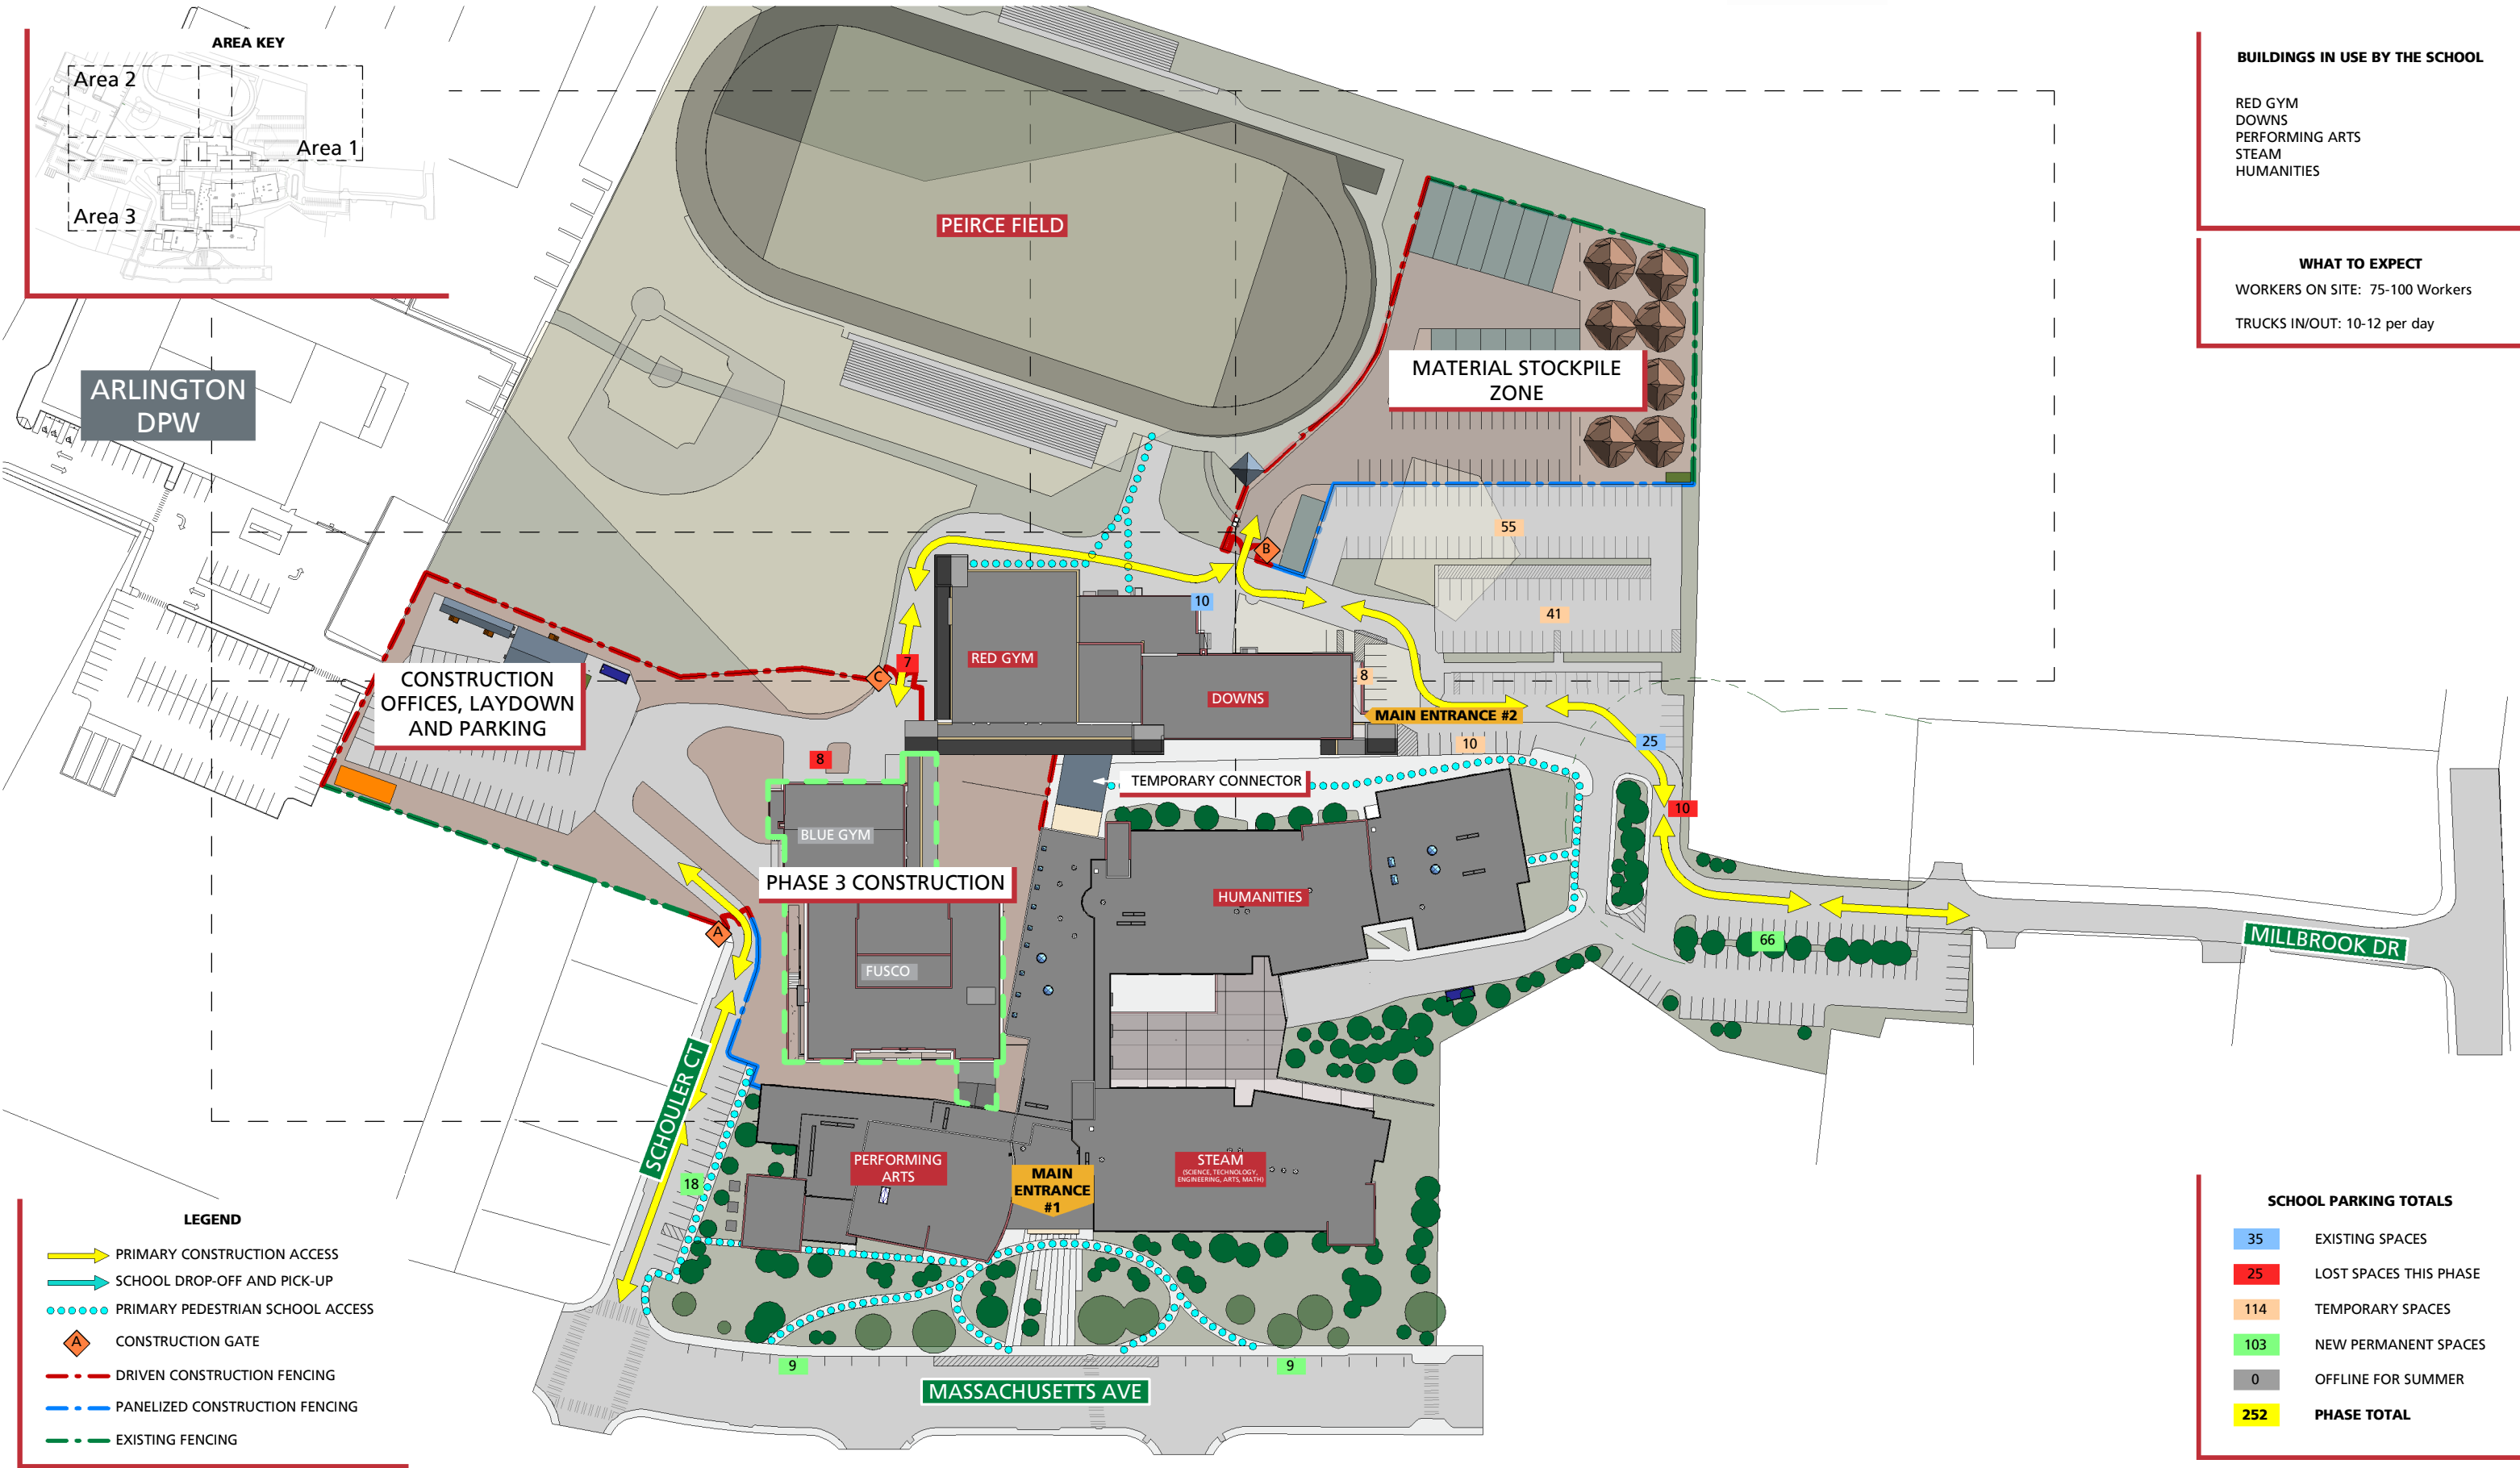


Arlington High School



Phase 3 - New Construction (B)
September 2024 Completion

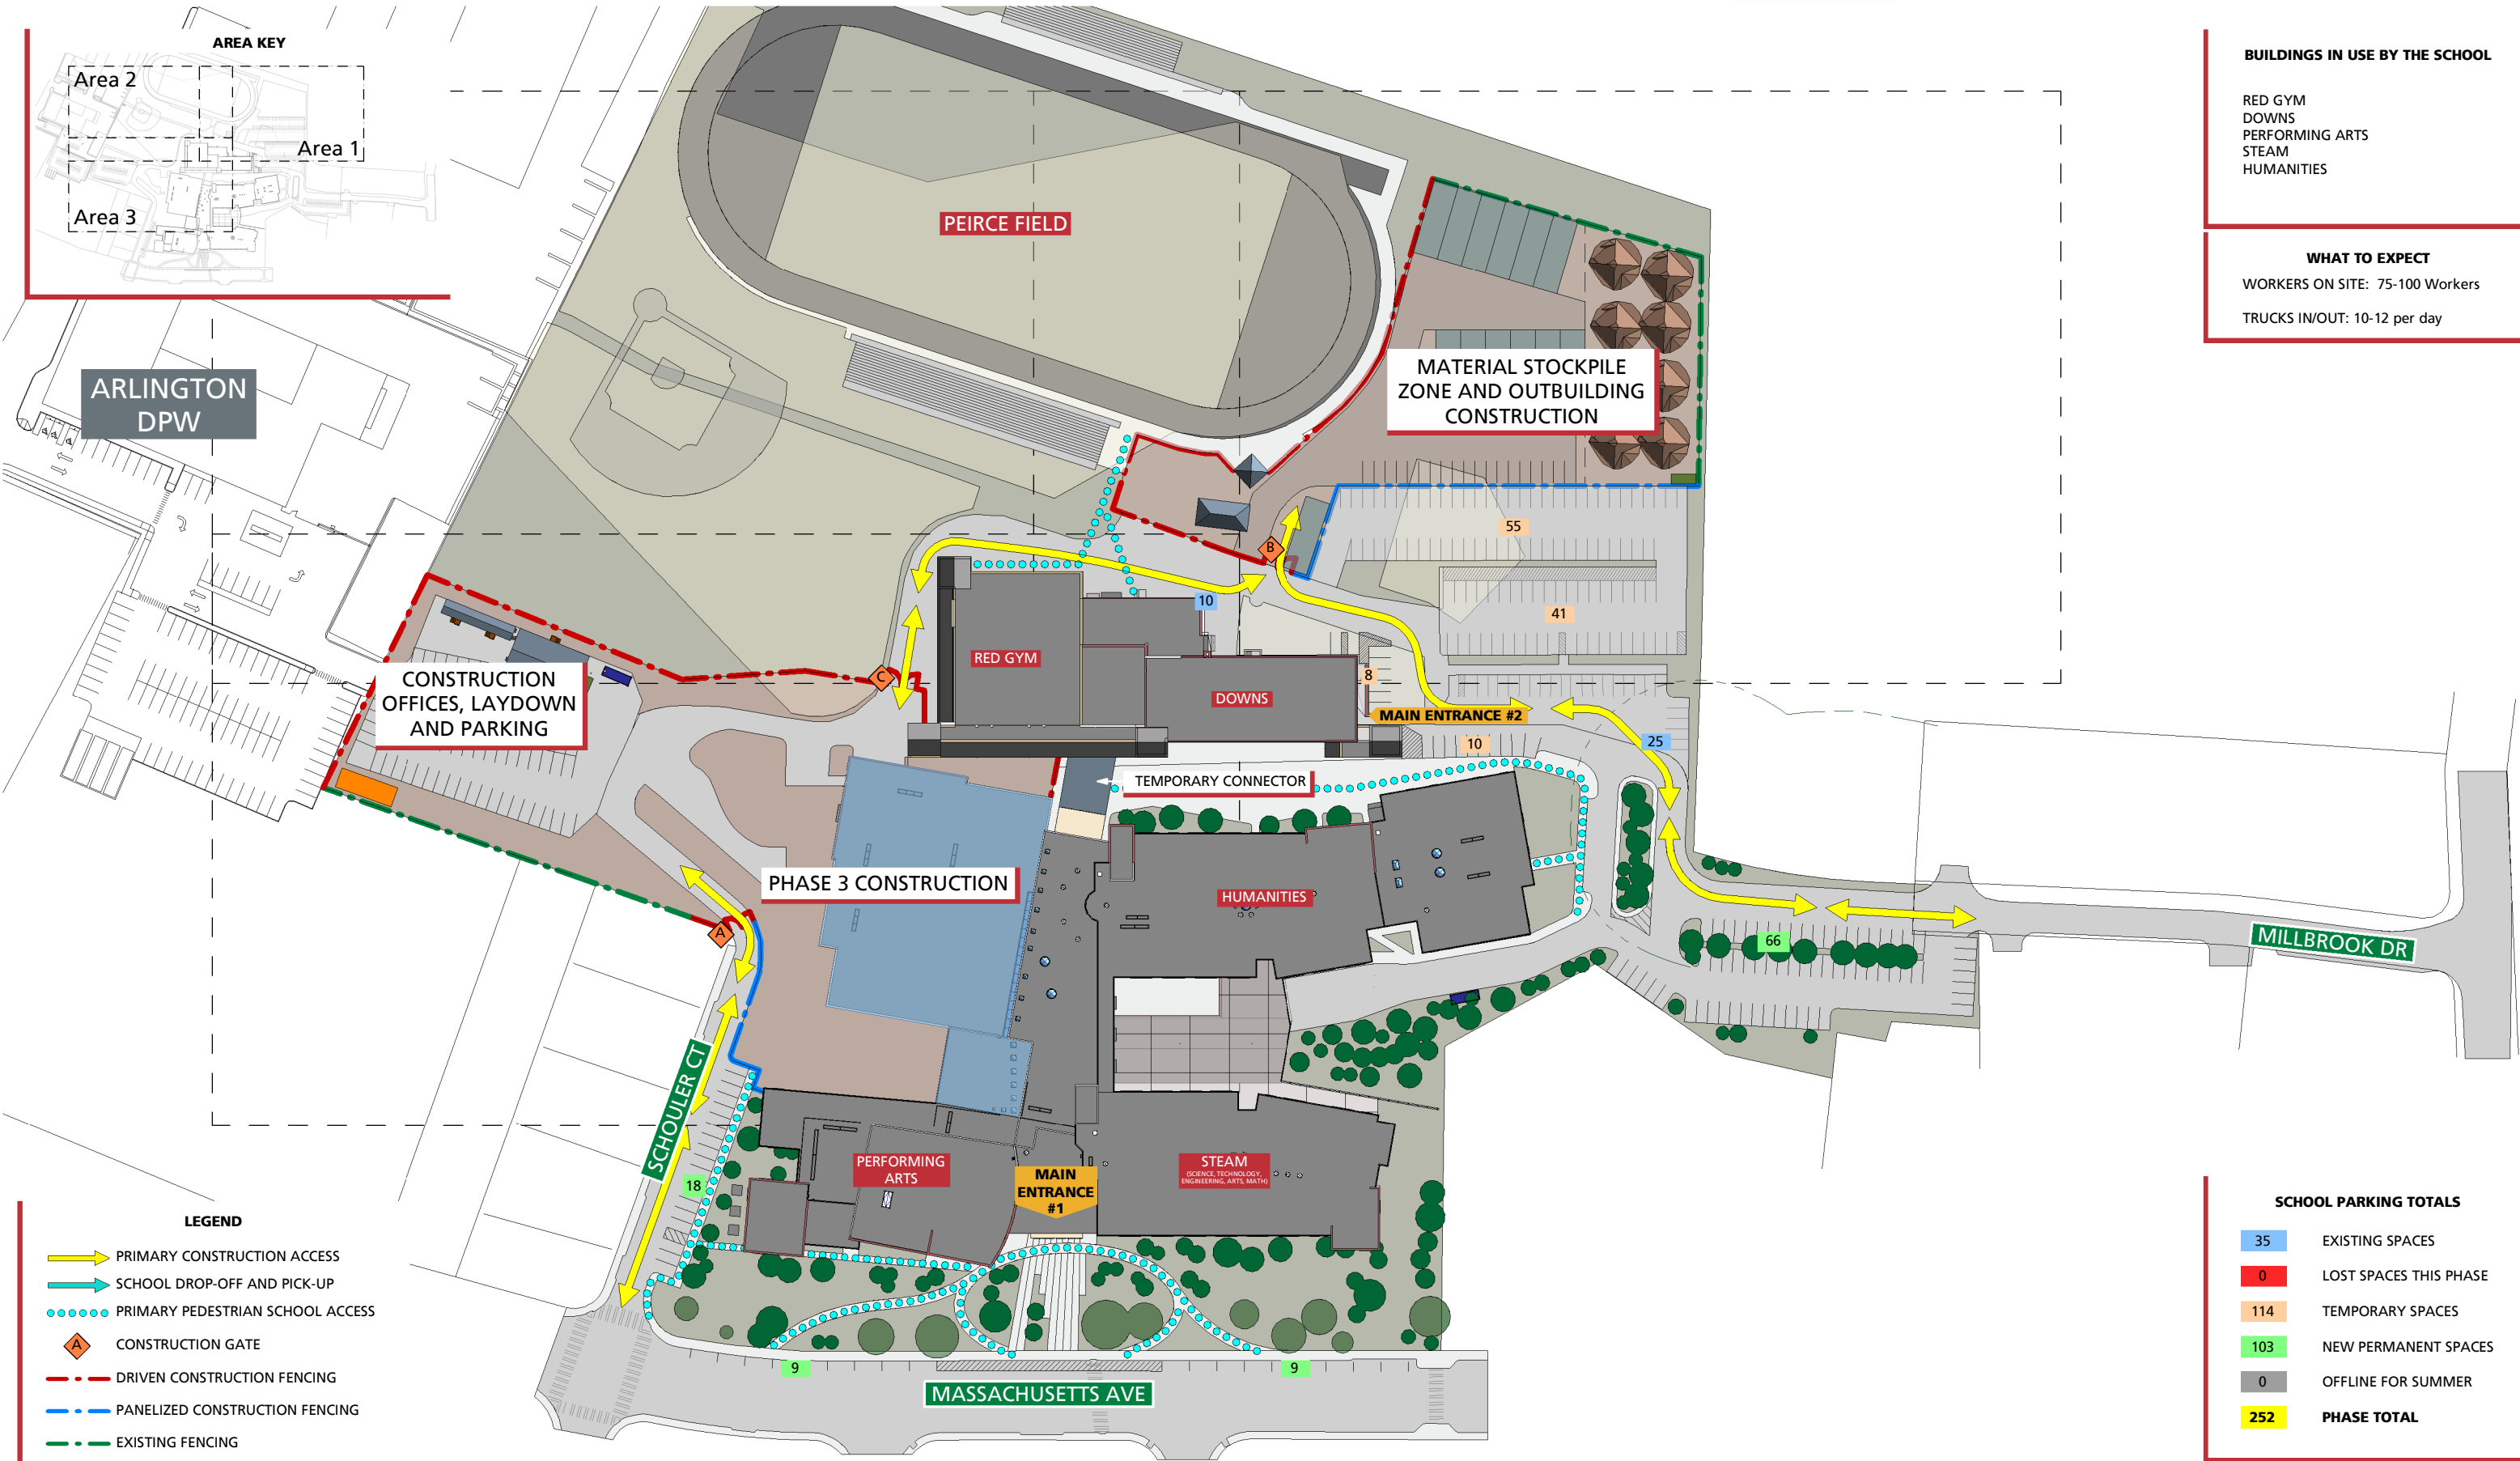


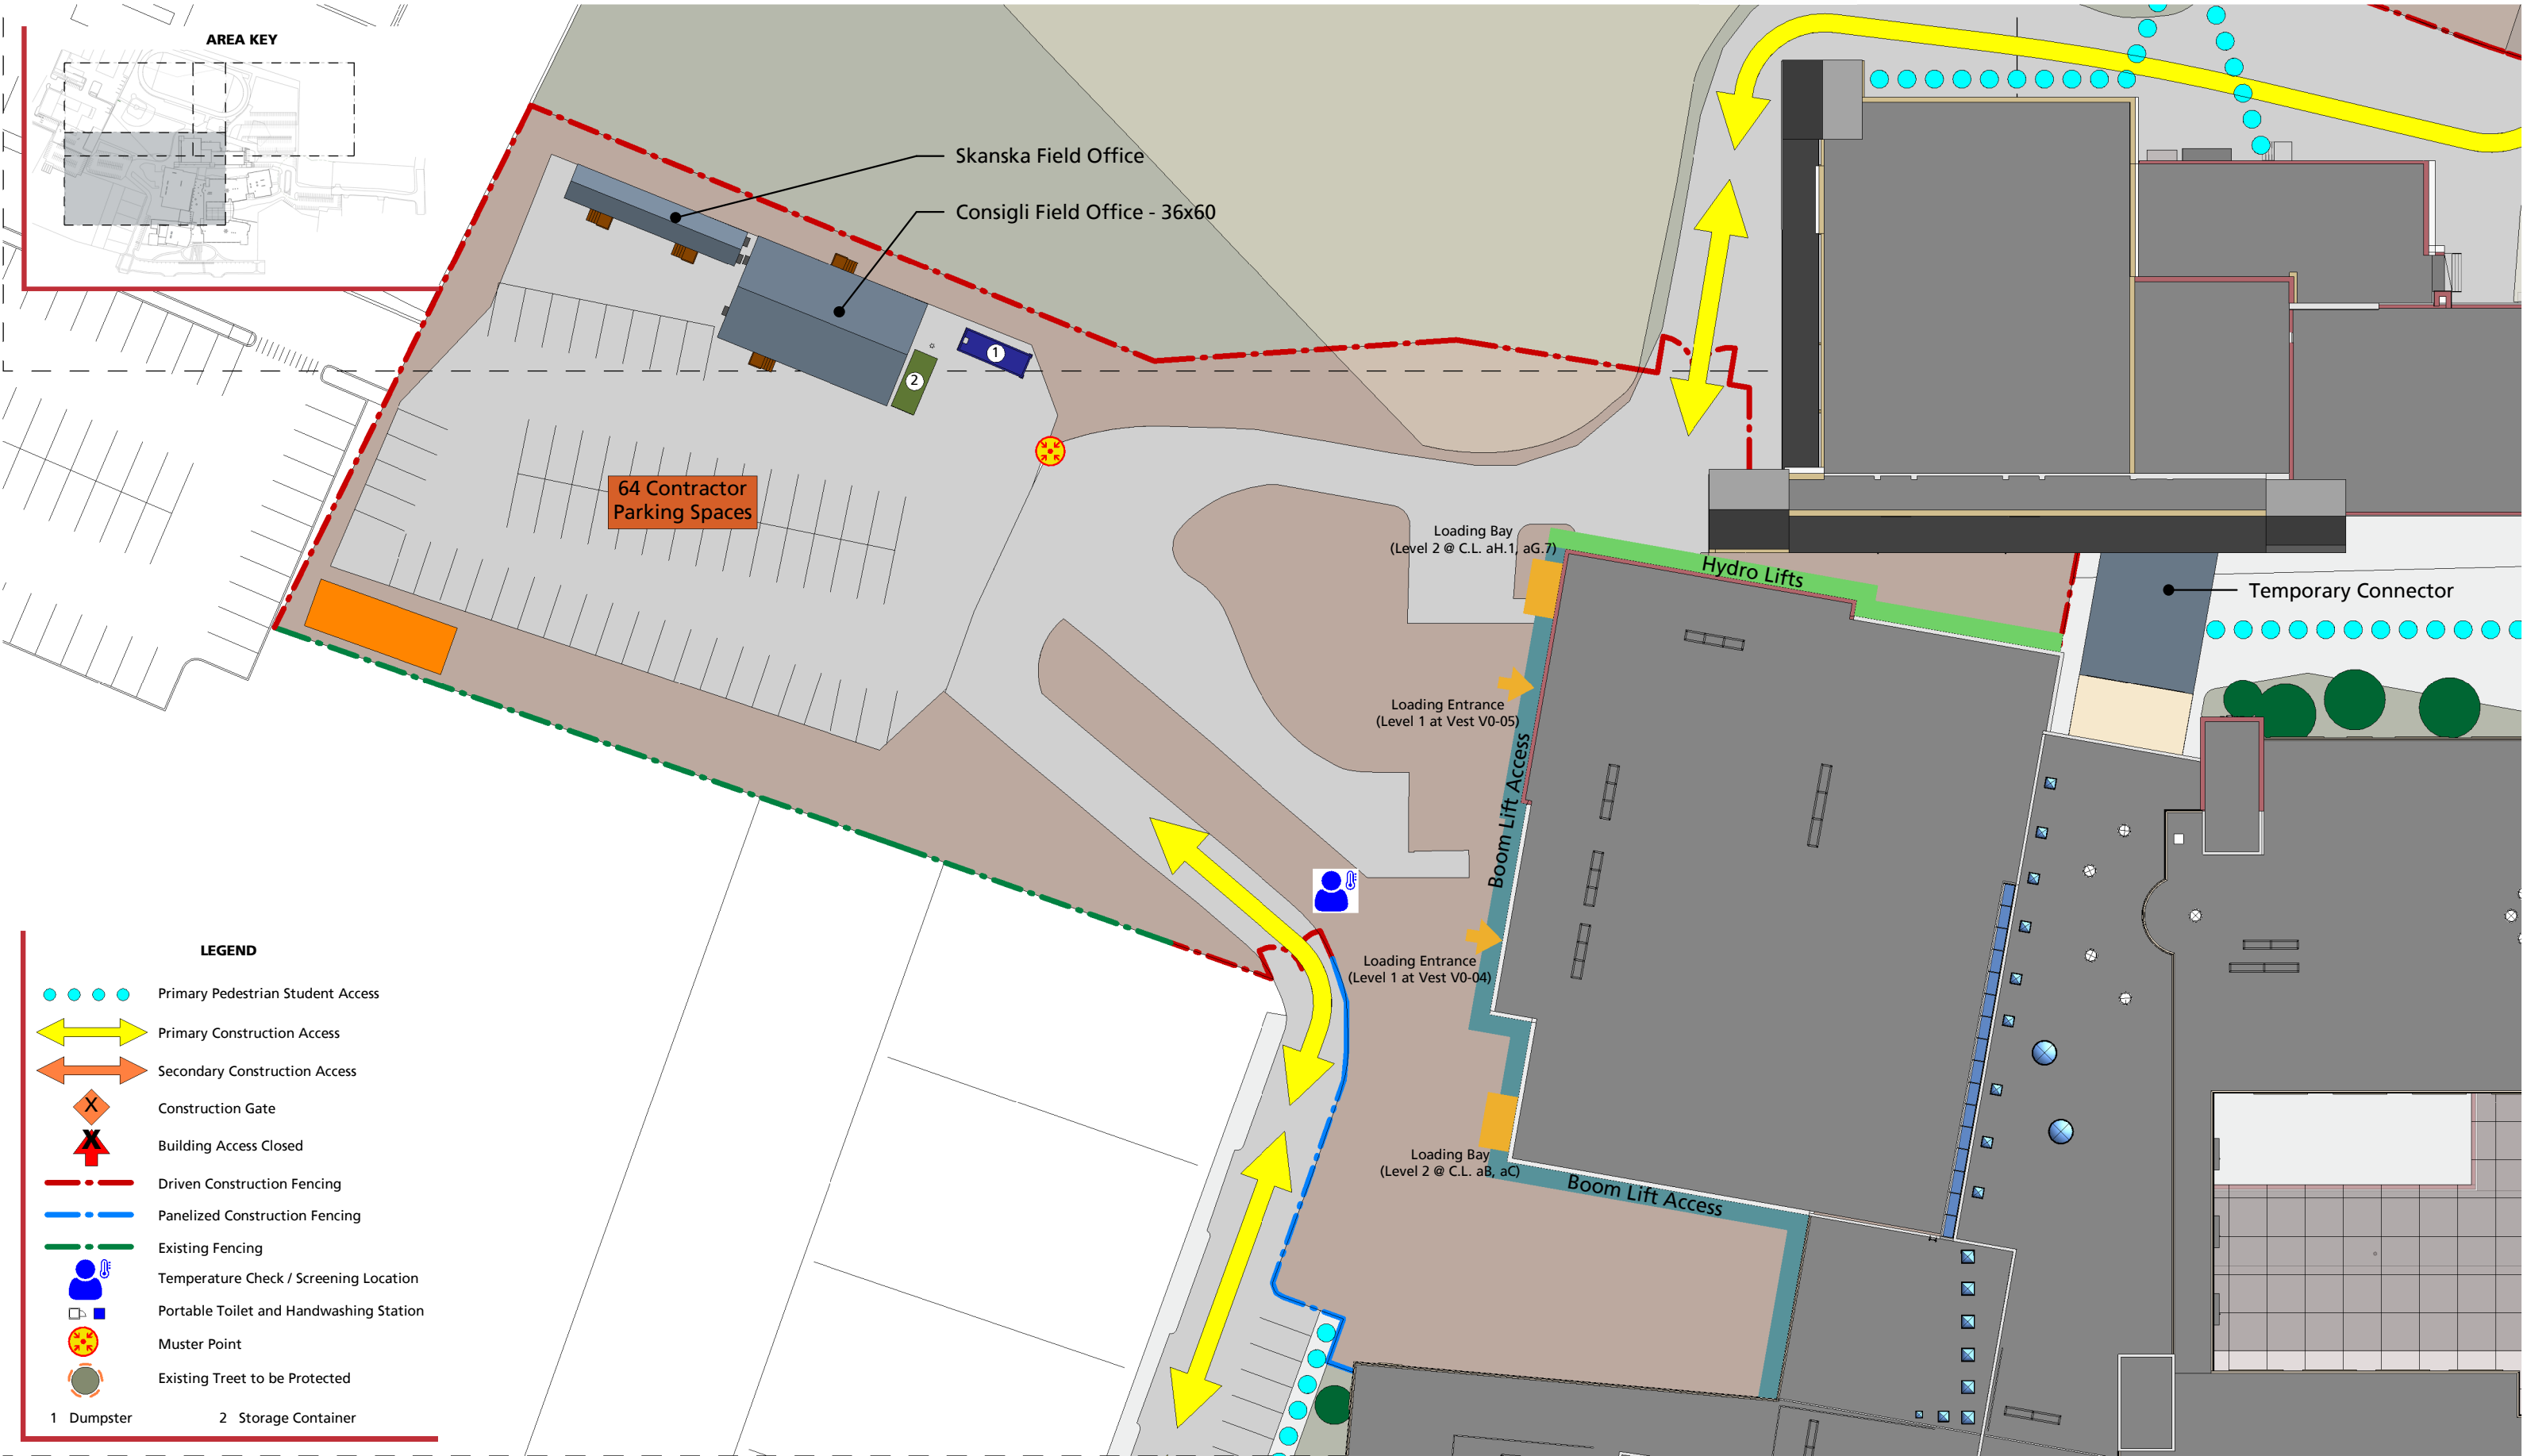

Arlington High School



Phase 4 - Demolition (A)
June 2024 Start

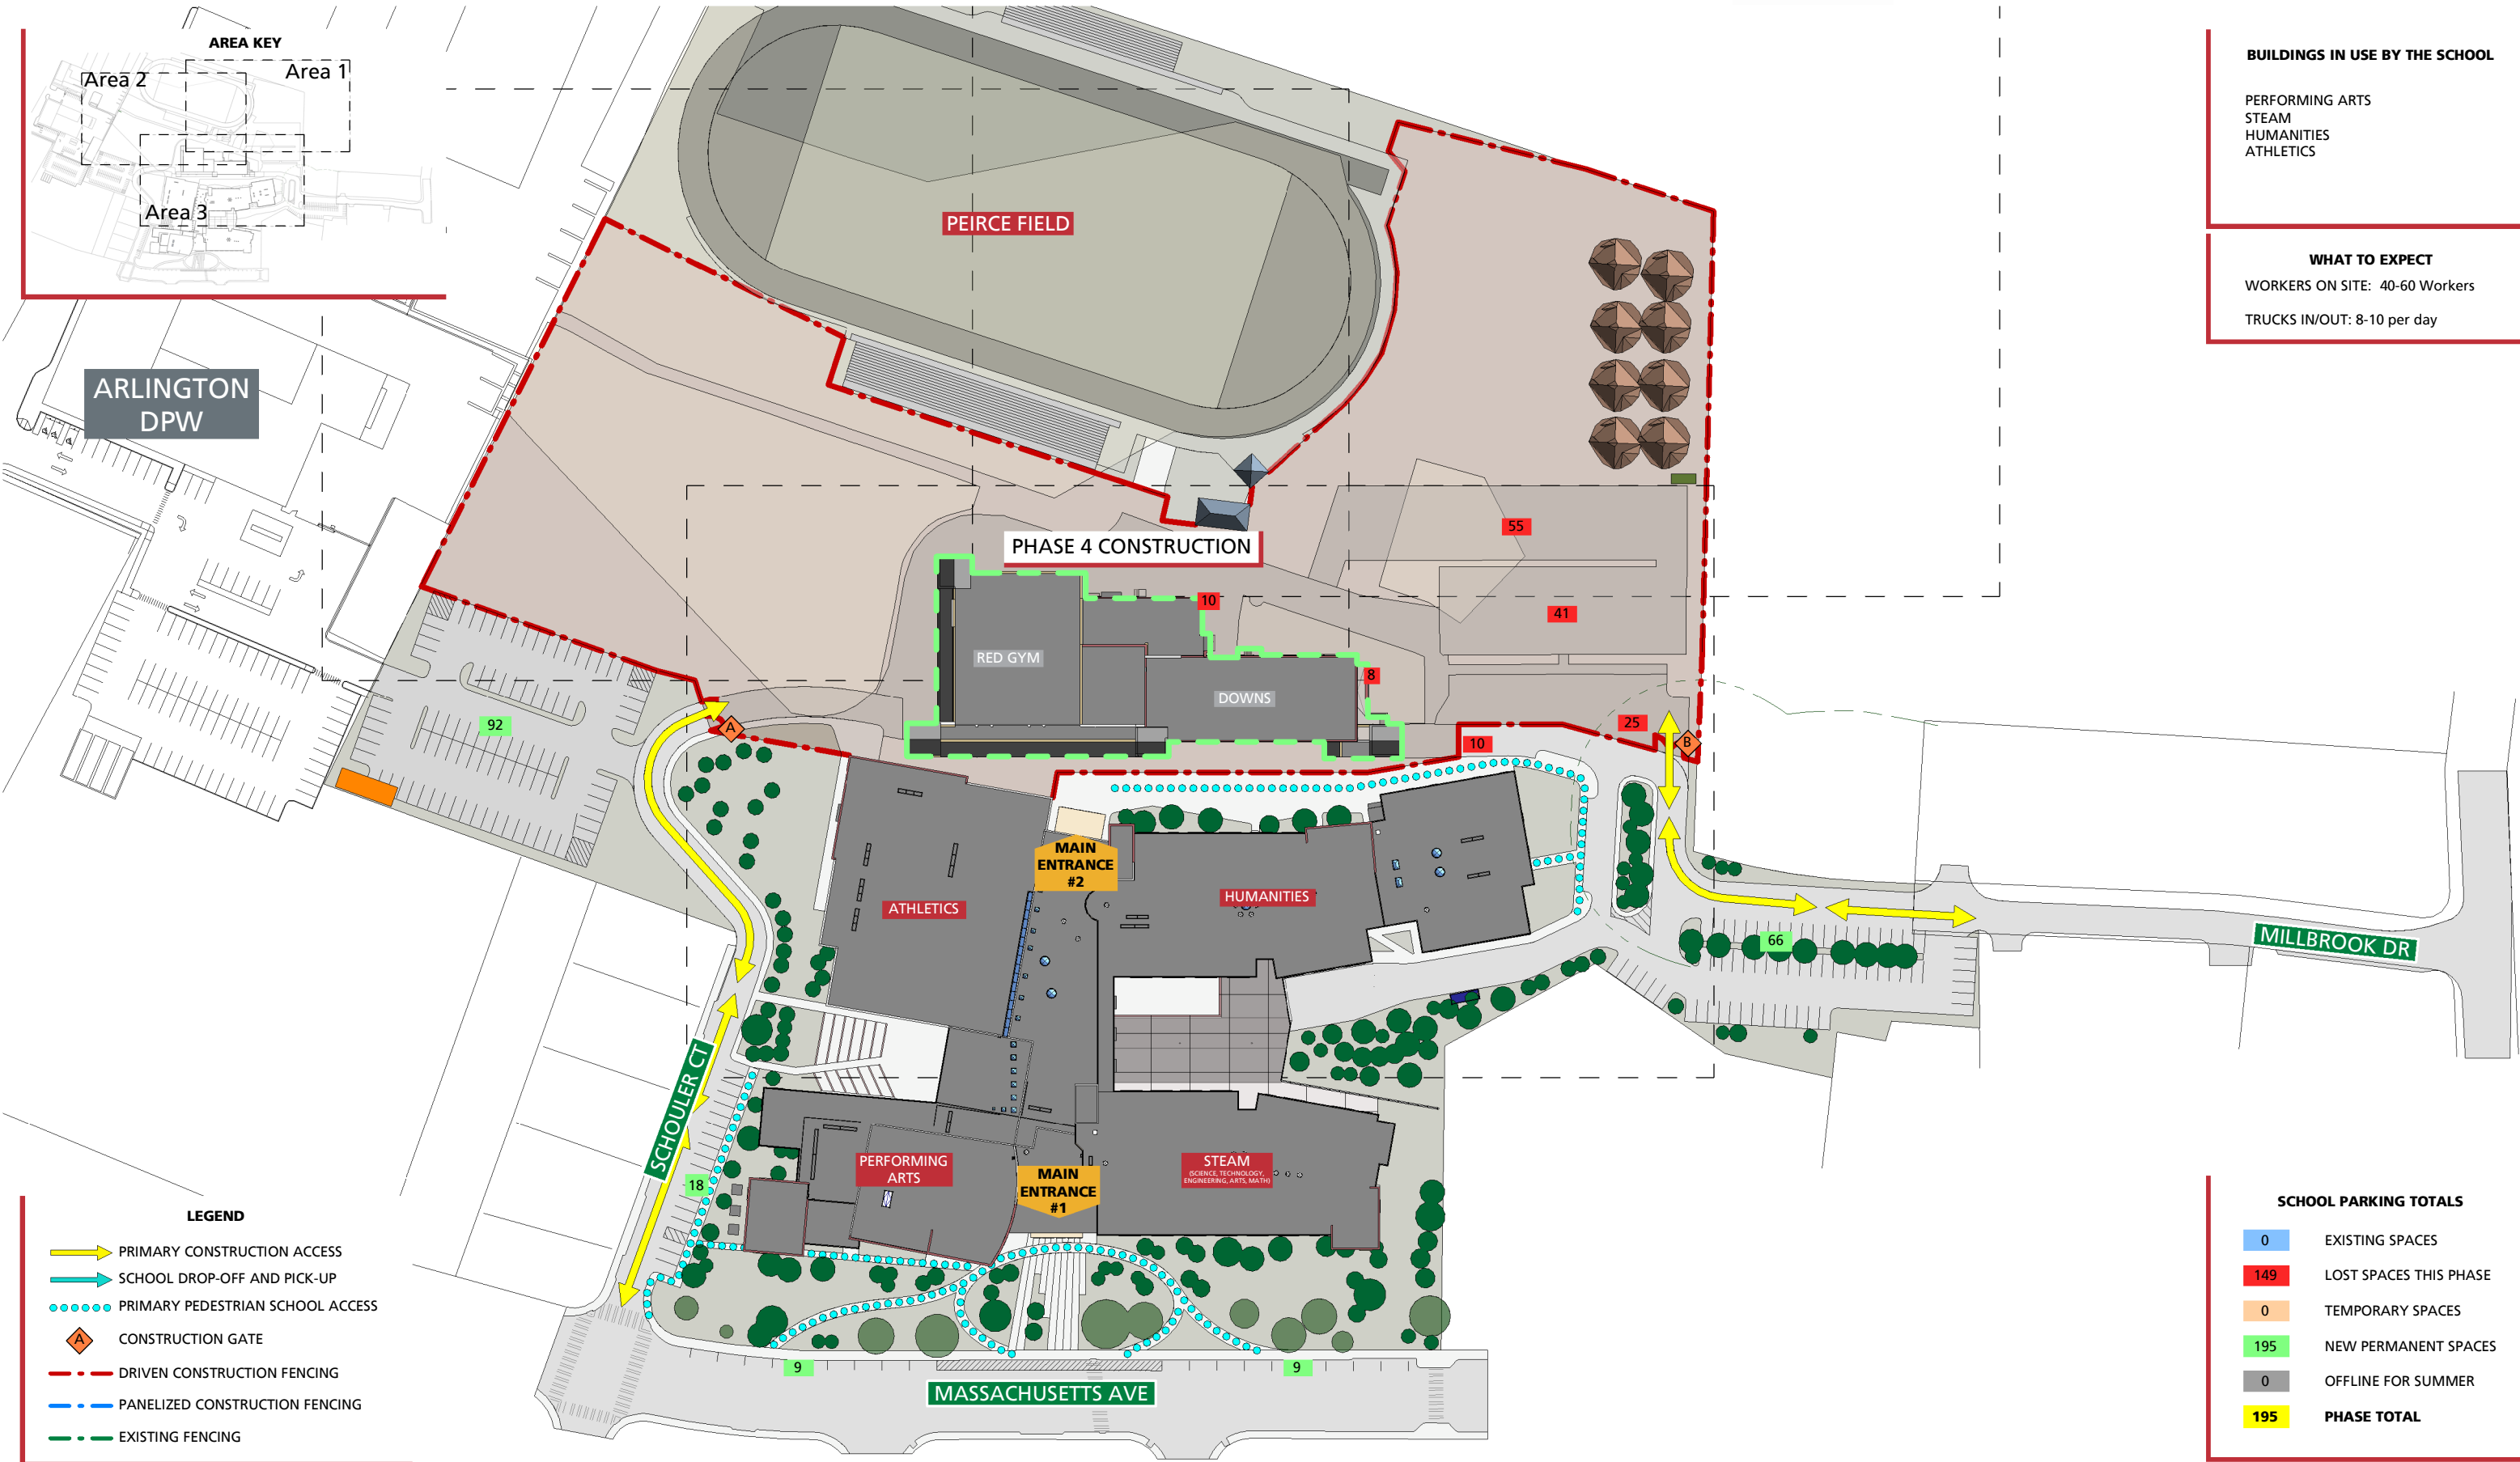

Arlington High School



Phase 4 - New Construction (B)
April 2025 Completion



| Arlington High School | | | | | | |
|---|--------------|---|-----------------------------------|-----------------------|----------------|--|
| Alternates & Potential Add Back In List - DRAFT | | | | | | |
| Items in bold were given priority by the Interior & Exterior Subcommittees | | | | | | |
| ALTERNATES | Phase | Items | Trade bid change order | Redesign costs | Costs | Notes |
| 1 | | Sports field lighting poles, lights, & wiring | | | 1,111,000 | |
| - | | Traffic light at Mill Street | | | 350,000 | |
| - | | Additional insulation at exterior walls of Athletics & Perf Arts wings | | | 228,045 | |
| - | | MM Bikeway connector ramp | | | 694,408 | |
| | | | | | | |
| INTERIOR | Phase | Items | Trade bid change order | Redesign costs | Costs | Notes |
| A | 2 | Extend terrazzo First Floor cafeteria | Yes | | 223,443 | aesthetics |
| B | 1 | Increase corridor wall tile height from 5'-0" to 7'-0" | Yes | | 290,640 | durability |
| C | 1 | Add wall tile at five main stairs (5'-0" typ/7'-0" at floor landings | Yes | | 374,939 | durability |
| D | 1 | Change toilet room floors from epoxy to tile | Yes | | 105,300 | aesthetics & greener product |
| E | 1 | Increase height of wet wall tile in adult toilet rooms from 3'-4" to 7'-0" | Yes | | 17,757 | durability |
| F | 1 | Change typical flooring from MCT to Modular | Yes | | 744,961 | increased thickness/ durability |
| G | 2 | Add back in food service equipment | | | 103,000 | |
| | | | | | | |

| EXTERIOR | Phase | Items | Trade bid change order | Redesign costs | Costs TBD | Notes |
|-----------------|--------------|---|-----------------------------------|-----------------------|------------------|------------------------------|
| H | 1 | Change CMU to brick | Yes | Yes | 1,056,000 | aesthetics |
| la | 1 | Change remaining CW to triple pane glazing | Yes | | 685,192 | increased thermal barrier |
| lb | 1 | Change all windows to triple pane glazing | Yes | | 178,332 | increased thermal barrier |
| | | | | | | |
| SITE | | Items | Trade bid change order | Redesign costs | Costs TBD | Notes |
| J | 4 | Add 2 batting cages | | Yes | 94,300 | |
| K | 4 | Baseball & softball warm up bullpens | | Yes | 27,990 | |
| L | 4 | Sports field Maroon Monster | | Yes | 56,000 | |
| M | 4 | Covered bike area for 80 bikes | | Yes | tbd | sustainability |
| N | 4 | Change walk to stadium from bituminous to concrete | | | 52,708 | aesthetics |
| O | 4 | Change MM Bikeway Connector from chain link to guardrail | Yes | Yes | 41,500 | aesthetics |
| P | 4 | Increase quantity of EV charging stations by 5 | | Yes | 82,000 | sustainability |
